



ID	Task Name	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TR4	Predecessors
1	Starting date	1 day	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	0 days		
2	Access date	270 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	1084 days		
3	Portion A	270 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	1084 days		
4	Portion B	210 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	1144 days		
5	Portion C1 & C2	270 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	1084 days		
6	Portion C3	0 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	1354 days		
7	Portion D	210 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	1144 days		
8	Portion E1	0 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	1354 days		
9	Portion E2	0 days	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	Mon 23/5/29	1084 days		
10	Completion Date	1155 days	Mon 26/7/27	Mon 26/7/27	Mon 26/7/27	Mon 26/7/27	Mon 26/7/27	Mon 26/7/27	0 days		
11	Section I - Drainage Improvement Works at Sung Shan New Village	1095 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days		
12	Section II - Drainage Improvement Works at Tai Wo	820 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days		
13	Section III - Drainage Improvement Works at Lin Fa Tai (except flood wall construction and drainage improvement works along Kam Sheung Road)	1155 days	Mon 26/7/27	Mon 26/7/27	Mon 26/7/27	Mon 26/7/27	Mon 26/7/27	Mon 26/7/27	0 days		
14	Section IV - Drainage Improvement Works at Ha Che (except pipe laying works by trenchless method and pipe rehabilitation works across Fan Kam Road)	1095 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days		
15	Section V - Drainage Improvement Works at Shan Ha Tsuen	973 days	Mon 26/7/26	Mon 26/7/26	Mon 26/7/26	Mon 26/7/26	Mon 26/7/26	Mon 26/7/26	0 days		
16	Section VI - Flood Wall Construction and Drainage Improvement Works along Kam Sheung Road at Lin Fa Tai	820 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days		
17	Section VII - Pipe Laying Works by Trenchless Method and Pipe Rehabilitation Works across Fan Kam Road and Upstream Channel and Downstream Box Culvert	820 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days		
39	Planned Completion Day of whole of the works	405 days	Tue 25/8/26	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
40	Section I - Drainage Improvement Works at Sung Shan New Village	130 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
41	EOT - In-cement weather (anticipated upto 31 Jul 2024)	70 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
42	EOT - Unchared/Retained Trees obstructing the works	60 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	129 days		
43	Section II - Drainage Improvement Works at Tai Wo	251 days	Wed 25/8/27	Mon 26/5/4	Mon 26/5/4	Mon 26/5/4	Mon 26/5/4	Mon 26/5/4	0 days		
44	EOT - Blockade of access by others	70 days	Tue 26/7/28	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
45	Section III - Drainage Improvement Works at Lin Fa Tai (except flood wall construction and drainage improvement works along Kam Sheung Road)	70 days	Tue 26/7/28	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
46	EOT - In-cement weather (anticipated upto 31 Jul 2024)	70 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
47	Section IV - Drainage Improvement Works at Ha Che (except pipe laying works by trenchless method and pipe rehabilitation works across Fan Kam Road)	70 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
48	EOT - In-cement weather (anticipated upto 31 Jul 2024)	70 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
49	Section V - Drainage Improvement Works at Shan Ha Tsuen	70 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
50	EOT - In-cement weather (anticipated upto 31 Jul 2024)	70 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
51	Section VI - Flood Wall Construction and Drainage Improvement Works along Kam Sheung Road at Lin Fa Tai	240 days	Wed 25/8/27	Mon 26/4/6	Mon 26/4/6	Mon 26/4/6	Mon 26/4/6	Mon 26/4/6	0 days		
52	EOT - In-cement weather (anticipated upto 31 Jul 2024)	70 days	Mon 26/4/6	Mon 26/4/6	Mon 26/4/6	Mon 26/4/6	Mon 26/4/6	Mon 26/4/6	0 days		
53	Section VII - Pipe Laying Works by Trenchless Method and Pipe Rehabilitation Works across Fan Kam Road and Upstream Channel and Downstream Box Culvert Construction Works (Change 626.224m - 678.859m) at Ha Che	240 days	Wed 25/8/27	Tue 25/8/26	Tue 25/8/26	Tue 25/8/26	Tue 25/8/26	Tue 25/8/26	534 days		
54	Project establishment	307 days	Mon 23/5/15	Sat 24/3/16	Mon 23/5/15	Sat 24/3/16	Mon 23/5/15	Mon 23/5/15	0 days		
55	PM1001 - Possession of Works Area at 22 Fan Kam Road [A]	197 days	Mon 23/5/15	Sat 24/3/16	Mon 23/5/15	Sat 24/3/16	Mon 23/5/15	Mon 23/5/15	1062 days		
56	Project Manager's Accommodation	209 days	Mon 23/5/15	Sat 24/3/16	Mon 23/5/15	Sat 24/3/16	Mon 23/5/15	Mon 23/5/15	1062 days		
57	Renovation and Certification of ex. PM accommodation	197 days	Sat 24/3/16	Sat 24/3/16	Sat 24/3/16	Sat 24/3/16	Sat 24/3/16	Sat 24/3/16	1062 days		
58	Inspection and review of ex. PM accommodation [A]	100 days	Sat 23/9/2	Sun 23/12/10	Sat 23/9/2	Sun 23/12/10	Sat 23/9/2	Sat 23/9/2	1062 days		
59	Arranging time slot with R55 for power and server down [A]	83 days	Mon 23/12/11	Sat 24/3/16	Mon 23/12/11	Sat 24/3/16	Mon 23/12/11	Mon 23/12/11	1062 days		
60	Issuance of check certificates [A]	14 days	Sun 24/3/16	Sun 24/3/16	Sun 24/3/16	Sun 24/3/16	Sun 24/3/16	Sun 24/3/16	1062 days		
61	C11 Tendering procedure for EDM& DWSS [A]	30 days	Mon 23/8/21	Mon 23/8/21	Mon 23/8/21	Mon 23/8/21	Mon 23/8/21	Mon 23/8/21	1201 days		
62	Installation and commissioning of EDM& DWSS [A]	40 days	Wed 23/10/29	Sun 23/10/29	Wed 23/10/29	Sun 23/10/29	Wed 23/10/29	Sun 23/10/29	1201 days		
63	Environmental Team (ET) procurement	190 days	Tue 23/8/15	Tue 23/8/15	Tue 23/8/15	Tue 23/8/15	Tue 23/8/15	Tue 23/8/15	15 days		
64	C9 Tendering procedure [A]	58 days	Tue 23/8/15	Tue 23/10/11	Wed 23/10/11	Wed 23/10/11	Wed 23/10/11	Wed 23/10/11	15 days		
65	Commencement of ET (Aurecon) [A]	1 day	Mon 23/10/12	Mon 23/10/12	Mon 23/10/12	Mon 23/10/12	Mon 23/10/12	Mon 23/10/12	15 days		
66	Proposal and acceptance of ET Members [A]	18 days	Mon 23/10/30	Mon 23/10/30	Mon 23/10/30	Mon 23/10/30	Mon 23/10/30	Mon 23/10/30	15 days		
67	Updating and acceptance of EM&A Manual [A]	23 days	Wed 23/10/31	Wed 23/10/31	Wed 23/10/31	Wed 23/10/31	Wed 23/10/31	Wed 23/10/31	15 days		
68	Notice of Commencement of Construction to EPD [A]	20 days	Tue 24/2/20	Tue 24/2/20	Tue 24/2/20	Tue 24/2/20	Tue 24/2/20	Tue 24/2/20	1087 days		
69	Complete necessary submissions to EPD [A]	30 days	Tue 24/2/21	Tue 24/2/21	Tue 24/2/21	Tue 24/2/21	Tue 24/2/21	Tue 24/2/21	1087 days		
70	Setup Public Liaison Team	120 days	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	0 days		
71	Recruitment of Public Liaison Officer [A]	30 days	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	0 days		
72	Appointment and Acceptance of Public Liaison Officer [A]	30 days	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	Mon 23/5/15	0 days		
73	Works Area Establishment	44 days	Mon 23/9/1	Mon 23/9/1	Mon 23/9/1	Mon 23/9/1	Mon 23/9/1	Mon 23/9/1	15 days		
74	PM1001 - Possession of Works Area at 22 Fan Kam Road [A]	1 day	Mon 23/9/1	Mon 23/9/1	Mon 23/9/1	Mon 23/9/1	Mon 23/9/1	Mon 23/9/1	15 days		
75	Establish concrete haul road and slab [A]	43 days	Sat 23/9/2	Sat 23/9/2	Sat 23/9/2	Sat 23/9/2	Sat 23/9/2	Sat 23/9/2	1216 days		
76	Contractor's Accommodation (office and welfare facilities)	145 days	Wed 24/1/24	Wed 24/1/24	Wed 24/1/24	Wed 24/1/24	Wed 24/1/24	Wed 24/1/24	15 days		
77	Establish temporary site office (containers) [A]	24 days	Mon 23/9/2	Mon 23/9/2	Mon 23/9/2	Mon 23/9/2	Mon 23/9/2	Mon 23/9/2	15 days		
78	C9 Tendering procedure for Contractor's Site Office [A]	28 days	Sat 23/9/2	Sat 23/9/2	Sat 23/9/2	Sat 23/9/2	Sat 23/9/2	Sat 23/9/2	1114 days		
79	Proposal and acceptance of Temp. Works Design and Method Statement [A]	35 days	Sat 23/9/30	Sat 23/9/30	Sat 23/9/30	Sat 23/9/30	Sat 23/9/30	Sat 23/9/30	98		
80	Construction of Footing [A]	15 days	Sat 23/11/4	Sat 23/11/4	Sat 23/11/4	Sat 23/11/4	Sat 23/11/4	Sat 23/11/4	99		
81	Construction of Structure [A]	45 days	Sun 23/11/19	Tue 24/1/2	Sun 23/11/19	Tue 24/1/2	Sun 23/11/19	Tue 24/1/2	99		
82	Interior furnishing and Furnitures [A]	15 days	Wed 24/1/3	Wed 24/1/3	Wed 24/1/3	Wed 24/1/3	Wed 24/1/3	Wed 24/1/3	114 days		
83	Move-in [A]	7 days	Wed 24/1/18	Wed 24/1/18	Wed 24/1/18	Wed 24/1/18	Wed 24/1/18	Wed 24/1/18	114 days		
84	access date of Portion A	1374 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days		
85	Section I	104	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days		
86	access date of Portion A	270 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days		
87	Period of section I (Sung Shan New Village)	1095 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	129 days		
88	Planned Completion Day	200 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
89	Early access (partial) [A]	130 days	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	Mon 26/10/5	0 days		
90	Site Establishment	878 days	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	0 days		
91	Prepare and Accept Temp. Works Design and Method Statement	664 days	Tue 23/9/26	Tue 23/9/26	Tue 23/9/26	Tue 23/9/26	Tue 23/9/26	Tue 23/9/26	0 days		
92	Public Liaison and Negotiation with Village Rep.	164 days	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	0 days		
93	Initial Survey	714 days	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	95 days		
94	Initial Safety & Environmental measures [A]	28 days	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	0 days		
95	Setup of instrumentation and monitoring [A]	21 days	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	Fri 24/2/23	0 days		
96	EIAO Commencement of Construction [A]	1 day	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	899 days		

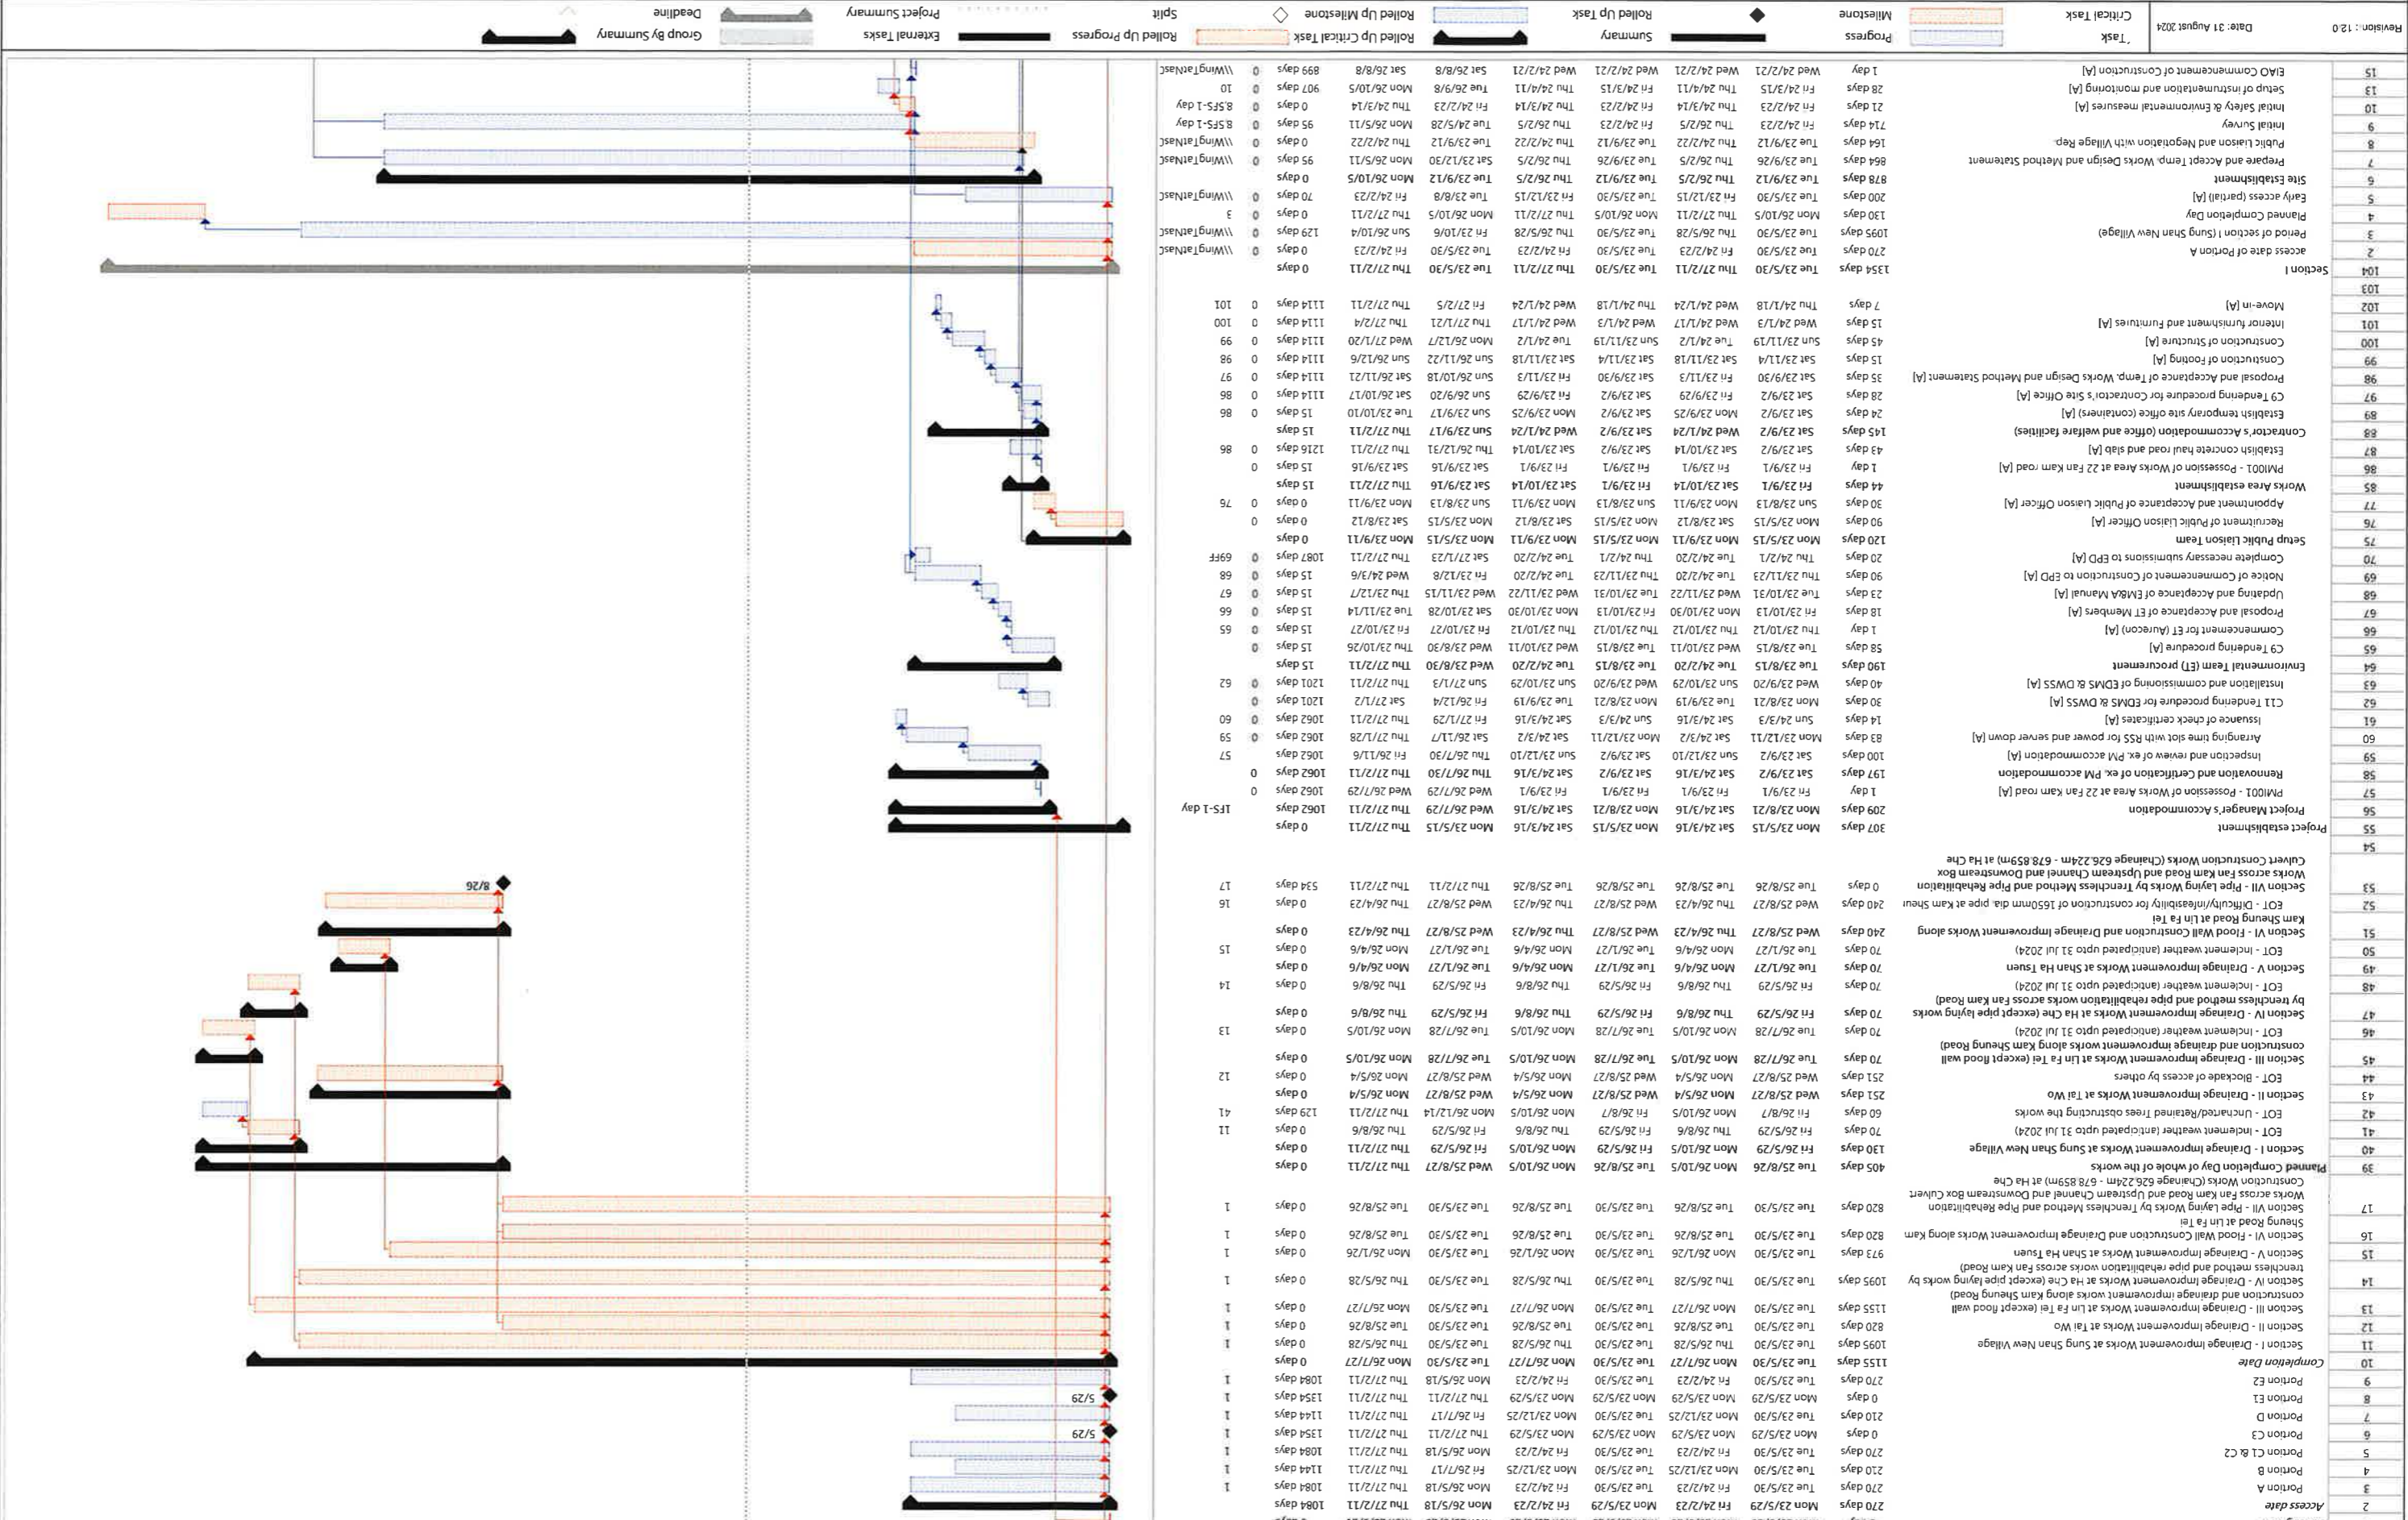

ID	Task Name	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	Free Slack	Predecessors
16	Environmental Baseline Monitoring [A]	Tue 24/1/23	Tue 24/1/23	Tue 24/1/23	Tue 24/1/23	Tue 24/1/23	Tue 24/1/23	0 days	0 days	15FS-30 days
17	Condition Survey [A]	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	0 days	0 days	0 days
18	Vegetation Survey [A]	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	0 days	0 days	0 days
19	Tree Survey [A]	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	0 days	0 days	0 days
20	[P]lixix] TRFP for Additional Trees (impact to be ascertained)	Fri 24/4/12	Fri 24/4/12	Fri 24/4/12	Fri 24/4/12	Fri 24/4/12	Fri 24/4/12	0 days	0 days	0 days
21	[P]li-xxx] Aquilaria sinensis seedling (impact to be ascertained)	Tue 24/2/20	Fri 24/4/19	Tue 24/2/20	Fri 24/4/19	Tue 24/2/20	Fri 24/4/19	60 days	0 days	0 days
22	Site Clearance [A]	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	0 days	0 days	0 days
23	UI detection	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	0 days	0 days	0 days
24	Establish accesses to channels [A]	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	0 days	0 days	0 days
25	Guarding / Barrier / Hoarding [A]	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	Mon 24/6/10	0 days	0 days	0 days
26	Drainage Channels Works	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	0 days	0 days	0 days
27	Excavate & Backfill ex. Unregistered feature [A]	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	0 days	0 days	0 days
28	Relocate/Direct ex. Utilities [A]	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	0 days	0 days	0 days
29	Demolish & relocate metal frame YLL796/B/9 [A]	Wed 24/7/31	Thu 24/8/29	Wed 24/7/31	Thu 24/8/29	Wed 24/7/31	Thu 24/8/29	0 days	0 days	0 days
30	[P]li-017] Unchartered/Additional Trees obstructing the works (impact to be ascertained)	Fri 24/8/30	Mon 24/10/28	Fri 24/8/30	Mon 24/10/28	Fri 24/8/30	Mon 24/10/28	0 days	0 days	0 days
31	SSNV04 CHA300-00-CHA400.00	Thu 24/10/29	Thu 25/1/16	Thu 24/10/29	Thu 25/1/16	Thu 24/10/29	Thu 25/1/16	0 days	0 days	0 days
32	Sheetpiling & Temp. Drainage Division	Tue 24/11/27	Tue 24/12/17	Tue 24/11/27	Tue 24/12/17	Tue 24/11/27	Tue 24/12/17	0 days	0 days	0 days
33	Excavation and Lateral Support	Tue 24/11/27	Tue 24/12/31	Tue 24/11/27	Tue 24/12/31	Tue 24/11/27	Tue 24/12/31	0 days	0 days	0 days
34	Ground and Edge Beams	Tue 24/11/26	Tue 24/12/25	Tue 24/11/26	Tue 24/12/25	Tue 24/11/26	Tue 24/12/25	0 days	0 days	0 days
35	Rebar Fixing	Tue 24/11/26	Sun 24/12/15	Tue 24/11/26	Sun 24/12/15	Tue 24/11/26	Sun 24/12/15	0 days	0 days	0 days
36	Formwork Erection and Cast-in-items	Fri 24/12/6	Fri 24/12/25	Fri 24/12/6	Fri 24/12/25	Fri 24/12/6	Fri 24/12/25	0 days	0 days	0 days
37	Concreting	Mon 24/12/16	Mon 24/12/16	Mon 24/12/16	Mon 24/12/16	Mon 24/12/16	Mon 24/12/16	0 days	0 days	0 days
38	Walls	Tue 24/12/17	Tue 24/12/17	Tue 24/12/17	Tue 24/12/17	Tue 24/12/17	Tue 24/12/17	0 days	0 days	0 days
39	Rebar Fixing	Tue 24/12/17	Sun 25/1/5	Tue 24/12/17	Sun 25/1/5	Tue 24/12/17	Sun 25/1/5	0 days	0 days	0 days
40	Formwork Erection and Cast-in-items	Wed 24/12/27	Mon 25/1/6	Wed 24/12/27	Mon 25/1/6	Wed 24/12/27	Mon 25/1/6	0 days	0 days	0 days
41	Concreting	Mon 25/1/6	Mon 25/1/6	Mon 25/1/6	Mon 25/1/6	Mon 25/1/6	Mon 25/1/6	0 days	0 days	0 days
42	Backfilling and Compaction	Tue 25/1/7	Thu 25/1/16	Tue 25/1/7	Thu 25/1/16	Tue 25/1/7	Thu 25/1/16	0 days	0 days	0 days
43	Removal of Sheepsfies	Thu 25/1/17	Thu 25/1/17	Thu 25/1/17	Thu 25/1/17	Thu 25/1/17	Thu 25/1/17	0 days	0 days	0 days
44	SSNV03 CHA400.00-CHA500.00	Fri 25/1/17	Thu 25/4/24	Fri 25/1/17	Thu 25/4/24	Fri 25/1/17	Thu 25/4/24	0 days	0 days	0 days
45	Sheetpiling & Temp. Drainage Division	Wed 25/3/5	Wed 25/3/5	Wed 25/3/5	Wed 25/3/5	Wed 25/3/5	Wed 25/3/5	0 days	0 days	0 days
46	Excavation and Lateral Support	Wed 25/3/17	Mon 25/3/17	Wed 25/3/17	Mon 25/3/17	Wed 25/3/17	Mon 25/3/17	0 days	0 days	0 days
47	Ground and Edge Beams	Mon 25/2/10	Tue 25/3/11	Mon 25/2/10	Tue 25/3/11	Mon 25/2/10	Tue 25/3/11	0 days	0 days	0 days
48	Rebar Fixing	Mon 25/2/10	Sat 25/3/1	Mon 25/2/10	Sat 25/3/1	Mon 25/2/10	Sat 25/3/1	0 days	0 days	0 days
49	Formwork Erection and Cast-in-items	Thu 25/2/20	Mon 25/3/3	Thu 25/2/20	Mon 25/3/3	Thu 25/2/20	Mon 25/3/3	0 days	0 days	0 days
50	Concreting	Mon 25/3/2	Mon 25/3/2	Mon 25/3/2	Mon 25/3/2	Mon 25/3/2	Mon 25/3/2	0 days	0 days	0 days
51	Walls	Tue 25/3/4	Tue 25/3/4	Tue 25/3/4	Tue 25/3/4	Tue 25/3/4	Tue 25/3/4	0 days	0 days	0 days
52	Rebar Fixing	Wed 25/3/4	Tue 25/3/4	Wed 25/3/4	Tue 25/3/4	Wed 25/3/4	Tue 25/3/4	0 days	0 days	0 days
53	Formwork Erection and Cast-in-items	Wed 25/3/4	Wed 25/3/4	Wed 25/3/4	Wed 25/3/4	Wed 25/3/4	Wed 25/3/4	0 days	0 days	0 days
54	Concreting	Mon 25/3/24	Tue 25/3/24	Mon 25/3/24	Tue 25/3/24	Mon 25/3/24	Tue 25/3/24	0 days	0 days	0 days
55	Backfilling and Compaction	Wed 25/3/26	Mon 25/4/4	Wed 25/3/26	Mon 25/4/4	Wed 25/3/26	Mon 25/4/4	0 days	0 days	0 days
56	Removal of Sheepsfies	Sat 25/4/5	Thu 25/4/24	Sat 25/4/5	Thu 25/4/24	Sat 25/4/5	Thu 25/4/24	0 days	0 days	0 days
57	1:2 slope works	Thu 25/4/25	Thu 25/5/29	Thu 25/4/25	Thu 25/5/29	Thu 25/4/25	Thu 25/5/29	0 days	0 days	0 days
58	Demolish & relocate OSC YLL796/B/14,14B	Mon 25/4/28	Tue 25/4/28	Mon 25/4/28	Tue 25/4/28	Mon 25/4/28	Tue 25/4/28	0 days	0 days	0 days
59	Demolish & relocate fence & wall YLL796/B/14	Mon 25/4/28	Tue 25/4/28	Mon 25/4/28	Tue 25/4/28	Mon 25/4/28	Tue 25/4/28	0 days	0 days	0 days
60	Demolish & relocate wall, hoarding YLL796/B/13,13B	Tue 25/4/28	Mon 25/4/28	Tue 25/4/28	Mon 25/4/28	Tue 25/4/28	Mon 25/4/28	0 days	0 days	0 days
61	SSNV05 CHA200.00-CHA300.00	Tue 25/4/29	Tue 25/4/29	Tue 25/4/29	Tue 25/4/29	Tue 25/4/29	Tue 25/4/29	0 days	0 days	0 days
62	Sheetpiling & Temp. Drainage Division	Tue 25/4/29	Sun 25/6/15	Tue 25/4/29	Sun 25/6/15	Tue 25/4/29	Sun 25/6/15	0 days	0 days	0 days
63	Excavation and Lateral Support	Fri 25/6/15	Fri 25/6/27	Fri 25/6/15	Fri 25/6/27	Fri 25/6/15	Fri 25/6/27	0 days	0 days	0 days
64	Ground and Edge Beams	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	0 days	0 days	0 days
65	Rebar Fixing	Wed 25/6/11	Fri 25/6/23	Wed 25/6/11	Fri 25/6/23	Wed 25/6/11	Fri 25/6/23	0 days	0 days	0 days
66	Formwork Erection and Cast-in-items	Sat 25/6/19	Thu 25/6/19	Sat 25/6/19	Thu 25/6/19	Sat 25/6/19	Thu 25/6/19	0 days	0 days	0 days
67	Concreting	Mon 25/6/8	Sun 25/6/8	Mon 25/6/8	Sun 25/6/8	Mon 25/6/8	Sun 25/6/8	0 days	0 days	0 days
68	Walls	Tue 25/7/8	Mon 25/6/9	Tue 25/7/8	Mon 25/6/9	Tue 25/7/8	Mon 25/6/9	0 days	0 days	0 days
69	Rebar Fixing	Mon 25/6/9	Sat 25/6/28	Mon 25/6/9	Sat 25/6/28	Mon 25/6/9	Sat 25/6/28	0 days	0 days	0 days
70	Formwork Erection and Cast-in-items	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	0 days	0 days	0 days
71	Concreting	Sun 25/6/29	Sun 25/6/29	Sun 25/6/29	Sun 25/6/29	Sun 25/6/29	Sun 25/6/29	0 days	0 days	0 days
72	Backfilling and Compaction	Mon 25/6/30	Sat 25/7/19	Mon 25/6/30	Sat 25/7/19	Mon 25/6/30	Sat 25/7/19	0 days	0 days	0 days
73	Removal of Sheepsfies	Thu 25/7/10	Thu 25/7/10	Thu 25/7/10	Thu 25/7/10	Thu 25/7/10	Thu 25/7/10	0 days	0 days	0 days
74	SSNV06 CHA100.00-CHA200.00	Mon 25/7/20	Mon 25/7/20	Mon 25/7/20	Mon 25/7/20	Mon 25/7/20	Mon 25/7/20	0 days	0 days	0 days
75	Sheetpiling & Temp. Drainage Division	Fri 25/7/20	Fri 25/7/20	Fri 25/7/20	Fri 25/7/20	Fri 25/7/20	Fri 25/7/20	0 days	0 days	0 days
76	Excavation and Lateral Support	Wed 25/8/1	Wed 25/8/1	Wed 25/8/1	Wed 25/8/1	Wed 25/8/1	Wed 25/8/1	0 days	0 days	0 days
77	Ground and Edge Beams	Tue 25/8/9	Tue 25/8/9	Tue 25/8/9	Tue 25/8/9	Tue 25/8/9	Tue 25/8/9	0 days	0 days	0 days
78	Rebar Fixing	Mon 25/8/13	Mon 25/8/13	Mon 25/8/13	Mon 25/8/13	Mon 25/8/13	Mon 25/8/13	0 days	0 days	0 days
79	Formwork Erection and Cast-in-items	Tue 25/8/21	Thu 25/8/21	Tue 25/8/21	Thu 25/8/21	Tue 25/8/21	Thu 25/8/21	0 days	0 days	0 days
80	Concreting	Fri 25/8/29	Fri 25/8/29	Fri 25/8/29	Fri 25/8/29	Fri 25/8/29	Fri 25/8/29	0 days	0 days	0 days
81	Walls	Mon 25/8/30	Sat 25/8/30	Mon 25/8/30	Sat 25/8/30	Mon 25/8/30	Sat 25/8/30	0 days	0 days	0 days
82	Rebar Fixing	Mon 25/8/30	Sat 25/8/30	Mon 25/8/30	Sat 25/8/30	Mon 25/8/30	Sat 25/8/30	0 days	0 days	0 days
83	Formwork Erection and Cast-in-items	Sat 25/8/30	Mon 25/8/30	Sat 25/8/30	Mon 25/8/30	Sat 25/8/30	Mon 25/8/30	0 days	0 days	0 days
84	Concreting	Sat 25/8/30	Sat 25/8/30	Sat 25/8/30	Sat 25/8/30	Sat 25/8/30	Sat 25/8/30	0 days	0 days	0 days
85	Backfilling and Compaction	Sun 25/8/31	Sun 25/8/31	Sun 25/8/31	Sun 25/8/31	Sun 25/8/31	Sun 25/8/31	0 days	0 days	0 days
86	Removal of Sheepsfies	Mon 25/9/10	Mon 25/9/10	Mon 25/9/10	Mon 25/9/10	Mon 25/9/10	Mon 25/9/10	0 days	0 days	0 days
87	Annual Escapes Ramp	Mon 25/9/10	Mon 25/9/10	Mon 25/9/10	Mon 25/9/10	Mon 25/9/10	Mon 25/9/10	0 days	0 days	0 days
88	Relocate/Direct ex. Utilities	Sat 25/9/20	Sat 25/9/20	Sat 25/9/20	Sat 25/9/20	Sat 25/9/20	Sat 25/9/20	0 days	0 days	0 days
89	Demolish & relocate wall and porch YLL796/B/5,5A	Sat 25/9/20	Sat 25/9/20	Sat 25/9/20	Sat 25/9/20	Sat 25/9/20	Sat 25/9/20	0 days	0 days	0 days
90	Demolish & relocate booth, metal frame YLL796/B/16	Fri 25/9/20	Fri 25/9/20	Fri 25/9/20	Fri 25/9/20	Fri 25/9/20	Fri 25/9/20	0 days	0 days	0 days
91	Demolish & relocate wall YLL796/B/17	Sat 25/9/20	Fri 25/10/3	Sat 25/9/20	Fri 25/10/3	Sat 25/9/20	Fri 25/10/3	0 days	0 days	0 days
92	SSNV07 CHA0.00-CHA100.00	Sat 25/10/4	Fri 26/1/23	Sat 25/10/4	Fri 26/1/23	Sat 25/10/4	Fri 26/1/23	0 days	0 days	0 days
93	Sheetpiling & Temp. Drainage Division	Sat 25/10/4	Thu 25/11/20	Sat 25/10/4	Thu 25/11/20	Sat 25/10/4	Thu 25/11/20	0 days	0 days	0 days
94	Excavation and Lateral Support	Tue 25/10/16	Tue 25/10/16	Tue 25/10/16	Tue 25/10/16	Tue 25/10/16	Tue 25/10/16	0 days	0 days	0 days
95	Ground and Edge Beams	Mon 25/11/24	Mon 25/11/24	Mon 25/11/24	Mon 25/11/24	Mon 25/11/24	Mon 25/11/24	0 days	0 days	0 days
96	Rebar Fixing	Tue 25/11/16	Sun 25/11/16	Tue 25/11/16	Sun 25/11/16	Tue 25/11/16	Sun 25/11/16	0 days	0 days	0 days

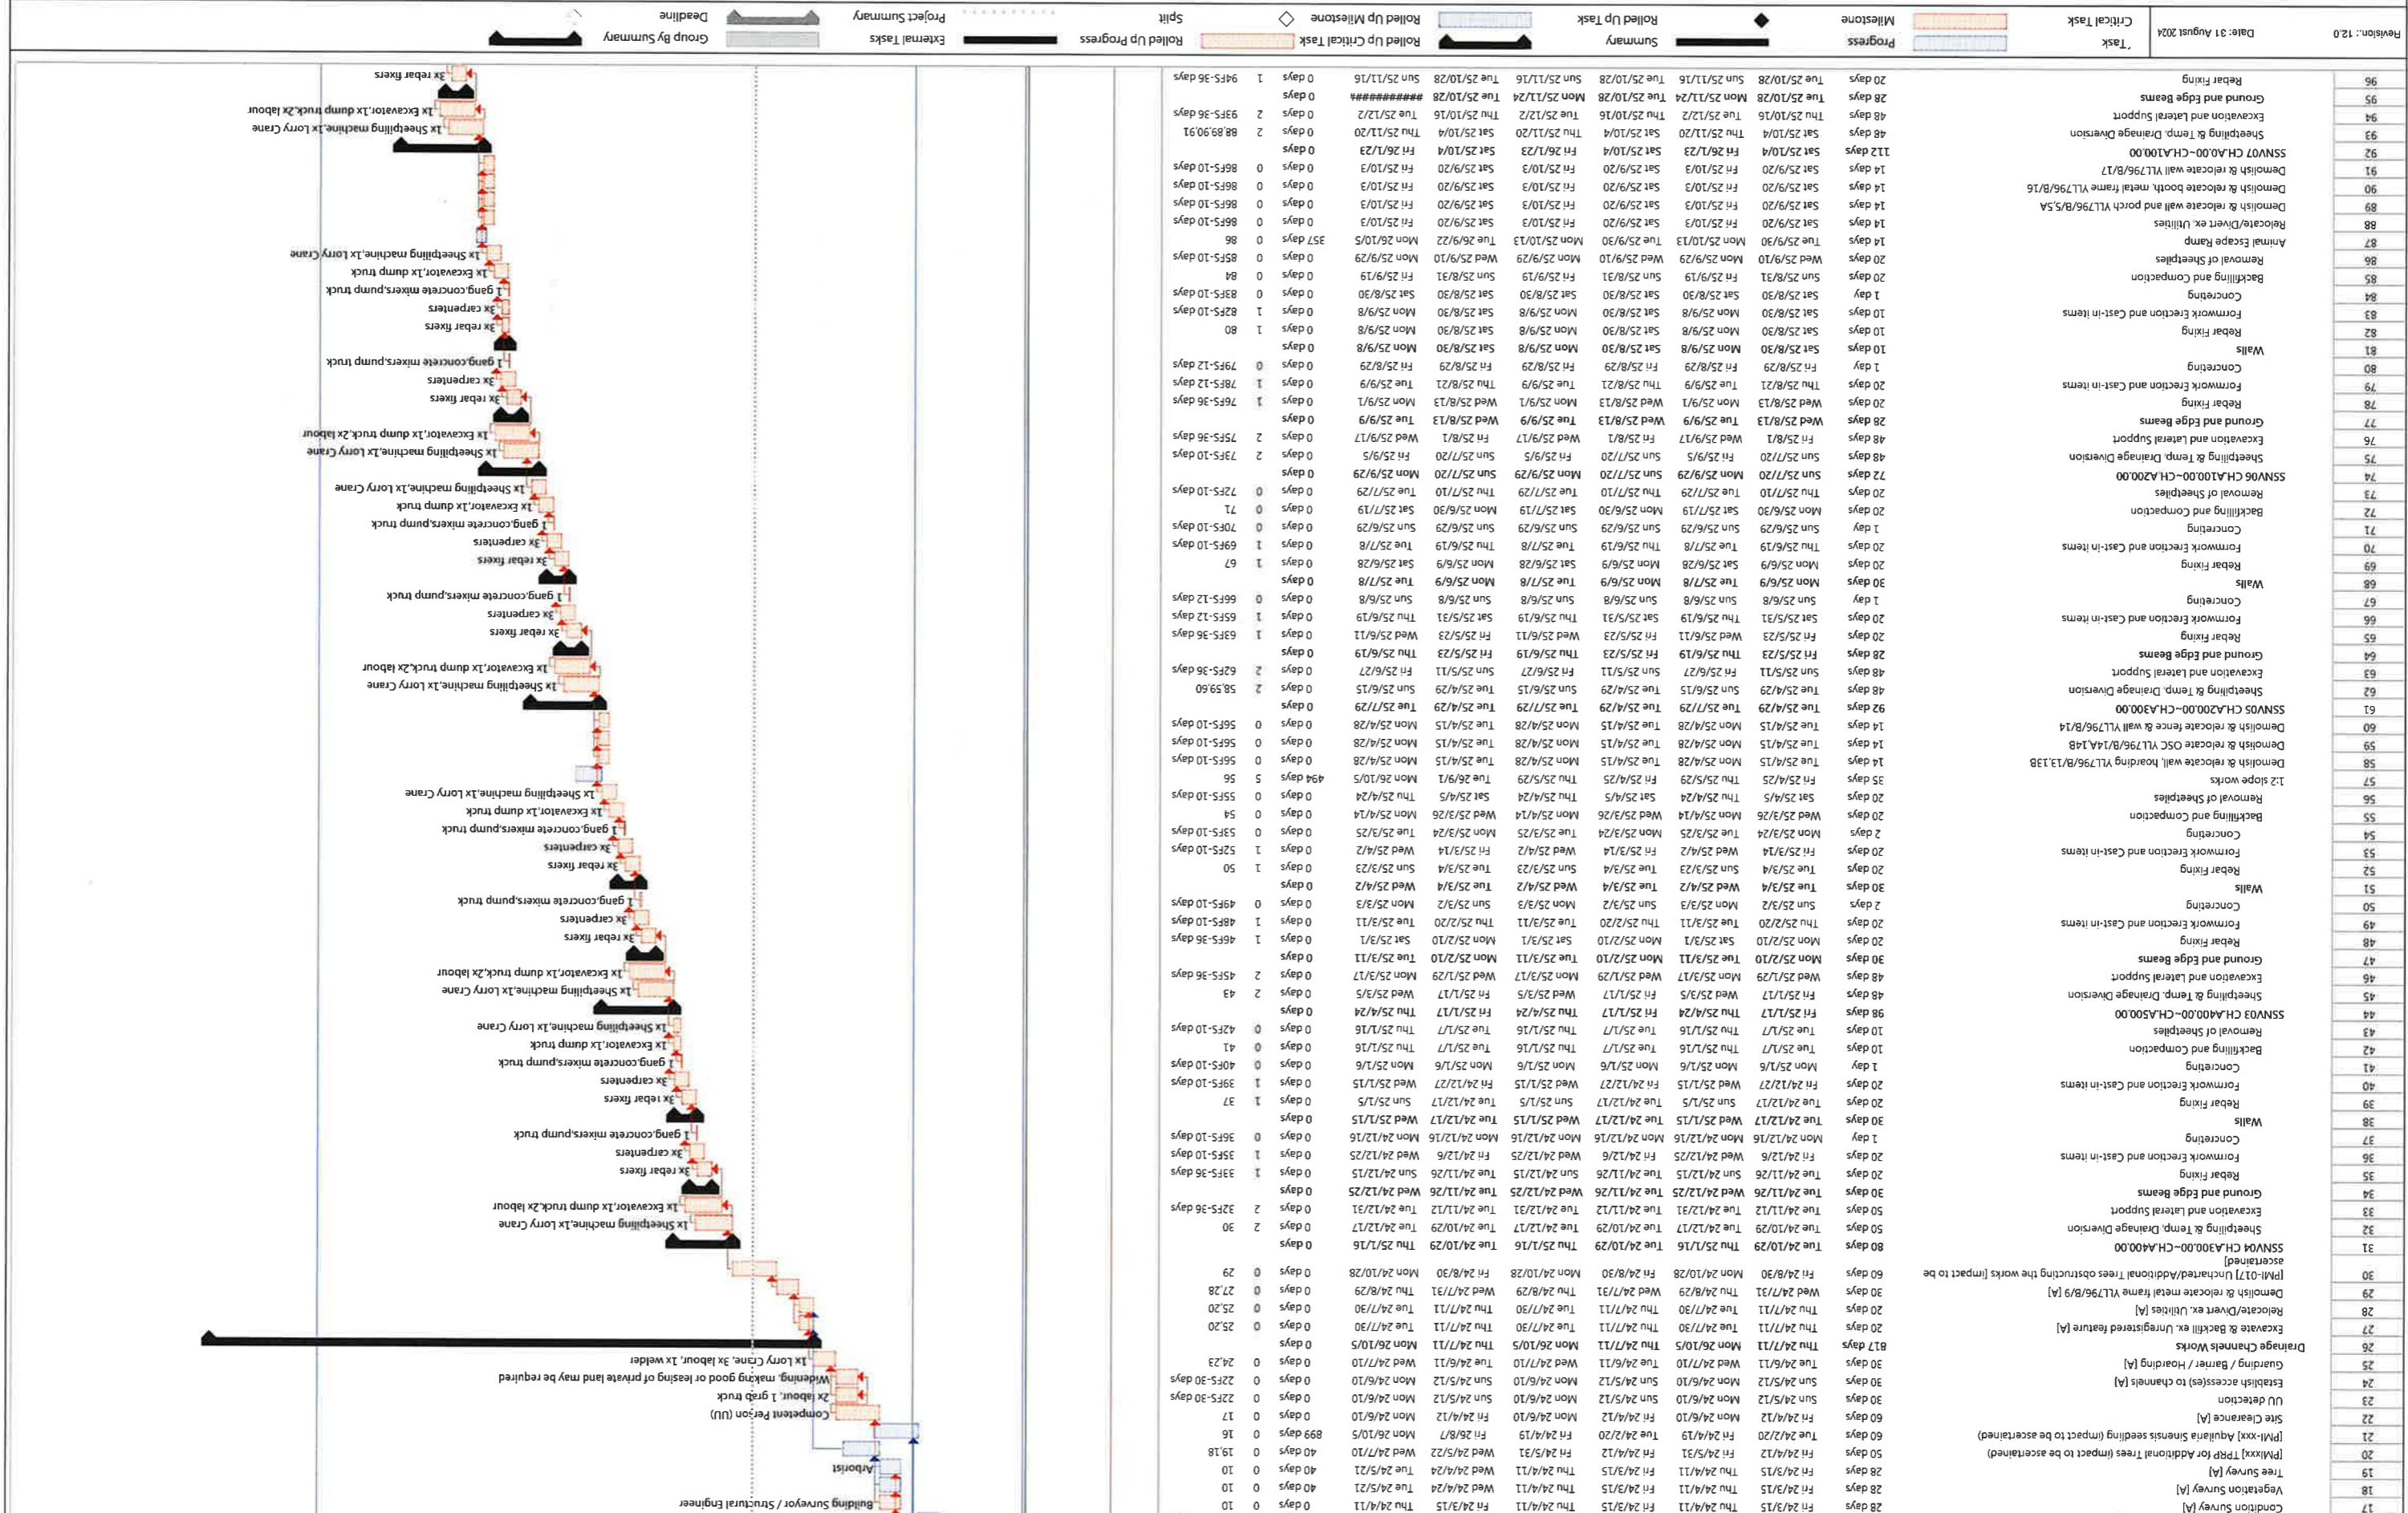


ID	Task Name	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TR	Predecessors
40	Rebar Fixing	Sun 24/12/21	Sat 25/1/4	Sun 24/12/21	Sat 25/1/4	Sun 24/12/21	Sat 25/1/4	0 days	1	38
41	Formwork Erection and Cast-in Items	Sun 24/12/15	Sat 25/1/18	Sun 24/12/15	Sat 25/1/18	Sun 24/12/15	Sat 25/1/18	0 days	1	40S-21 days
42	Concrete	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	0 days	1	40S-21 days
43	Backfilling and Compaction	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	Sun 24/12/29	0 days	1	40S-21 days
44	Removal of Sheepiles	Sat 25/1/11	Sun 25/2/9	Sat 25/1/11	Sun 25/2/9	Sat 25/1/11	Sun 25/2/9	0 days	0	42
45	Connection to ex Channel at Outlet	Thu 25/1/23	Thu 25/1/23	Thu 25/1/23	Thu 25/1/23	Thu 25/1/23	Thu 25/1/23	0 days	0	44S-18 days
46	CH A100-CH A200	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	0 days	1	44S-18 days
47	Sheepiling & Temp. Drainage Diversion (for non-open-cut portions)	Mon 25/3/24	Mon 25/3/31	Mon 25/3/24	Mon 25/3/31	Mon 25/3/24	Mon 25/3/31	0 days	1	44S-18 days
48	Excavation and Lateral Support	Sun 25/2/12	Sun 25/3/18	Sun 25/2/12	Sun 25/3/18	Sun 25/2/12	Sun 25/3/18	0 days	1	47S-36 days
49	Base Slab	Mon 25/3/21	Mon 25/3/21	Mon 25/3/21	Mon 25/3/21	Mon 25/3/21	Mon 25/3/21	0 days	1	47S-36 days
50	Rebar Fixing	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	0 days	1	48S-36 days
51	Formwork Erection and Cast-in Items	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	0 days	1	50S-21 days
52	Concrete	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	Mon 25/3/31	0 days	1	50S-21 days
53	No works at wet season	1 day	1 day	1 day	1 day	1 day	1 day	0 days	0	52
54	CH A100-CH A200 (continue)	Wed 25/12/17	Wed 25/12/17	Wed 25/12/17	Wed 25/12/17	Wed 25/12/17	Wed 25/12/17	0 days	0	52
55	Walls	Wed 25/10/1	Wed 25/11/18	Wed 25/10/1	Wed 25/11/18	Wed 25/10/1	Wed 25/11/18	0 days	1	52
56	Rebar Fixing	Wed 25/10/1	Wed 25/11/18	Wed 25/10/1	Wed 25/11/18	Wed 25/10/1	Wed 25/11/18	0 days	1	53
57	Formwork Erection and Cast-in Items	Wed 25/10/15	Wed 25/11/18	Wed 25/10/15	Wed 25/11/18	Wed 25/10/15	Wed 25/11/18	0 days	1	53
58	Concrete	Wed 25/10/29	Wed 25/11/18	Wed 25/10/29	Wed 25/11/18	Wed 25/10/29	Wed 25/11/18	0 days	1	56S-21 days
59	Backfilling and Compaction	Thu 25/10/30	Thu 25/10/30	Thu 25/10/30	Thu 25/10/30	Thu 25/10/30	Thu 25/10/30	0 days	0	58
60	Removal of Sheepiles	Thu 25/11/13	Thu 25/12/17	Thu 25/11/13	Thu 25/12/17	Thu 25/11/13	Thu 25/12/17	0 days	0	59S-21 days
61	CH A169-CH A100	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	0 days	0	59S-21 days
62	Sheepiling & Temp. Drainage Diversion (for non-open-cut portions)	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	0 days	1	60S-21 days
63	Excavation and Lateral Support	Sat 25/12/6	Mon 26/1/19	Sat 25/12/6	Mon 26/1/19	Sat 25/12/6	Mon 26/1/19	0 days	1	62S-36 days
64	Base Slab	Mon 25/12/15	Sun 26/1/18	Mon 25/12/15	Sun 26/1/18	Mon 25/12/15	Sun 26/1/18	0 days	1	62S-36 days
65	Rebar Fixing	Mon 25/12/15	Sun 26/1/18	Mon 25/12/15	Sun 26/1/18	Mon 25/12/15	Sun 26/1/18	0 days	1	63S-36 days
66	Formwork Erection and Cast-in Items	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	0 days	0	65S-21 days
67	Concrete	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	0 days	0	65S-21 days
68	Walls	Tue 26/1/13	Mon 26/1/13	Tue 26/1/13	Mon 26/1/13	Tue 26/1/13	Mon 26/1/13	0 days	0	66S-21 days
69	Rebar Fixing	Tue 26/1/13	Mon 26/1/13	Tue 26/1/13	Mon 26/1/13	Tue 26/1/13	Mon 26/1/13	0 days	1	67S-21 days
70	Formwork Erection and Cast-in Items	Mon 26/1/27	Mon 26/1/27	Mon 26/1/27	Mon 26/1/27	Mon 26/1/27	Mon 26/1/27	0 days	0	69S-21 days
71	Concrete	Tue 26/2/10	Tue 26/2/10	Tue 26/2/10	Tue 26/2/10	Tue 26/2/10	Tue 26/2/10	0 days	0	70S-21 days
72	Backfilling and Compaction	Wed 26/2/11	Wed 26/2/11	Wed 26/2/11	Wed 26/2/11	Wed 26/2/11	Wed 26/2/11	0 days	0	71
73	Removal of Sheepiles	Wed 26/2/25	Wed 26/3/1	Wed 26/2/25	Wed 26/3/1	Wed 26/2/25	Wed 26/3/1	0 days	0	72S-21 days
74	900 pipe with flap valve	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	0 days	0	73S-21 days
75	Box Culvert & Pedestrian Crossing	Wed 26/3/11	Wed 26/3/11	Wed 26/3/11	Wed 26/3/11	Wed 26/3/11	Wed 26/3/11	0 days	0	73S-21 days
76	ABWF	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	0 days	0	73S-21 days
77	Bedding works	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	Tue 26/3/11	0 days	0	73S-21 days
78	No works at wet season	Wed 26/3/14	Mon 26/5/4	Wed 26/3/14	Mon 26/5/4	Wed 26/3/14	Mon 26/5/4	0 days	0	74S-76.77
79	U-Channel Works	Sat 26/3/14	Thu 26/4/23	Sat 26/3/14	Thu 26/4/23	Sat 26/3/14	Thu 26/4/23	0 days	0	74S-76.77
80	CH A00-CH A16.60.900CU.L=16.60	Sat 26/3/14	Thu 26/4/23	Sat 26/3/14	Thu 26/4/23	Sat 26/3/14	Thu 26/4/23	0 days	1	72S-4 days
81	Excavation and Lateral Support	Wed 26/3/25	Thu 26/4/23	Wed 26/3/25	Thu 26/4/23	Wed 26/3/25	Thu 26/4/23	0 days	1	72S-4 days
82	Channel Formwork Erection	Sat 26/4/4	Sat 26/4/4	Sat 26/4/4	Sat 26/4/4	Sat 26/4/4	Sat 26/4/4	0 days	0	81S-19 days
83	Concrete	Sun 26/4/5	Mon 26/5/4	Sun 26/4/5	Mon 26/5/4	Sun 26/4/5	Mon 26/5/4	0 days	0	82S-20 days
84	Drain Laying Works	Sun 26/4/5	Mon 26/5/4	Sun 26/4/5	Mon 26/5/4	Sun 26/4/5	Mon 26/5/4	0 days	0	82S-20 days
85	CH A16.60-CH A19.69.900FC.B.L=3.0.D=1.5	Sun 26/4/5	Mon 26/5/4	Sun 26/4/5	Mon 26/5/4	Sun 26/4/5	Mon 26/5/4	0 days	0	83
86	Excavation and Lateral Support	Mon 26/4/13	Mon 26/4/13	Mon 26/4/13	Mon 26/4/13	Mon 26/4/13	Mon 26/4/13	0 days	0	86S-10 days
87	Drain Laying	Wed 26/4/22	Thu 26/4/30	Wed 26/4/22	Thu 26/4/30	Wed 26/4/22	Thu 26/4/30	0 days	0	87S-5 days
88	Bedding and Backfilling	Wed 26/4/22	Thu 26/4/30	Wed 26/4/22	Thu 26/4/30	Wed 26/4/22	Thu 26/4/30	0 days	0	88S-5 days
89	Reinstatement	Sun 26/4/26	Mon 26/5/4	Sun 26/4/26	Mon 26/5/4	Sun 26/4/26	Mon 26/5/4	0 days	0	88S-5 days
107		Tue 23/5/30	Mon 26/1/5	Tue 23/5/30	Mon 26/1/5	Tue 23/5/30	Mon 26/1/5	0 days	0	107
108	Section III (In Fa)	Mon 26/1/23	Mon 26/1/23	Mon 26/1/23	Mon 26/1/23	Mon 26/1/23	Mon 26/1/23	0 days	0	108
2	section III (In Fa)	Mon 26/1/27	Mon 26/1/27	Mon 26/1/27	Mon 26/1/27	Mon 26/1/27	Mon 26/1/27	0 days	0	108
3	section III (In Fa)	Tue 23/5/30	Mon 26/1/27	Tue 23/5/30	Mon 26/1/27	Tue 23/5/30	Mon 26/1/27	0 days	0	115S days
4	Planned Completion Day	Mon 26/1/28	Mon 26/1/28	Mon 26/1/28	Mon 26/1/28	Mon 26/1/28	Mon 26/1/28	0 days	0	3
5	Early access (partial) (A)	Wed 23/5/30	Wed 23/5/30	Wed 23/5/30	Wed 23/5/30	Wed 23/5/30	Wed 23/5/30	0 days	0	3
6	Site Establishment	Tue 23/9/12	Wed 26/5/27	Tue 23/9/12	Wed 26/5/27	Tue 23/9/12	Wed 26/5/27	15 days	0	15 days
7	Prepare and Accept Temp. Works Design and Method Statement	Tue 23/9/12	Wed 26/5/27	Tue 23/9/12	Wed 26/5/27	Tue 23/9/12	Wed 26/5/27	15 days	0	15 days
8	Public Liaison and Negotiation with Village Rep. (A)	Thu 24/2/22	Wed 26/5/27	Thu 24/2/22	Wed 26/5/27	Thu 24/2/22	Wed 26/5/27	35 days	0	15 days
9	Initial Survey	Thu 24/2/23	Wed 26/5/27	Thu 24/2/23	Wed 26/5/27	Thu 24/2/23	Wed 26/5/27	35 days	0	15 days
11	Initial Safety & Environmental measures (A)	Thu 24/2/23	Thu 24/3/7	Thu 24/2/23	Thu 24/3/7	Thu 24/2/23	Thu 24/3/7	15 days	0	8.5S-1 day
12	EIA Commencement of Construction (A)	Wed 24/2/21	Mon 24/3/19	Wed 24/2/21	Mon 24/3/19	Wed 24/2/21	Mon 24/3/19	90 days	0	13S-30 days
13	Environmental Baseline Monitoring (A)	Mon 24/3/4	Mon 24/3/4	Mon 24/3/4	Mon 24/3/4	Mon 24/3/4	Mon 24/3/4	107 days	0	13S-30 days
16	Subcontracting of works	Sat 23/12/16	Wed 24/8/21	Sat 23/12/16	Wed 24/8/21	Sat 23/12/16	Wed 24/8/21	77S days	0	5
17	Setup of instrumentation and monitoring (A)	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	15 days	0	11
18	Condition Survey (A)	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	15 days	0	11
19	Freshwater Crab Translocation Plan (A)	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	15 days	0	11
20	Archaeological Survey	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	483 days	0	11
21	Tree Survey (A)	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	15 days	0	11
22	Vegetation Survey (A)	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	Mon 24/3/8	15 days	0	11
23	Site Clearance (A)	Sat 24/4/6	Sat 24/4/6	Sat 24/4/6	Sat 24/4/6	Sat 24/4/6	Sat 24/4/6	15 days	0	18.19
24	Site Clearance (A)	Sat 24/4/6	Sat 24/4/6	Sat 24/4/6	Sat 24/4/6	Sat 24/4/6	Sat 24/4/6	15 days	0	18.19
25	Establish accesses to channels (A)	Sun 24/4/7	Wed 24/5/1	Sun 24/4/7	Wed 24/5/1	Sun 24/4/7	Wed 24/5/1	15 days	0	24.23
26	Guarding / Barrier / Hoarding (A)	Mon 24/4/7	Mon 24/4/7	Mon 24/4/7	Mon 24/4/7	Mon 24/4/7	Mon 24/4/7	15 days	0	24.23
27	Drainage Channels Works	Thu 24/5/2	Thu 24/5/2	Thu 24/5/2	Thu 24/5/2	Thu 24/5/2	Thu 24/5/2	15 days	0	24.23
28	Demolish & relocate retaining wall VLL795/A4-5 (A)	Thu 24/5/2	Thu 24/5/2	Thu 24/5/2	Thu 24/5/2	Thu 24/5/2	Thu 24/5/2	15 days	0	24.23
29	Pedestrian & Vehicular Crossing no. 1 (A)	Sat 24/5/11	Mon 24/5/24	Sat 24/5/11	Mon 24/5/24	Sat 24/5/11	Mon 24/5/24	28S-21 days	4	29
30	CLP Cable Trough	Tue 24/6/25	Wed 24/7/24	Tue 24/6/25	Wed 24/7/24	Tue 24/6/25	Wed 24/7/24	932 days	3	29
31	LFT06 CH A173.5-CH A227.75 (FVCI)	Tue 24/6/18	Fri 24/10/18	Tue 24/6/18	Fri 24/10/18	Tue 24/6/18	Fri 24/10/18	15 days	1	29S-7 days
32	Temp. Drainage Diversion / Sheepiling (A)	Tue 24/6/18	Sat 24/7/27	Tue 24/6/18	Sat 24/7/27	Tue 24/6/18	Sat 24/7/27	15 days	1	29S-7 days
33	Excavation and Lateral Support (A)	Sat 24/7/13	Wed 24/8/21	Sat 24/7/13	Wed 24/8/21	Sat 24/7/13	Wed 24/8/21	15 days	1	32S-15 days
34	Ground and Edge Beams	Mon 24/8/5	Sat 24/9/14	Mon 24/8/5	Sat 24/9/14	Mon 24/8/5	Sat 24/9/14	15 days	1	32S-15 days

Task	Progress	Summary	Rolled Up Task	Rolled Up Milestone	Split	Project Summary	Group By Summary	Deadline
Task	Progress	Summary	Rolled Up Task	Rolled Up Milestone	Split	Project Summary	Group By Summary	Deadline


ID	Task Name	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TF4	Predecessors
35	Install precast reinforcement cage (ground beam) [A]	Mon 24/8/25	Mon 24/9/16	Mon 24/8/25	Mon 24/9/16	Mon 24/8/25	Mon 24/9/16	0	33FS-17 days	Mon 24/8/20
36	Rebar fixing [A]	Mon 24/8/25	Mon 24/9/16	Mon 24/8/25	Mon 24/9/16	Mon 24/8/25	Mon 24/9/16	0	36FS-20 days	Mon 24/8/20
37	Formwork Erection and Cast-in Items [A]	Wed 24/8/21	Wed 24/9/14	Wed 24/8/21	Wed 24/9/14	Wed 24/8/21	Wed 24/9/14	0	1 days	Mon 24/8/20
38	Concrete [A]	Thu 24/8/29	Thu 24/9/14	Thu 24/8/29	Thu 24/9/14	Thu 24/8/29	Thu 24/9/14	0	37FS-17 days	Mon 24/8/20
39	Walls	Mon 24/8/30	Mon 24/9/14	Mon 24/8/30	Mon 24/9/14	Mon 24/8/30	Mon 24/9/14	0	15 days	Mon 24/8/20
40	Rebar fixing	Mon 24/8/30	Mon 24/9/14	Mon 24/8/30	Mon 24/9/14	Mon 24/8/30	Mon 24/9/14	0	15 days	Mon 24/8/20
41	Formwork Erection and Cast-in Items	Sat 24/9/7	Tue 24/10/1	Sat 24/9/7	Tue 24/10/1	Sat 24/9/7	Tue 24/10/1	0	40FS-17 days	Mon 24/8/20
42	Concrete	Sun 24/9/15	Mon 24/9/30	Sun 24/9/15	Mon 24/9/30	Sun 24/9/15	Mon 24/9/30	0	41FS-17 days	Mon 24/8/20
43	Backfilling and Compaction	Mon 24/9/16	Mon 24/10/1	Mon 24/9/16	Mon 24/10/1	Mon 24/9/16	Mon 24/10/1	0	42	Mon 24/8/20
44	Removal of Sheepsheets	Tue 24/9/24	Tue 24/10/1	Tue 24/9/24	Tue 24/10/1	Tue 24/9/24	Tue 24/10/1	0	43FS-17 days	Mon 24/8/20
45	FT07 CHA227.5-CHA300.75	Mon 24/9/9	Mon 24/12/26	Mon 24/9/9	Mon 24/12/26	Mon 24/9/9	Mon 24/12/26	0	44FS-40 days	Mon 24/8/20
46	Temp. Drainage Diversion / Sheepsheeting	Mon 24/9/9	Mon 24/10/1	Mon 24/9/9	Mon 24/10/1	Mon 24/9/9	Mon 24/10/1	0	44FS-40 days	Mon 24/8/20
47	Excavation and Lateral Support	Wed 24/9/27	Wed 24/10/29	Wed 24/9/27	Wed 24/10/29	Wed 24/9/27	Wed 24/10/29	0	46FS-15 days	Mon 24/8/20
48	Ground and Edge Beams	Sun 24/10/13	Fri 24/11/22	Sun 24/10/13	Fri 24/11/22	Sun 24/10/13	Fri 24/11/22	0	46FS-15 days	Mon 24/8/20
49	Install precast reinforcement cage (ground beam)	Sun 24/10/13	Fri 24/11/22	Sun 24/10/13	Fri 24/11/22	Sun 24/10/13	Fri 24/11/22	0	47FS-17 days	Mon 24/8/20
50	Rebar fixing	Mon 24/10/21	Mon 24/11/14	Mon 24/10/21	Mon 24/11/14	Mon 24/10/21	Mon 24/11/14	0	47FS-17 days	Mon 24/8/20
51	Formwork Erection and Cast-in Items	Tue 24/10/29	Wed 24/11/22	Tue 24/10/29	Wed 24/11/22	Tue 24/10/29	Wed 24/11/22	0	49FS-20 days	Mon 24/8/20
52	Concrete	Wed 24/11/6	Wed 24/11/22	Wed 24/11/6	Wed 24/11/22	Wed 24/11/6	Wed 24/11/22	0	51FS-17 days	Mon 24/8/20
53	Walls	Mon 24/11/7	Mon 24/12/9	Mon 24/11/7	Mon 24/12/9	Mon 24/11/7	Mon 24/12/9	0	15 days	Mon 24/8/20
54	Rebar fixing	Sun 24/11/7	Mon 24/12/9	Sun 24/11/7	Mon 24/12/9	Sun 24/11/7	Mon 24/12/9	0	15 days	Mon 24/8/20
55	Formwork Erection and Cast-in Items	Mon 24/11/15	Mon 24/12/9	Mon 24/11/15	Mon 24/12/9	Mon 24/11/15	Mon 24/12/9	0	52	Mon 24/8/20
56	Backfilling and Compaction	Sun 24/11/24	Mon 24/12/18	Sun 24/11/24	Mon 24/12/18	Sun 24/11/24	Mon 24/12/18	0	54FS-17 days	Mon 24/8/20
57	Concrete	1 day	Sat 24/11/23	Sat 24/11/23	Sat 24/11/23	Sat 24/11/23	Sat 24/11/23	0	55FS-17 days	Mon 24/8/20
58	Removal of Sheepsheets	Mon 24/12/2	Mon 24/12/26	Mon 24/12/2	Mon 24/12/26	Mon 24/12/2	Mon 24/12/26	0	56	Mon 24/8/20
59	Pedestrian & Vehicular Crossing no. 2	Mon 24/12/10	Mon 26/1/6	Mon 24/12/10	Mon 26/1/6	Mon 24/12/10	Mon 26/1/6	637 days	58FS-17 days	Mon 24/8/20
60	FT05 CHA163.00-CHA173.50	Tue 24/12/10	Wed 24/12/19	Tue 24/12/10	Wed 24/12/19	Tue 24/12/10	Wed 24/12/19	15 days	58FS-17 days	Mon 24/8/20
61	Temp. Drainage Diversion / Sheepsheeting	Tue 24/12/10	Sun 25/1/5	Tue 24/12/10	Sun 25/1/5	Tue 24/12/10	Sun 25/1/5	15 days	58FS-17 days	Mon 24/8/20
62	Excavation and Lateral Support	Sun 24/12/22	Mon 24/1/17	Sun 24/12/22	Mon 24/1/17	Sun 24/12/22	Mon 24/1/17	0	61FS-15 days	Mon 24/8/20
63	Ground and Edge Beams	Wed 25/1/1	Wed 25/1/22	Wed 25/1/1	Wed 25/1/22	Wed 25/1/1	Wed 25/1/22	0	61FS-15 days	Mon 24/8/20
64	Rebar fixing	Wed 25/1/1	Sat 25/1/25	Wed 25/1/1	Sat 25/1/25	Wed 25/1/1	Sat 25/1/25	0	62FS-17 days	Mon 24/8/20
65	Formwork Erection and Cast-in Items	Thu 25/1/7	Mon 25/1/27	Thu 25/1/7	Mon 25/1/27	Thu 25/1/7	Mon 25/1/27	0	64FS-17 days	Mon 24/8/20
66	Concrete	1 day	Sat 25/1/17	Sat 25/1/17	Sat 25/1/17	Sat 25/1/17	Sat 25/1/17	0	65FS-17 days	Mon 24/8/20
67	Walls	Sat 25/1/18	Wed 25/2/19	Sat 25/1/18	Wed 25/2/19	Sat 25/1/18	Wed 25/2/19	0	66	Mon 24/8/20
68	Rebar fixing	Wed 25/2/19	Wed 25/2/26	Wed 25/2/19	Wed 25/2/26	Wed 25/2/19	Wed 25/2/26	0	68FS-17 days	Mon 24/8/20
69	Formwork Erection and Cast-in Items	Mon 25/2/23	Mon 25/2/23	Mon 25/2/23	Mon 25/2/23	Mon 25/2/23	Mon 25/2/23	0	69FS-17 days	Mon 24/8/20
70	Concrete	1 day	Mon 25/2/23	Mon 25/2/23	Mon 25/2/23	Mon 25/2/23	Mon 25/2/23	0	70	Mon 24/8/20
71	Removal of Sheepsheets	Thu 25/2/24	Mon 25/2/28	Thu 25/2/24	Mon 25/2/28	Thu 25/2/24	Mon 25/2/28	0	71FS-7 days	Mon 24/8/20
72	Backfilling and Compaction	Mon 25/2/26	Mon 25/2/26	Mon 25/2/26	Mon 25/2/26	Mon 25/2/26	Mon 25/2/26	0	72FS-7 days	Mon 24/8/20
73	Animal Escape Ramps	Fri 25/2/20	Mon 26/10/5	Fri 25/2/20	Mon 26/10/5	Fri 25/2/20	Mon 26/10/5	592 days	72FS-7 days	Mon 24/8/20
74	Demolish & relocate retaining wall YLL796/A/5-6	Fri 25/2/20	Mon 26/10/5	Fri 25/2/20	Mon 26/10/5	Fri 25/2/20	Mon 26/10/5	592 days	72FS-7 days	Mon 24/8/20
75	Demolish & relocate AFD Weir & pedestrian crossing	Sat 25/3/1	Sat 25/3/1	Sat 25/3/1	Sat 25/3/1	Sat 25/3/1	Sat 25/3/1	0	72FS-17 days	Mon 24/8/20
76	FT02 CHA100.00-CHA163.00	Mon 25/3/5	Mon 25/3/5	Mon 25/3/5	Mon 25/3/5	Mon 25/3/5	Mon 25/3/5	0	74FS-20 days	Mon 24/8/20
77	Temp. Drainage Diversion / Sheepsheeting	Mon 25/3/6	Mon 25/3/16	Mon 25/3/6	Mon 25/3/16	Mon 25/3/6	Mon 25/3/16	0	77FS-15 days	Mon 24/8/20
78	Excavation and Lateral Support	Thu 25/3/20	Mon 25/3/31	Thu 25/3/20	Mon 25/3/31	Thu 25/3/20	Mon 25/3/31	0	78FS-15 days	Mon 24/8/20
79	Ground and Edge Beams	Fri 25/3/28	Tue 25/4/1	Fri 25/3/28	Tue 25/4/1	Fri 25/3/28	Tue 25/4/1	0	78FS-15 days	Mon 24/8/20
80	Rebar fixing	Mon 25/3/24	Mon 25/3/24	Mon 25/3/24	Mon 25/3/24	Mon 25/3/24	Mon 25/3/24	0	78FS-15 days	Mon 24/8/20
81	Formwork Erection and Cast-in Items	Tue 25/4/1	Sat 25/4/16	Tue 25/4/1	Sat 25/4/16	Tue 25/4/1	Sat 25/4/16	0	80FS-17 days	Mon 24/8/20
82	Concrete	Sun 25/3/16	Mon 25/3/16	Sun 25/3/16	Mon 25/3/16	Sun 25/3/16	Mon 25/3/16	0	81FS-17 days	Mon 24/8/20
83	Walls	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	0	81FS-17 days	Mon 24/8/20
84	Rebar fixing	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	Mon 25/3/17	0	82	Mon 24/8/20
85	Formwork Erection and Cast-in Items	Wed 25/4/2	Wed 25/4/18	Wed 25/4/2	Wed 25/4/18	Wed 25/4/2	Wed 25/4/18	0	84FS-17 days	Mon 24/8/20
86	Concrete	1 day	Wed 25/4/2	Wed 25/4/2	Wed 25/4/2	Wed 25/4/2	Wed 25/4/2	0	85FS-17 days	Mon 24/8/20
87	Backfilling and Compaction	Thu 25/4/3	Mon 25/4/27	Thu 25/4/3	Mon 25/4/27	Thu 25/4/3	Mon 25/4/27	0	86	Mon 24/8/20
88	Removal of Sheepsheets	Fri 25/4/11	Mon 25/5/5	Fri 25/4/11	Mon 25/5/5	Fri 25/4/11	Mon 25/5/5	0	87FS-17 days	Mon 24/8/20
89	Pedestrian Crossing no. 2	Sat 25/4/19	Fri 27/12/22	Sat 25/4/19	Fri 27/12/22	Sat 25/4/19	Fri 27/12/22	643 days	87FS-17 days	Mon 24/8/20
90	Demolish & relocate retaining wall YLL796/A/14-15	Sat 25/4/19	Mon 25/5/18	Sat 25/4/19	Mon 25/5/18	Sat 25/4/19	Mon 25/5/18	0	88FS-17 days	Mon 24/8/20
91	FT08 CHA300.75-CHA391.0	Tue 25/4/29	Tue 25/4/29	Tue 25/4/29	Tue 25/4/29	Tue 25/4/29	Tue 25/4/29	0	90FS-15 days	Mon 24/8/20
92	Temp. Drainage Diversion / Sheepsheeting	Mon 25/5/2	Mon 25/5/2	Mon 25/5/2	Mon 25/5/2	Mon 25/5/2	Mon 25/5/2	0	90FS-15 days	Mon 24/8/20
93	Excavation and Lateral Support	Fri 25/5/9	Mon 25/6/2	Fri 25/5/9	Mon 25/6/2	Fri 25/5/9	Mon 25/6/2	0	92FS-20 days	Mon 24/8/20
94	Ground and Edge Beams	Wed 25/6/13	Thu 25/6/13	Wed 25/6/13	Thu 25/6/13	Wed 25/6/13	Thu 25/6/13	0	92FS-20 days	Mon 24/8/20
95	Install precast portion (ground beam)	Sat 25/6/17	Sun 25/6/17	Sat 25/6/17	Sun 25/6/17	Sat 25/6/17	Sun 25/6/17	0	93FS-21 days	Mon 24/8/20
96	Rebar fixing	Tue 25/6/24	Tue 25/6/24	Tue 25/6/24	Tue 25/6/24	Tue 25/6/24	Tue 25/6/24	0	95FS-21 days	Mon 24/8/20
97	Formwork Erection and Cast-in Items	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	0	96FS-17 days	Mon 24/8/20
98	Concrete	1 day	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	0	97FS-17 days	Mon 24/8/20
99	Walls	Tue 25/6/10	Sat 25/7/12	Tue 25/6/10	Sat 25/7/12	Tue 25/6/10	Sat 25/7/12	0	97FS-17 days	Mon 24/8/20
100	Rebar fixing	Wed 25/6/18	Sat 25/7/12	Wed 25/6/18	Sat 25/7/12	Wed 25/6/18	Sat 25/7/12	0	98	Mon 24/8/20
101	Formwork Erection and Cast-in Items	Wed 25/6/18	Sat 25/7/12	Wed 25/6/18	Sat 25/7/12	Wed 25/6/18	Sat 25/7/12	0	100FS-17 days	Mon 24/8/20
102	Concrete	1 day	Thu 25/6/26	Thu 25/6/26	Thu 25/6/26	Thu 25/6/26	Thu 25/6/26	0	101FS-17 days	Mon 24/8/20
103	Backfilling and Compaction	Mon 25/7/21	Mon 25/7/21	Mon 25/7/21	Mon 25/7/21	Mon 25/7/21	Mon 25/7/21	0	102	Mon 24/8/20
104	Removal of Sheepsheets	Tue 25/7/29	Sat 25/7/15	Tue 25/7/29	Sat 25/7/15	Tue 25/7/29	Sat 25/7/15	0	103FS-17 days	Mon 24/8/20
105	Pedestrian Crossing no. 4	Sat 25/7/13	Sat 25/8/2	Sat 25/7/13	Sat 25/8/2	Sat 25/7/13	Sat 25/8/2	0	104FS-17 days	Mon 24/8/20
106	Demolition of existing crossing	Thu 25/8/15	Fri 25/8/15	Thu 25/8/15	Fri 25/8/15	Thu 25/8/15	Fri 25/8/15	0	105FS-17 days	Mon 24/8/20
107	FT01 CHA00.00-CHA100.00 (PC2)	Fri 25/10/24	Fri 25/10/24	Fri 25/10/24	Fri 25/10/24	Fri 25/10/24	Fri 25/10/24	0	106FS-20 days	Mon 24/8/20
108	Temp. Drainage Diversion / Sheepsheeting	Sun 25/7/27	Wed 25/8/20	Sun 25/7/27	Wed 25/8/20	Sun 25/7/27	Wed 25/8/20	0	106FS-20 days	Mon 24/8/20
109	Excavation and Lateral Support	Wed 25/8/6	Sat 25/8/30	Wed 25/8/6	Sat 25/8/30	Wed 25/8/6	Sat 25/8/30	0	108FS-15 days	Mon 24/8/20
110	Ground and Edge Beams	Mon 25/8/14	Mon 25/9/22	Mon 25/8/14	Mon 25/9/22	Mon 25/8/14	Mon 25/9/22	0	108FS-15 days	Mon 24/8/20
111	Install precast portion (ground beam)	Thu 25/8/14	Wed 25/9/10	Thu 25/8/14	Wed 25/9/10	Thu 25/8/14	Wed 25/9/10	0	109FS-17 days	Mon 24/8/20
112	Rebar fixing	Thu 25/8/14	Mon 25/9/14	Thu 25/8/14	Mon 25/9/14	Thu 25/8/14	Mon 25/9/14	0	109FS-17 days	Mon 24/8/20
113	Formwork Erection and Cast-in Items	Fri 25/8/29	Mon 25/9/22	Fri 25/8/29	Mon 25/9/22	Fri 25/8/29	Mon 25/9/22	0	112FS-17 days	Mon 24/8/20
114	Concrete	Sat 25/9/6	Sat 25/9/6	Sat 25/9/6	Sat 25/9/6	Sat 25/9/6	Sat 25/9/6	0	113FS-17 days	Mon 24/8/20
116	Rebar									

ID	Task Name	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRK	Predecessors
66	Excavation and Lateral Support	Fri 25/6/20	Fri 25/6/20	Fri 25/6/20	Fri 25/6/20	Fri 25/6/20	Fri 25/6/20	0 days	1	65FS-2 days
67	Drain Laying	Thu 25/6/25	Thu 25/6/25	Thu 25/6/25	Thu 25/6/25	Thu 25/6/25	Thu 25/6/25	0 days	0	66FS-2 days
68	Bedding and Backfilling	Tue 25/6/24	Sun 25/6/24	Tue 25/6/24	Sun 25/6/24	Tue 25/6/24	Sun 25/6/24	0 days	0	67FS-2 days
69	Manhole Construction	Fri 25/6/28	Fri 25/6/28	Fri 25/6/28	Fri 25/6/28	Fri 25/6/28	Fri 25/6/28	0 days	0	68FS-2 days
70	Reinstatement	Sat 25/7/5	Thu 25/7/10	Sat 25/7/5	Thu 25/7/10	Sat 25/7/5	Thu 25/7/10	0 days	0	69FS-2 days
71	T/A Removal	Fri 25/7/11	Fri 25/7/11	Fri 25/7/11	Fri 25/7/11	Fri 25/7/11	Fri 25/7/11	0 days	0	70FS-2 days
72	LFT-D2-LFT-D3,1650PC,B.L=39,D=3.34	Wed 25/7/12	Wed 25/7/12	Wed 25/7/12	Wed 25/7/12	Wed 25/7/12	Wed 25/7/12	0 days	0	71FS-2 days
73	T/A Implementation	Sat 25/7/13	Sat 25/7/13	Sat 25/7/13	Sat 25/7/13	Sat 25/7/13	Sat 25/7/13	0 days	0	72FS-2 days
74	Excavation and Lateral Support	Sat 25/7/12	Sun 25/7/12	Sat 25/7/12	Sun 25/7/12	Sat 25/7/12	Sun 25/7/12	0 days	0	73FS-2 days
75	Breaking Ground	Sat 25/7/12	Sun 25/7/12	Sat 25/7/12	Sun 25/7/12	Sat 25/7/12	Sun 25/7/12	0 days	0	74FS-2 days
76	Excavation and Lateral Support	Sat 25/7/12	Sun 25/7/12	Sat 25/7/12	Sun 25/7/12	Sat 25/7/12	Sun 25/7/12	0 days	0	75FS-2 days
77	Drain Laying	Mon 25/7/28	Tue 25/8/5	Mon 25/7/28	Tue 25/8/5	Mon 25/7/28	Tue 25/8/5	0 days	2	76FS-2 days
78	Bedding and Backfilling	Mon 25/8/4	Sun 25/8/10	Mon 25/8/4	Sun 25/8/10	Mon 25/8/4	Sun 25/8/10	0 days	2	77FS-2 days
79	Manhole Construction	Sat 25/8/9	Sun 25/8/17	Sat 25/8/9	Sun 25/8/17	Sat 25/8/9	Sun 25/8/17	0 days	2	78FS-2 days
80	Reinstatement	Mon 25/8/18	Sun 25/8/24	Mon 25/8/18	Sun 25/8/24	Mon 25/8/18	Sun 25/8/24	0 days	0	79FS-2 days
81	T/A Removal	Mon 25/8/25	Mon 25/8/26	Mon 25/8/25	Mon 25/8/26	Mon 25/8/25	Mon 25/8/26	0 days	0	80FS-2 days
82	Stage 2	Wed 25/8/27	Wed 25/10/1	Wed 25/8/27	Wed 25/10/1	Wed 25/8/27	Wed 25/10/1	0 days	0	81FS-2 days
83	T/A Implementation	Tue 25/8/27	Thu 25/8/28	Tue 25/8/27	Thu 25/8/28	Tue 25/8/27	Thu 25/8/28	0 days	0	82FS-2 days
84	Breaking Ground	Tue 25/8/27	Tue 25/9/2	Tue 25/8/27	Tue 25/9/2	Tue 25/8/27	Tue 25/9/2	0 days	0	83FS-2 days
85	Excavation and Lateral Support	Mon 25/9/1	Mon 25/9/9	Mon 25/9/1	Mon 25/9/9	Mon 25/9/1	Mon 25/9/9	0 days	0	84FS-2 days
86	Drain Laying	Mon 25/9/8	Sun 25/9/14	Mon 25/9/8	Sun 25/9/14	Mon 25/9/8	Sun 25/9/14	0 days	1	85FS-2 days
87	Bedding and Backfilling	Sat 25/9/13	Thu 25/9/18	Sat 25/9/13	Thu 25/9/18	Sat 25/9/13	Thu 25/9/18	0 days	1	86FS-2 days
88	Manhole Construction	Wed 25/9/17	Wed 25/9/24	Wed 25/9/17	Wed 25/9/24	Wed 25/9/17	Wed 25/9/24	0 days	1	87FS-2 days
89	Reinstatement	Thu 25/9/25	Thu 25/9/30	Thu 25/9/25	Thu 25/9/30	Thu 25/9/25	Thu 25/9/30	0 days	0	88FS-2 days
90	T/A Removal	Wed 25/10/1	Wed 25/10/1	Wed 25/10/1	Wed 25/10/1	Wed 25/10/1	Wed 25/10/1	0 days	0	89FS-2 days
91	LFT-D1B-LFT-D2,1650PC,B.L=45.56,D=3.34	Thu 25/10/2	Thu 25/10/2	Thu 25/10/2	Thu 25/10/2	Thu 25/10/2	Thu 25/10/2	0 days	0	90FS-2 days
92	Stage 1	Thu 25/10/2	Thu 25/10/2	Thu 25/10/2	Thu 25/10/2	Thu 25/10/2	Thu 25/10/2	0 days	0	91FS-2 days
93	T/A Implementation	Fri 25/10/3	Fri 25/10/3	Fri 25/10/3	Fri 25/10/3	Fri 25/10/3	Fri 25/10/3	0 days	0	92FS-2 days
94	Breaking Ground	Thu 25/10/2	Sat 25/10/11	Thu 25/10/2	Sat 25/10/11	Thu 25/10/2	Sat 25/10/11	0 days	2	93FS-2 days
95	Excavation and Lateral Support	Fri 25/10/20	Mon 25/10/20	Fri 25/10/20	Mon 25/10/20	Fri 25/10/20	Mon 25/10/20	0 days	2	94FS-2 days
96	Drain Laying	Tue 25/10/19	Tue 25/10/28	Tue 25/10/19	Tue 25/10/28	Tue 25/10/19	Tue 25/10/28	0 days	2	95FS-2 days
97	Bedding and Backfilling	Mon 25/10/27	Mon 25/11/3	Mon 25/10/27	Mon 25/11/3	Mon 25/10/27	Mon 25/11/3	0 days	0	96FS-2 days
98	Manhole Construction	Wed 25/11/12	Wed 25/11/12	Wed 25/11/12	Wed 25/11/12	Wed 25/11/12	Wed 25/11/12	0 days	2	97FS-2 days
99	Reinstatement	Wed 25/11/12	Wed 25/11/12	Wed 25/11/12	Wed 25/11/12	Wed 25/11/12	Wed 25/11/12	0 days	0	98FS-2 days
100	T/A Removal	Fri 25/11/20	Fri 25/11/20	Fri 25/11/20	Fri 25/11/20	Fri 25/11/20	Fri 25/11/20	0 days	0	99FS-2 days
101	Stage 2	Sat 25/11/22	Sat 25/11/22	Sat 25/11/22	Sat 25/11/22	Sat 25/11/22	Sat 25/11/22	0 days	0	100FS-2 days
102	T/A Implementation	Sun 25/11/23	Sun 25/11/23	Sun 25/11/23	Sun 25/11/23	Sun 25/11/23	Sun 25/11/23	0 days	0	101FS-2 days
103	Breaking Ground	Sat 25/11/22	Mon 25/12/1	Sat 25/11/22	Mon 25/12/1	Sat 25/11/22	Mon 25/12/1	0 days	2	102FS-2 days
104	Excavation and Lateral Support	Wed 25/12/10	Wed 25/12/10	Wed 25/12/10	Wed 25/12/10	Wed 25/12/10	Wed 25/12/10	0 days	2	103FS-2 days
105	Drain Laying	Thu 25/12/18	Thu 25/12/18	Thu 25/12/18	Thu 25/12/18	Thu 25/12/18	Thu 25/12/18	0 days	0	104FS-2 days
106	Bedding and Backfilling	Wed 25/12/17	Wed 25/12/17	Wed 25/12/17	Wed 25/12/17	Wed 25/12/17	Wed 25/12/17	0 days	0	105FS-2 days
107	Manhole Construction	Thu 25/12/23	Thu 25/12/23	Thu 25/12/23	Thu 25/12/23	Thu 25/12/23	Thu 25/12/23	0 days	2	106FS-2 days
108	Reinstatement	Fri 26/1/2	Fri 26/1/2	Fri 26/1/2	Fri 26/1/2	Fri 26/1/2	Fri 26/1/2	0 days	0	107FS-2 days
109	T/A Removal	Sat 26/1/10	Sat 26/1/10	Sat 26/1/10	Sat 26/1/10	Sat 26/1/10	Sat 26/1/10	0 days	0	108FS-2 days
110	LFT-D1A-LFT-D1B,1650PC,B.L=25.59,D=3.411	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	0 days	0	109FS-2 days
111	Stage 1	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	0 days	0	110FS-2 days
112	Breaking Ground	Sun 26/1/11	Sun 26/1/11	Sun 26/1/11	Sun 26/1/11	Sun 26/1/11	Sun 26/1/11	0 days	0	111FS-2 days
113	Excavation and Lateral Support	Sun 26/1/18	Tue 26/1/27	Sun 26/1/18	Tue 26/1/27	Sun 26/1/18	Tue 26/1/27	0 days	0	112FS-2 days
114	Drain Laying	Mon 26/1/26	Mon 26/1/26	Mon 26/1/26	Mon 26/1/26	Mon 26/1/26	Mon 26/1/26	0 days	2	113FS-2 days
115	Bedding and Backfilling	Sun 26/2/8	Sun 26/2/8	Sun 26/2/8	Sun 26/2/8	Sun 26/2/8	Sun 26/2/8	0 days	1	114FS-2 days
116	Manhole Construction	Mon 26/2/16	Mon 26/2/16	Mon 26/2/16	Mon 26/2/16	Mon 26/2/16	Mon 26/2/16	0 days	2	115FS-2 days
117	Reinstatement	Tue 26/2/24	Tue 26/2/24	Tue 26/2/24	Tue 26/2/24	Tue 26/2/24	Tue 26/2/24	0 days	1	116FS-2 days
118	T/A Removal	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	Wed 26/2/25	0 days	0	117FS-2 days
119	LFT-D1-LFT-D1A,1650PC,B.L=5.65,D=3.411	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	0 days	0	118FS-2 days
120	Stage 2	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	0 days	0	119FS-2 days
121	Breaking Ground	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	0 days	0	120FS-2 days
122	Excavation and Lateral Support	Mon 26/3/9	Mon 26/3/9	Mon 26/3/9	Mon 26/3/9	Mon 26/3/9	Mon 26/3/9	0 days	1	121FS-2 days
123	Drain Laying	Sun 26/3/14	Sun 26/3/14	Sun 26/3/14	Sun 26/3/14	Sun 26/3/14	Sun 26/3/14	0 days	1	122FS-2 days
124	Bedding and Backfilling	Mon 26/3/16	Mon 26/3/16	Mon 26/3/16	Mon 26/3/16	Mon 26/3/16	Mon 26/3/16	0 days	0	123FS-2 days
125	Manhole Construction	Sat 26/3/21	Sun 26/3/21	Sat 26/3/21	Sun 26/3/21	Sat 26/3/21	Sun 26/3/21	0 days	0	124FS-2 days
126	Reinstatement	Sun 26/3/22	Sun 26/3/22	Sun 26/3/22	Sun 26/3/22	Sun 26/3/22	Sun 26/3/22	0 days	0	125FS-2 days
127	T/A Removal	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	Thu 26/3/26	0 days	4	126FS-2 days
128	CCTV Inspection and T&C	Fri 26/4/9	Fri 26/4/9	Fri 26/4/9	Fri 26/4/9	Fri 26/4/9	Fri 26/4/9	0 days	4	127FS-2 days
129	Final Reinstatement	Thu 26/4/23	Thu 26/4/23	Thu 26/4/23	Thu 26/4/23	Thu 26/4/23	Thu 26/4/23	0 days	4	128FS-2 days
111	Section IV	Tue 23/5/30	Thu 26/8/6	Tue 23/5/30	Thu 26/8/6	Tue 23/5/30	Thu 26/8/6	0 days	0	129FS-2 days
112	access date of Portion D	Mon 23/1/25	Mon 23/1/25	Mon 23/1/25	Mon 23/1/25	Mon 23/1/25	Mon 23/1/25	0 days	0	130FS-2 days
2	Planned Completion Day	Thu 26/8/6	Thu 26/8/6	Thu 26/8/6	Thu 26/8/6	Thu 26/8/6	Thu 26/8/6	0 days	0	131FS-2 days
3	section IV (Ha Ché)	Thu 26/5/28	Thu 26/5/28	Thu 26/5/28	Thu 26/5/28	Thu 26/5/28	Thu 26/5/28	0 days	0	132FS-2 days
4	105 days	Thu 26/5/29	Thu 26/5/29	Thu 26/5/29	Thu 26/5/29	Thu 26/5/29	Thu 26/5/29	0 days	0	133FS-2 days
5	Early access (portion)	Fri 23/10/20	Fri 23/10/20	Fri 23/10/20	Fri 23/10/20	Fri 23/10/20	Fri 23/10/20	0 days	0	134FS-2 days
6	Access to remaining STLA	Mon 23/12/25	Mon 23/12/25	Mon 23/12/25	Mon 23/12/25	Mon 23/12/25	Mon 23/12/25	0 days	0	135FS-2 days
7	Private Land Leasing	Sat 23/12/23	Sat 23/12/23	Sat 23/12/23	Sat 23/12/23	Sat 23/12/23	Sat 23/12/23	0 days	0	136FS-2 days
8	Site Establishment	Tue 23/9/12	Tue 26/1/27	Tue 23/9/12	Tue 26/1/27	Tue 23/9/12	Tue 26/1/27	18 days	0	137FS-2 days
9	Prepare and Accept Temp. Works Design and Method Statement	Tue 23/9/12	Tue 26/1/27	Tue 23/9/12	Tue 26/1/27	Tue 23/9/12	Tue 26/1/27	18 days	0	138FS-2 days
10	Public Liaison and Negotiation with Village Rep. [A]	Mon 23/10/16	Mon 23/10/16	Mon 23/10/16	Mon 23/10/16	Mon 23/10/16	Mon 23/10/16	15 days	0	139FS-2 days
11	Initial Survey [A]	Fri 23/10/20	Tue 26/1/27	Fri 23/10/20	Tue 26/1/27	Fri 23/10/20	Tue 26/1/27	15 days	0	140FS-2 days
13	Initial Safety & Environmental measures [A]	Fri 23/10/20	Wed 23/11/8	Fri 23/10/20	Wed 23/11/8	Fri 23/10/20	Wed 23/11/8	15 days	0	141FS-2 days
15	EIA/Co Commencement of Construction [A]	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	Wed 24/2/21	0 days	0	142FS-2 days
17	Environmental Baseline Monitoring [A]	Tue 24/1/23	Tue 24/2/20	Tue 24/1/23	Tue 24/2/20	Tue 24/1/23	Tue 24/2/20	898 days	0	143FS-2 days
18	Freshwater Carv Translocation Plan [A]	Mon 24/1/22	Mon 24/1/22	Mon 24/1/22	Mon 24/1/22	Mon 24/1/22	Mon 24/1/22	928 days	0	144FS-2 days
19	Condition Survey & Str. Assessment (Shui Kan Shek, Fu Hing Garden, Twin 150k	Thu 23/11/9	Thu 24/1/17	Thu 23/11/9	Thu 24/1/17	Thu 23/11/9	Thu 24/1/17	577 days	0	145FS-2 days
20	UI detection [A]	Thu 23/11/9	Tue 23/11/28	Thu 23/11/9	Tue 23/11/28	Thu 23/11/9	Tue 23/11/28	65 days	0	146FS-2 days

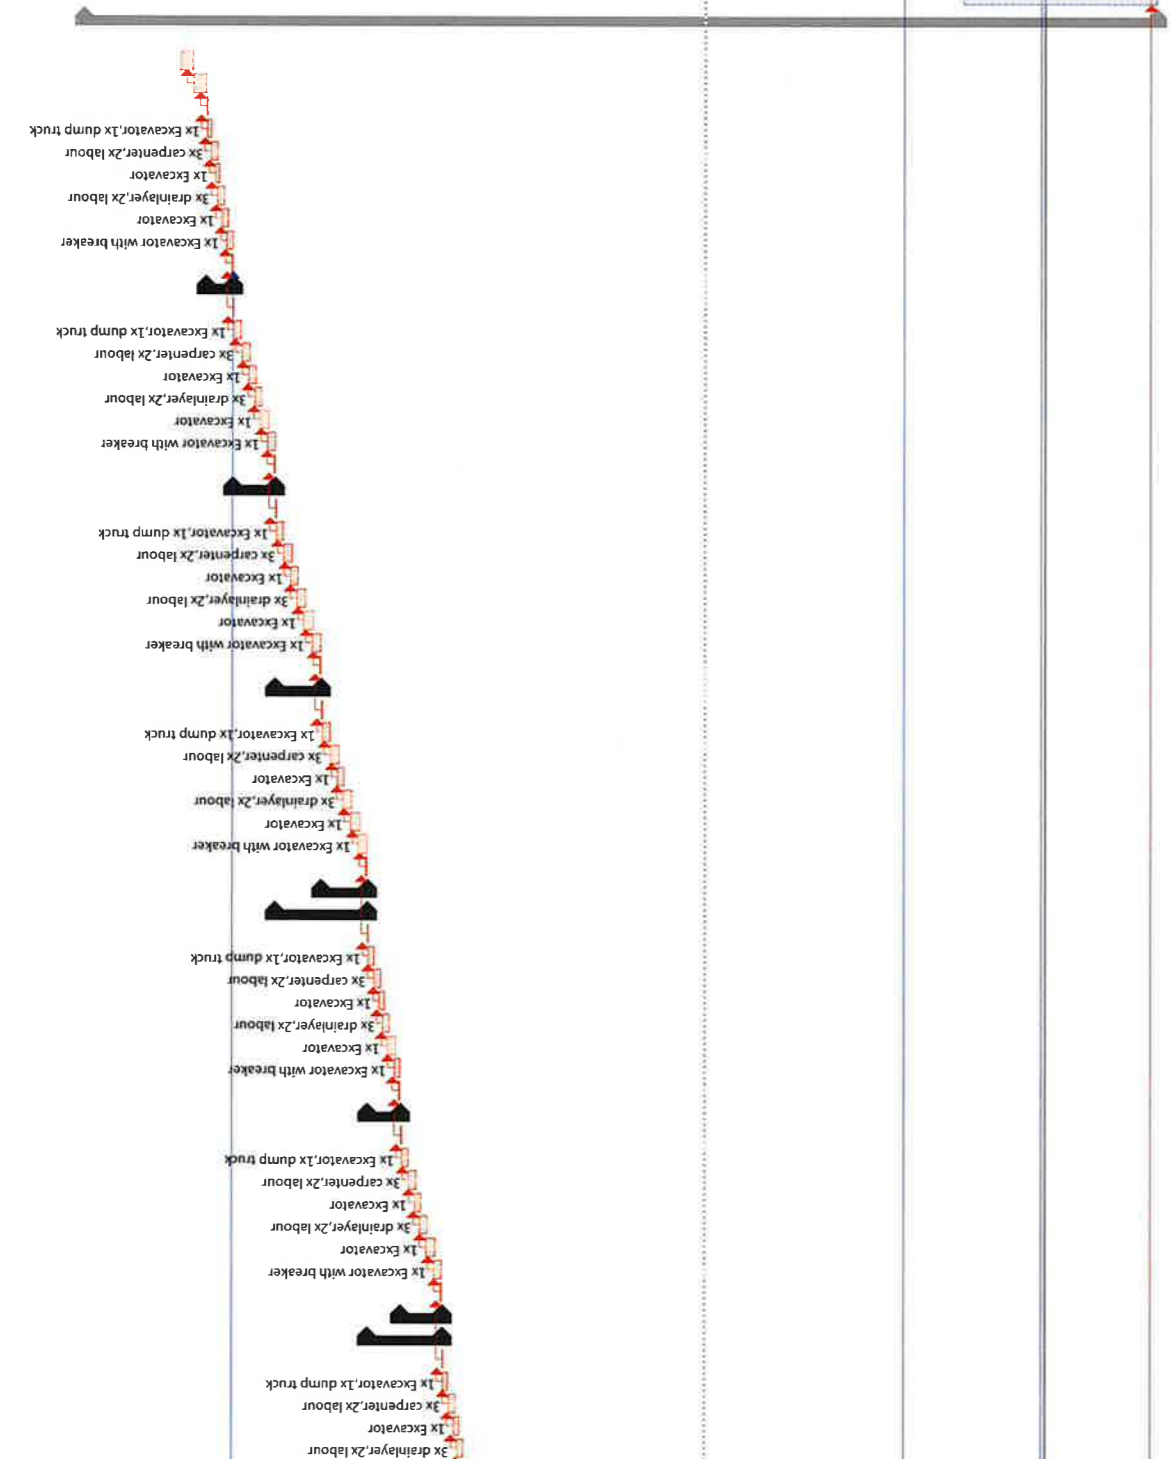


Task	Progress	Summary	Rollled Up Task	
------	----------	---------	-----------------	--

ID	Task Name	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	Predecessors
102	Concreting	1d	Tue 25/2/24	Mon 25/2/24	Tue 25/2/24	Mon 25/2/24	Tue 25/2/24	Mon 25/2/24	0 days	101
103	Backfilling and Compaction	30 days	Tue 25/2/25	Wed 25/2/26	Tue 25/2/25	Wed 25/2/26	Tue 25/2/25	Wed 25/2/26	0 days	102
104	Removal of Sheelies	30 days	Fri 25/3/7	Sat 25/4/5	Fri 25/3/7	Sat 25/4/5	Fri 25/3/7	Sat 25/4/5	0 days	103
105	Temp support to 3x ex Cabie bridge	60 days	Mon 25/3/17	Thu 26/6/6	Mon 25/3/17	Thu 26/6/6	Mon 25/3/17	Thu 26/6/6	4d8	104
106	Demolish & relocate porch YLL797/34,37	20 days	Mon 25/3/17	Sat 25/4/5	Mon 25/3/17	Sat 25/4/5	Mon 25/3/17	Sat 25/4/5	0 days	105
107	Demolish & relocate car body YLL797/36	20 days	Mon 25/3/17	Sat 25/4/5	Mon 25/3/17	Sat 25/4/5	Mon 25/3/17	Sat 25/4/5	0 days	106
108	Demolish & relocate godown YLL797/35	187 days	Mon 25/3/17	Wed 25/9/24	Mon 25/3/17	Wed 25/9/24	Mon 25/3/17	Wed 25/9/24	0 days	107
109	HC07 CHA400.00-CH.A500.00	20 days	Mon 25/3/17	Sat 25/4/5	Mon 25/3/17	Sat 25/4/5	Mon 25/3/17	Sat 25/4/5	0 days	108
110	Sheepiling & Temp. Drainage Diversion	35 days	Sat 25/3/22	Fri 25/4/25	Sat 25/3/22	Fri 25/4/25	Sat 25/3/22	Fri 25/4/25	0 days	109
111	Excavation and Lateral Support	35 days	Tue 25/4/8	Mon 25/5/12	Tue 25/4/8	Mon 25/5/12	Tue 25/4/8	Mon 25/5/12	0 days	110
112	Ground and Edge Beams	69 days	Wed 25/4/25	Fri 25/4/25	Wed 25/4/25	Fri 25/4/25	Wed 25/4/25	Fri 25/4/25	0 days	111
113	Initial precast portion	40 days	Tue 25/4/25	Tue 25/6/3	Tue 25/4/25	Tue 25/6/3	Tue 25/4/25	Tue 25/6/3	0 days	112
114	Rebar Fixing	35 days	Mon 25/5/12	Mon 25/6/15	Mon 25/5/12	Mon 25/6/15	Mon 25/5/12	Mon 25/6/15	0 days	113
115	Formwork Erection and Cast-in-items	35 days	Wed 25/5/29	Wed 25/7/2	Wed 25/5/29	Wed 25/7/2	Wed 25/5/29	Wed 25/7/2	0 days	114
116	Concreting	1d	Sat 25/6/15	Sat 25/6/28	Sat 25/6/15	Sat 25/6/28	Sat 25/6/15	Sat 25/6/28	0 days	115
117	Walls	52 days	Sun 25/6/29	Sun 25/8/19	Sun 25/6/29	Sun 25/8/19	Sun 25/6/29	Sun 25/8/19	0 days	116
118	Rebar Fixing	35 days	Sat 25/6/29	Sat 25/8/2	Sat 25/6/29	Sat 25/8/2	Sat 25/6/29	Sat 25/8/2	0 days	117
119	Formwork Erection and Cast-in-items	35 days	Wed 25/7/16	Tue 25/8/19	Wed 25/7/16	Tue 25/8/19	Wed 25/7/16	Tue 25/8/19	0 days	118
120	Concreting	1d	Sat 25/8/15	Fri 25/8/15	Sat 25/8/15	Fri 25/8/15	Sat 25/8/15	Fri 25/8/15	0 days	119
121	Backfilling and Compaction	30 days	Sun 25/8/16	Sat 25/8/15	Sun 25/8/16	Sat 25/8/15	Sun 25/8/16	Sat 25/8/15	0 days	120
122	Removal of Sheelies	30 days	Tue 25/8/26	Tue 25/9/24	Tue 25/8/26	Tue 25/9/24	Tue 25/8/26	Tue 25/9/24	0 days	121
123	Demolish & relocate porch, hoarding YLL797/44	20 days	Wed 25/9/24	Fri 25/9/24	Wed 25/9/24	Fri 25/9/24	Wed 25/9/24	Fri 25/9/24	0 days	122
124	Demolish & relocate porch YLL797/38,39	20 days	Wed 25/9/24	Fri 25/9/24	Wed 25/9/24	Fri 25/9/24	Wed 25/9/24	Fri 25/9/24	0 days	123
125	HC08 CH.A500.00-CH.A546.816	170 days	Wed 25/9/10	Thu 26/2/26	Wed 25/9/10	Thu 26/2/26	Wed 25/9/10	Thu 26/2/26	0 days	124
126	Sheepiling & Temp. Drainage Diversion	30 days	Wed 25/9/10	Thu 25/10/9	Wed 25/9/10	Thu 25/10/9	Wed 25/9/10	Thu 25/10/9	0 days	125
127	Excavation and Lateral Support	30 days	Fri 25/10/24	Fri 25/10/24	Fri 25/10/24	Fri 25/10/24	Fri 25/10/24	Fri 25/10/24	0 days	126
128	Ground and Edge Beams	65 days	Fri 25/10/10	Fri 25/12/13	Fri 25/10/10	Fri 25/12/13	Fri 25/10/10	Fri 25/12/13	0 days	127
129	Initial precast portion	40 days	Tue 25/11/18	Tue 25/11/18	Tue 25/11/18	Tue 25/11/18	Tue 25/11/18	Tue 25/11/18	0 days	128
130	Rebar Fixing	30 days	Fri 25/11/28	Thu 25/11/28	Fri 25/11/28	Thu 25/11/28	Fri 25/11/28	Thu 25/11/28	0 days	129
131	Formwork Erection and Cast-in-items	30 days	Fri 25/12/13	Fri 25/12/13	Fri 25/12/13	Fri 25/12/13	Fri 25/12/13	Fri 25/12/13	0 days	130
132	Concreting	10 days	Mon 25/12/8	Sat 25/12/8	Mon 25/12/8	Sat 25/12/8	Mon 25/12/8	Sat 25/12/8	0 days	131
133	Walls	45 days	Tue 25/12/9	Thu 26/1/22	Tue 25/12/9	Thu 26/1/22	Tue 25/12/9	Thu 26/1/22	0 days	132
134	Rebar Fixing	30 days	Wed 26/1/7	Tue 25/12/9	Wed 26/1/7	Tue 25/12/9	Wed 26/1/7	Tue 25/12/9	0 days	133
135	Formwork Erection and Cast-in-items	30 days	Wed 26/1/24	Wed 26/1/24	Wed 26/1/24	Wed 26/1/24	Wed 26/1/24	Wed 26/1/24	0 days	134
136	Concreting	10 days	Sat 26/1/17	Sat 26/1/17	Sat 26/1/17	Sat 26/1/17	Sat 26/1/17	Sat 26/1/17	0 days	135
137	Backfilling and Compaction	30 days	Mon 26/1/18	Mon 26/1/18	Mon 26/1/18	Mon 26/1/18	Mon 26/1/18	Mon 26/1/18	0 days	136
138	Removal of Sheelies	30 days	Wed 26/1/26	Wed 26/1/26	Wed 26/1/26	Wed 26/1/26	Wed 26/1/26	Wed 26/1/26	0 days	137
139	Pedestrian & Vehicular Crossing no. 3 (Box Culvert no. 4)	60 days	Tue 26/4/7	Sat 26/2/27	Tue 26/4/7	Sat 26/2/27	Tue 26/4/7	Sat 26/2/27	121 days	138
140	Demolish & relocate hoarding, wall YLL797/40	20 days	Sat 26/2/27	Thu 26/2/26	Sat 26/2/27	Thu 26/2/26	Sat 26/2/27	Thu 26/2/26	0 days	139
141	Demolish & relocate storage YLL797/42	20 days	Sat 26/2/27	Thu 26/2/26	Sat 26/2/27	Thu 26/2/26	Sat 26/2/27	Thu 26/2/26	0 days	140
142	HC09 CH.A546.816-CH.A611.404	155 days	Thu 26/2/12	Thu 26/7/16	Thu 26/2/12	Thu 26/7/16	Thu 26/2/12	Thu 26/7/16	0 days	141
143	Sheepiling & Temp. Drainage Diversion	30 days	Thu 26/3/13	Thu 26/2/12	Thu 26/3/13	Thu 26/2/12	Thu 26/3/13	Thu 26/2/12	0 days	142
144	Excavation and Lateral Support	30 days	Sat 26/3/28	Fri 26/2/27	Sat 26/3/28	Fri 26/2/27	Sat 26/3/28	Fri 26/2/27	0 days	143
145	Base Slab	45 days	Mon 26/4/27	Sat 26/3/14	Mon 26/4/27	Sat 26/3/14	Mon 26/4/27	Sat 26/3/14	0 days	144
146	Rebar Fixing	30 days	Mon 26/4/27	Sat 26/3/14	Mon 26/4/27	Sat 26/3/14	Mon 26/4/27	Sat 26/3/14	0 days	145
147	Formwork Erection and Cast-in-items	30 days	Mon 26/4/27	Sat 26/3/14	Mon 26/4/27	Sat 26/3/14	Mon 26/4/27	Sat 26/3/14	0 days	146
148	Concreting	10 days	Wed 26/4/13	Wed 26/4/13	Wed 26/4/13	Wed 26/4/13	Wed 26/4/13	Wed 26/4/13	0 days	147
149	Walls and Roof Slab	45 days	Mon 26/4/23	Sat 26/4/23	Mon 26/4/23	Sat 26/4/23	Mon 26/4/23	Sat 26/4/23	0 days	148
150	Rebar Fixing	30 days	Thu 26/4/23	Fri 26/5/22	Thu 26/4/23	Fri 26/5/22	Thu 26/4/23	Fri 26/5/22	0 days	149
151	Formwork Erection and Cast-in-items	30 days	Sat 26/5/8	Fri 26/5/8	Sat 26/5/8	Fri 26/5/8	Sat 26/5/8	Fri 26/5/8	0 days	150
152	Concreting	10 days	Sat 26/5/23	Mon 26/6/1	Sat 26/5/23	Mon 26/6/1	Sat 26/5/23	Mon 26/6/1	0 days	151
153	Backfilling and Compaction	30 days	Tue 26/6/2	Wed 26/7/1	Tue 26/6/2	Wed 26/7/1	Tue 26/6/2	Wed 26/7/1	0 days	152
154	Removal of Sheelies	30 days	Wed 26/6/17	Thu 26/7/16	Wed 26/6/17	Thu 26/7/16	Wed 26/6/17	Thu 26/7/16	0 days	153
155	Facing stone	21 days	Fri 26/7/17	Thu 26/8/6	Fri 26/7/17	Thu 26/8/6	Fri 26/7/17	Thu 26/8/6	0 days	154
156	ABWF works	21 days	Thu 26/8/6	Fri 26/7/17	Thu 26/8/6	Fri 26/7/17	Thu 26/8/6	Fri 26/7/17	0 days	155
157	Bedding works	21 days	Thu 26/8/6	Fri 26/7/17	Thu 26/8/6	Fri 26/7/17	Thu 26/8/6	Fri 26/7/17	0 days	156
158	Drainage Channel Works (West)	637 days	Fri 24/11/8	Thu 26/8/6	Fri 24/11/8	Thu 26/8/6	Fri 24/11/8	Thu 26/8/6	577 days	157
159	HC11 CH.A674.13-CH.A740.619 (ex CH Str. Assessment)	60 days	Mon 25/7/16	Mon 25/11/8	Mon 25/7/16	Mon 25/11/8	Mon 25/7/16	Mon 25/11/8	0 days	158
160	Demolish ex Geotechnical feature 6NE-B/R19	25 days	Mon 25/7/21	Thu 25/8/14	Mon 25/7/21	Thu 25/8/14	Mon 25/7/21	Thu 25/8/14	0 days	159
161	Demolish & relocate boundary wall, platform, gate YLL797/46	25 days	Mon 25/7/21	Thu 25/8/14	Mon 25/7/21	Thu 25/8/14	Mon 25/7/21	Thu 25/8/14	0 days	160
162	HC12 CH.A740.619-CH.A863.619	221 days	Thu 25/7/31	Thu 25/7/31	Thu 25/7/31	Thu 25/7/31	Thu 25/7/31	Thu 25/7/31	0 days	161
163	Excavation and Lateral Support	50 days	Mon 25/8/25	Mon 25/10/13	Mon 25/8/25	Mon 25/10/13	Mon 25/8/25	Mon 25/10/13	0 days	162
164	Ground and Edge Beams	77 days	Fri 25/9/19	Fri 25/12/4	Fri 25/9/19	Fri 25/12/4	Fri 25/9/19	Fri 25/12/4	0 days	163
165	Excavation and Lateral Support	50 days	Mon 25/9/18	Thu 25/9/18	Mon 25/9/18	Thu 25/9/18	Mon 25/9/18	Thu 25/9/18	0 days	164
166	Initial precast portion	50 days	Fri 25/9/19	Fri 25/11/7	Fri 25/9/19	Fri 25/11/7	Fri 25/9/19	Fri 25/11/7	0 days	165
167	Rebar Fixing	35 days	Mon 25/10/14	Mon 25/11/17	Mon 25/10/14	Mon 25/11/17	Mon 25/10/14	Mon 25/11/17	0 days	166
168	Formwork Erection and Cast-in-items	35 days	Mon 25/11/17	Mon 25/11/17	Mon 25/11/17	Mon 25/11/17	Mon 25/11/17	Mon 25/11/17	0 days	167
169	Formwork Erection and Cast-in-items	35 days	Thu 25/12/4	Fri 25/12/4	Thu 25/12/4	Fri 25/12/4	Thu 25/12/4	Fri 25/12/4	0 days	168
170	Concreting	1d	Mon 25/12/1	Mon 25/12/1	Mon 25/12/1	Mon 25/12/1	Mon 25/12/1	Mon 25/12/1	0 days	169
171	Walls	52 days	Wed 26/1/21	Mon 25/12/1	Wed 26/1/21	Mon 25/12/1	Wed 26/1/21	Mon 25/12/1	0 days	170
172	Rebar Fixing	35 days	Thu 25/12/18	Wed 26/1/18	Thu 25/12/18	Wed 26/1/18	Thu 25/12/18	Wed 26/1/18	0 days	171
173	Formwork Erection and Cast-in-items	35 days	Wed 26/1/21	Sat 26/1/21	Wed 26/1/21	Sat 26/1/21	Wed 26/1/21	Sat 26/1/21	0 days	172
174	Concreting	1d	Sun 26/1/14	Sat 26/1/14	Sun 26/1/14	Sat 26/1/14	Sun 26/1/14	Sat 26/1/14	0 days	173
175	Backfilling and Compaction	30 days	Mon 26/1/18	Mon 26/1/18	Mon 26/1/18	Mon 26/1/18	Mon 26/1/18	Mon 26/1/18	0 days	174
176	Removal of Sheelies	30 days	Wed 26/1/26	Thu 26/1/26	Wed 26/1/26	Thu 26/1/26	Wed 26/1/26	Thu 26/1/26	0 days	175
177	HC13 CH.A863.619-CH.A905.630	180 days	Sat 26/2/7	Wed 26/8/5	Sat 26/2/7	Wed 26/8/5	Sat 26/2/7	Wed 26/8/5	0 days	176
178	Sheepiling & Temp. Drainage Diversion	50 days	Wed 26/3/4	Wed 26/3/4	Wed 26/3/4	Wed 26/3/4	Wed 26/3/4	Wed 26/3/4	0 days	177
179	Excavation and Lateral Support	50 days	Wed 26/3/4	Wed 26/3/4	Wed 26/3/4	Wed 26/3/4	Wed 26/3/4	Wed 26/3/4	0 days	178
180	Ground and Edge Beams	65 days	Mon 26/3/29	Mon 26/6/1	Mon 26/3/29	Mon 26/6/1	Mon 26/3/29	Mon 26/6/1	0 days	179
181	Initial precast portion	40 days	Thu 26/3/29	Thu 26/3/29	Thu 26/3/29	Thu 26/3/29	Thu 26/3/29	Thu 26/3/29	0 days	180
182	Rebar Fixing	30 days	Sat 26/4/18	Sun 26/5/17	Sat 26/4/18	Sun 26/5/17	Sat 26/4/18	Sun 26/5/17	0 days	181
183	Formwork Erection and Cast-in-items	30 days	Sun 26/5/3	Mon 26/6/1	Sun 26/5/3	Mon 26/6/1	Sun 26/5/3	Mon 26/6/1	0 days	182

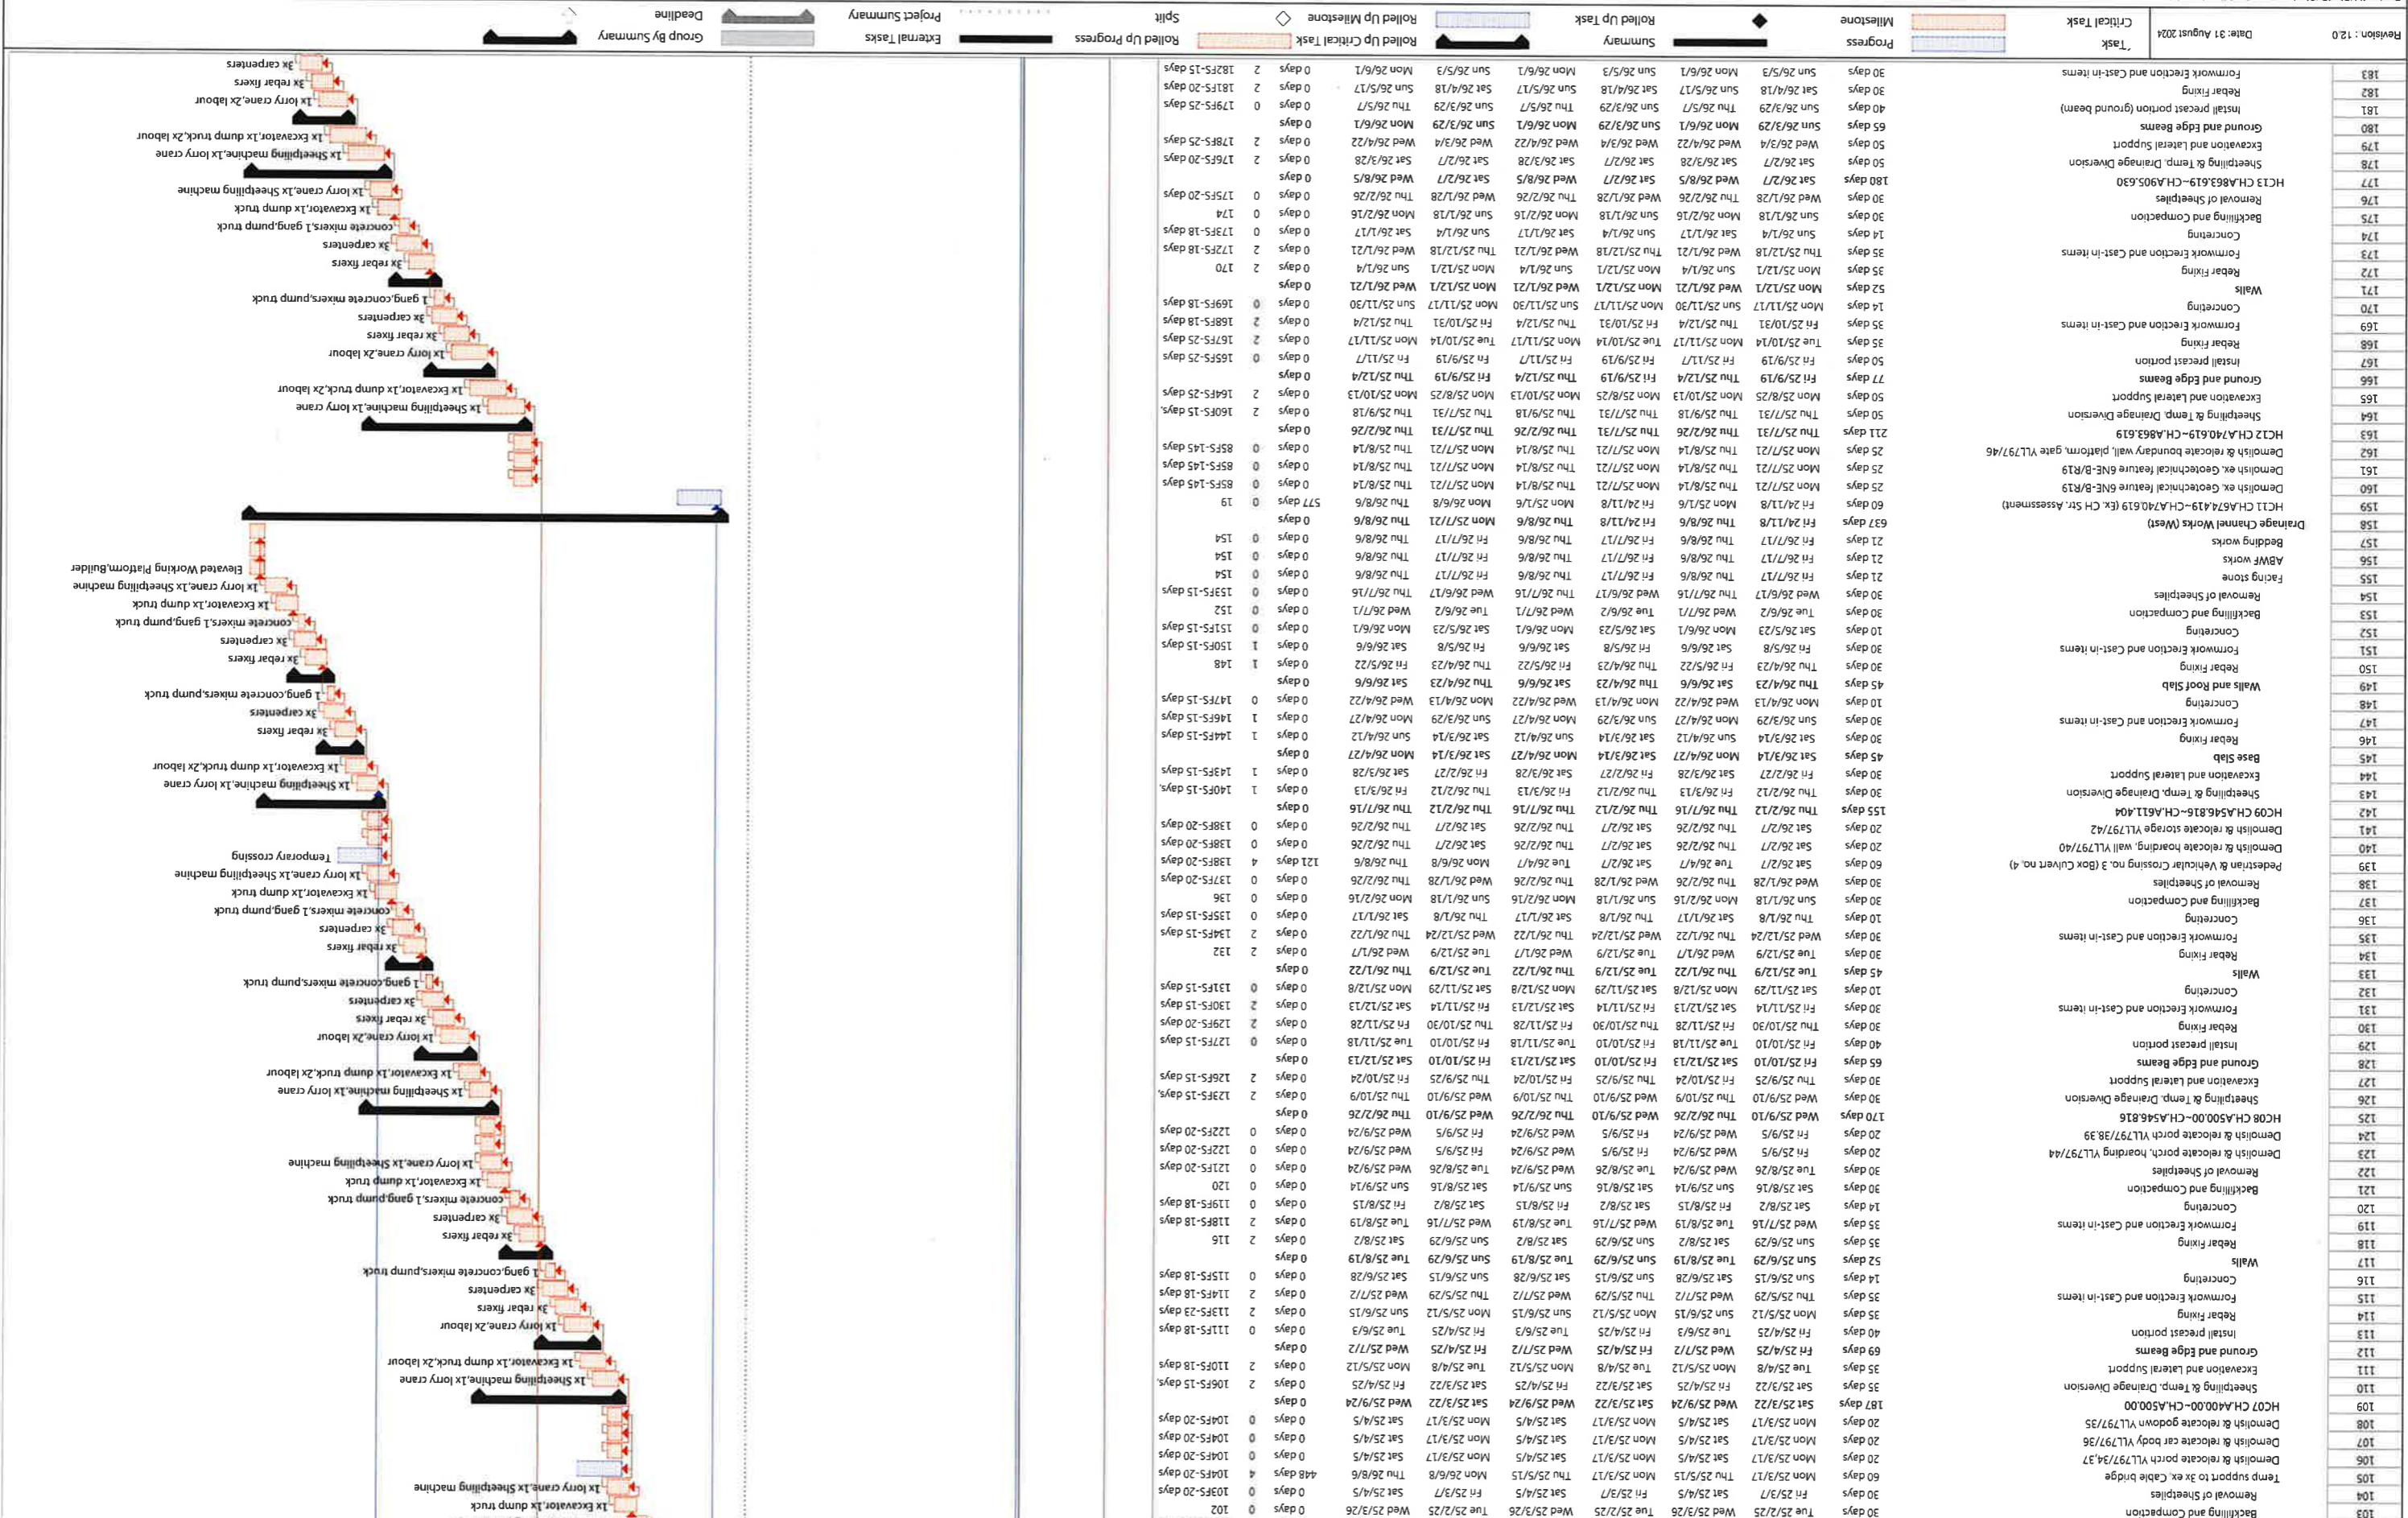


ID	Task Name	Duration	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TRA	Predecessors
----	-----------	----------	-------	--------	-------------	--------------	------------	-------------	-------------	-----	--------------


184	Concreting	10 days	Mon 26/5/18	Wed 26/5/27	Mon 26/5/18	Wed 26/5/27	Mon 26/5/18	Wed 26/5/27	0 days	0	183F5-15 days
185	Walls	30 days	Thu 26/5/28	Thu 26/6/16	Thu 26/5/28	Thu 26/6/16	Thu 26/5/28	Thu 26/6/16	0 days	2	184
186	Rebar Fixing	20 days	Thu 26/5/28	Thu 26/6/16	Thu 26/5/28	Thu 26/6/16	Thu 26/5/28	Thu 26/6/16	0 days	2	186F5-10 days
187	Formwork Erection and Cast-in Items	20 days	Thu 26/5/28	Thu 26/6/16	Thu 26/5/28	Thu 26/6/16	Thu 26/5/28	Thu 26/6/16	0 days	2	186F5-10 days
188	Formwork and Compaction	30 days	Sat 26/6/27	Sat 26/7/26	Sat 26/6/27	Sat 26/7/26	Sat 26/6/27	Sat 26/7/26	0 days	0	188
189	Backfilling and Compaction	30 days	Sat 26/6/27	Sat 26/7/26	Sat 26/6/27	Sat 26/7/26	Sat 26/6/27	Sat 26/7/26	0 days	0	189F5-20 days
190	Removal of Sheelies	30 days	Wed 26/7/7	Wed 26/8/5	Wed 26/7/7	Wed 26/8/5	Wed 26/7/7	Wed 26/8/5	0 days	0	189F5-20 days
191	Facing stone	21 days	Thu 26/7/17	Thu 26/8/6	Thu 26/7/17	Thu 26/8/6	Thu 26/7/17	Thu 26/8/6	0 days	0	190F5-20 days
192	ABWF works	21 days	Thu 26/7/17	Thu 26/8/6	Thu 26/7/17	Thu 26/8/6	Thu 26/7/17	Thu 26/8/6	0 days	0	190F5-20 days
193	Bedding works	21 days	Fri 26/7/17	Thu 26/8/6	Fri 26/7/17	Thu 26/8/6	Fri 26/7/17	Thu 26/8/6	0 days	0	190F5-20 days
113											
114	Section VII	820 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days	0	\\WingTatNac
3	access date of Portion D	820 days	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	Tue 23/5/30	0 days	0	\\WingTatNac
4	Site Establishment	389 days	Tue 23/9/12	Fri 24/10/4	Tue 23/9/12	Fri 24/10/4	Tue 23/9/12	Fri 24/10/4	10 days	0	\\WingTatNac
5	Public Liaison and Negotiation with Village Rep. [A]	104 days	Mon 23/12/25	Fri 24/10/4	Mon 23/12/25	Fri 24/10/4	Mon 23/12/25	Fri 24/10/4	10 days	0	\\WingTatNac
6	Initial Survey	95 days	Mon 23/12/25	Sun 24/3/24	Mon 23/12/25	Sun 24/3/24	Mon 23/12/25	Sun 24/3/24	874 days	0	2F5-1 days
8	Initial Safety & Environmental measures	281 days	Mon 23/12/25	Sun 24/3/24	Mon 23/12/25	Sun 24/3/24	Mon 23/12/25	Sun 24/3/24	874 days	0	2F5-1 days
9	Setup of instrumentation and monitoring	60 days	Mon 24/3/25	Thu 24/5/23	Mon 24/3/25	Thu 24/5/23	Mon 24/3/25	Thu 24/5/23	874 days	0	8
10	Tree Survey [A]	60 days	Mon 24/3/25	Thu 24/5/23	Mon 24/3/25	Thu 24/5/23	Mon 24/3/25	Thu 24/5/23	874 days	0	8
11	Condition Survey	60 days	Fri 24/5/24	Mon 24/7/22	Fri 24/5/24	Mon 24/7/22	Fri 24/5/24	Mon 24/7/22	934 days	0	910
12	UI detection	60 days	Mon 24/7/22	Thu 24/10/14	Mon 24/7/22	Thu 24/10/14	Mon 24/7/22	Thu 24/10/14	874 days	0	910
13	Site Clearance	60 days	Fri 24/9/20	Thu 24/10/14	Fri 24/9/20	Thu 24/10/14	Fri 24/9/20	Thu 24/10/14	874 days	0	12
14	Temporary Traffic Arrangement	281 days	Mon 24/9/30	#####	Mon 24/9/30	#####	Mon 24/9/30	#####	0 days	0	2F5-1 day
15	Application of XP [A]	251 days	Mon 23/12/25	Sat 24/8/31	Mon 23/12/25	Sat 24/8/31	Mon 23/12/25	Sat 24/8/31	0 days	0	2F5-1 day
16	Submission of TTA and Arrange TMLG [A]	251 days	Mon 23/12/25	Sat 24/8/31	Mon 23/12/25	Sat 24/8/31	Mon 23/12/25	Sat 24/8/31	0 days	0	2F5-1 day
17	Approval of TTA [A]	30 days	Sun 24/9/1	Mon 24/9/30	Sun 24/9/1	Mon 24/9/30	Sun 24/9/1	Mon 24/9/30	0 days	0	15.16
18	Drain Laying Works	684 days	Fri 23/10/13	Fri 23/10/13	Fri 23/10/13	Fri 23/10/13	Fri 23/10/13	Fri 23/10/13	0 days	0	0
19	[PMO22] Alternative methodology design for drainage channel underneath	324 days	Sat 24/8/31	Fri 23/10/13	Sat 24/8/31	Fri 23/10/13	Sat 24/8/31	Fri 23/10/13	0 days	0	0
20	Acceptance of alternative methodology and protection method to ex.	30 days	Mon 24/9/1	Mon 24/9/30	Mon 24/9/1	Mon 24/9/30	Mon 24/9/1	Mon 24/9/30	0 days	0	19
21	Protection to ex Dongjiang Water Main	14 days	Tue 24/10/14	Mon 24/10/14	Tue 24/10/14	Mon 24/10/14	Tue 24/10/14	Mon 24/10/14	0 days	0	17.20
22	HClO CH A611.404-CH A674.419 (Fan Kam Road)	286 days	Tue 24/10/15	Tue 24/10/15	Tue 24/10/15	Tue 24/10/15	Tue 24/10/15	Tue 24/10/15	0 days	0	0
23	N/B TTA Implementation	7 days	Tue 24/10/15	Mon 24/10/21	Tue 24/10/15	Mon 24/10/21	Tue 24/10/15	Mon 24/10/21	0 days	0	21.17.6
24	Sheet Piles Installation	15 days	Tue 24/10/22	Tue 24/10/22	Tue 24/10/22	Tue 24/10/22	Tue 24/10/22	Tue 24/10/22	0 days	0	23
25	Construction of top slab	32 days	Wed 24/11/6	Sat 24/12/7	Wed 24/11/6	Sat 24/12/7	Wed 24/11/6	Sat 24/12/7	0 days	0	24
26	Backfilling and reinstatement	15 days	Mon 24/12/30	Mon 25/1/13	Mon 24/12/30	Mon 25/1/13	Mon 24/12/30	Mon 25/1/13	0 days	0	27
27	S/B TTA Implementation	7 days	Mon 24/12/23	Mon 24/12/23	Mon 24/12/23	Mon 24/12/23	Mon 24/12/23	Mon 24/12/23	0 days	0	26
28	Sheet Piles Installation	15 days	Mon 24/12/30	Mon 25/1/13	Mon 24/12/30	Mon 25/1/13	Mon 24/12/30	Mon 25/1/13	0 days	0	27
29	Construction of top slab	32 days	Tue 25/1/14	Fri 25/2/14	Tue 25/1/14	Fri 25/2/14	Tue 25/1/14	Fri 25/2/14	0 days	0	28
30	Backfilling and reinstatement	15 days	Sat 25/2/15	Sat 25/2/15	Sat 25/2/15	Sat 25/2/15	Sat 25/2/15	Sat 25/2/15	0 days	0	29
31	Demolition of existing culvert & install temp. support	60 days	Sun 25/2/12	Wed 25/4/30	Sun 25/2/12	Wed 25/4/30	Sun 25/2/12	Wed 25/4/30	0 days	0	30
32	Construction of alternative box-culvert	60 days	Thu 25/5/1	Sun 25/6/29	Thu 25/5/1	Sun 25/6/29	Thu 25/5/1	Sun 25/6/29	0 days	0	31
33	Removal of temporary support	28 days	Mon 25/6/30	Mon 25/7/27	Mon 25/6/30	Mon 25/7/27	Mon 25/6/30	Mon 25/7/27	0 days	0	32
34	CCTV inspection and TRC	30 days	Mon 25/7/28	Mon 25/8/26	Mon 25/7/28	Mon 25/8/26	Mon 25/7/28	Mon 25/8/26	0 days	0	33
116	Section V	1045 days	Mon 23/5/29	Tue 26/4/7	Mon 23/5/29	Tue 26/4/7	Mon 23/5/29	Tue 26/4/7	1 day	0	\\WingTatNac
2	access date of Portion E1	0 days	Mon 23/5/29	Mon 26/1/26	Mon 23/5/29	Mon 26/1/26	Mon 23/5/29	Mon 26/1/26	15 days	0	\\WingTatNac
3	section V (Shan Ha Tsuen - Shan Ha Road)	973 days	Mon 23/5/30	Mon 26/1/26	Mon 23/5/30	Mon 26/1/26	Mon 23/5/30	Mon 26/1/26	0 days	0	\\WingTatNac
4	Planned Completion Day	70 days	Tue 26/1/27	Mon 26/4/6	Tue 26/1/27	Mon 26/4/6	Tue 26/1/27	Mon 26/4/6	0 days	0	3
5	Site Establishment	751 days	Mon 23/5/29	Wed 25/10/15	Mon 23/5/29	Wed 25/10/15	Mon 23/5/29	Wed 25/10/15	15 days	0	\\WingTatNac
6	Prepare and Accept Temp. Works Design and Method Statement [A]	751 days	Tue 23/9/26	Wed 25/10/15	Tue 23/9/26	Wed 25/10/15	Tue 23/9/26	Wed 25/10/15	15 days	0	\\WingTatNac
7	Public Liaison and Negotiation with Village Rep. [A]	104 days	Tue 23/9/12	Sun 23/12/24	Tue 23/9/12	Sun 23/12/24	Tue 23/9/12	Sun 23/12/24	27 days	0	\\WingTatNac
8	Initial Survey [A]	85 days	Mon 23/9/29	Mon 23/12/25	Mon 23/9/29	Mon 23/12/25	Mon 23/9/29	Mon 23/12/25	15 days	0	2F5-1 day
9	[EWN011] Objection and additional request of Village Rep.	85 days	Mon 23/12/25	Mon 24/3/18	Mon 23/12/25	Mon 24/3/18	Mon 23/12/25	Mon 24/3/18	27 days	0	7
10	[EWN011] Objection and additional request of Village Rep.	30 days	Wed 24/3/19	Tue 24/5/14	Wed 24/3/19	Tue 24/5/14	Wed 24/3/19	Tue 24/5/14	27 days	0	9
12	Initial Safety & Environmental measures [A]	30 days	Sun 24/3/31	Mon 24/4/29	Sun 24/3/31	Mon 24/4/29	Sun 24/3/31	Mon 24/4/29	15 days	0	17F
14	Setup of instrumentation and monitoring	45 days	Mon 24/3/16	Mon 24/4/29	Mon 24/3/16	Mon 24/4/29	Mon 24/3/16	Mon 24/4/29	15 days	0	17F
15	Tree Survey [A]	45 days	Sat 24/3/16	Mon 24/4/29	Sat 24/3/16	Mon 24/4/29	Sat 24/3/16	Mon 24/4/29	15 days	0	17F
16	UI detection [A]	30 days	Mon 24/3/31	Mon 24/4/29	Mon 24/3/31	Mon 24/4/29	Mon 24/3/31	Mon 24/4/29	15 days	0	17F
17	Site Clearance [A]	30 days	Mon 24/3/31	Mon 24/4/29	Mon 24/3/31	Mon 24/4/29	Mon 24/3/31	Mon 24/4/29	15 days	0	17F
18	Temporary Traffic Arrangement	337 days	Mon 23/5/29	Mon 24/4/29	Mon 23/5/29	Mon 24/4/29	Mon 23/5/29	Mon 24/4/29	15 days	0	2F5-1 day
19	Application of TTA [A]	307 days	Mon 23/5/29	Sat 24/3/30	Mon 23/5/29	Sat 24/3/30	Mon 23/5/29	Sat 24/3/30	15 days	0	2F5-1 day
20	Submission of TTA and Arrange TMLG [A]	307 days	Mon 23/5/29	Sat 24/3/30	Mon 23/5/29	Sat 24/3/30	Mon 23/5/29	Sat 24/3/30	15 days	0	2F5-1 day
21	Approval of TTA [A]	30 days	Sun 24/3/31	Mon 24/4/29	Sun 24/3/31	Mon 24/4/29	Sun 24/3/31	Mon 24/4/29	15 days	0	19.20.9
22	Drain Laying Works	692 days	Tue 24/3/30	Mon 24/3/22	Tue 24/3/30	Mon 24/3/22	Tue 24/3/30	Mon 24/3/22	15 days	0	19.20.9
23	SHT A3A-SHT A04.I500P.C.B.L=49.29.D=3.65	161 days	Tue 24/4/30	Mon 24/10/7	Tue 24/4/30	Mon 24/10/7	Tue 24/4/30	Mon 24/10/7	15 days	0	19.20.9
24	Stage 1	83 days	Sun 24/7/21	Sun 24/4/30	Sun 24/7/21	Sun 24/4/30	Sun 24/7/21	Sun 24/4/30	15 days	0	19.20.9
25	TTA Implementation (trial run) [A]	14 days	Tue 24/4/30	Mon 24/5/6	Tue 24/4/30	Mon 24/5/6	Tue 24/4/30	Mon 24/5/6	15 days	0	17.21.12.14.15.
26	Excavation and Lateral Support [A]	20 days	Fri 24/5/17	Fri 24/6/5	Fri 24/5/17	Fri 24/6/5	Fri 24/5/17	Fri 24/6/5	15 days	2	26F5-2 days
27	Excavation and Lateral Support [A]	20 days	Tue 24/6/4	Tue 24/6/23	Tue 24/6/4	Tue 24/6/23	Tue 24/6/4	Tue 24/6/23	15 days	2	26F5-2 days
28	Drain Laying [A]	18 days	Sat 24/6/22	Tue 24/7/9	Sat 24/6/22	Tue 24/7/9	Sat 24/6/22	Tue 24/7/9	15 days	0	26F5-2 days
29	Bedding and Backfilling [A]	12 days	Mon 24/7/8	Mon 24/7/19	Mon 24/7/8	Mon 24/7/19	Mon 24/7/8	Mon 24/7/19	15 days	0	26F5-2 days
30	RTA Renovation [A]	78 days	Mon 24/7/22	Mon 24/10/7	Mon 24/7/22	Mon 24/10/7	Mon 24/7/22	Mon 24/10/7	15 days	0	30
31	RTA Renovation [A]	78 days	Mon 24/7/22	Mon 24/10/7	Mon 24/7/22	Mon 24/10/7	Mon 24/7/22	Mon 24/10/7	15 days	0	30
32	Stage 2	78 days	Mon 24/7/22	Mon 24/10/7	Mon 24/7/22	Mon 24/10/7	Mon 24/7/22	Mon 24/10/7	15 days	0	30
33	TTA Implementation [A]	4 days	Mon 24/7/22	Thu 24/7/25	Mon 24/7/22	Thu 24/7/25	Mon 24/7/22	Thu 24/7/25	15 days	0	31
34	Excavation and Lateral Support [A]	14 days	Wed 24/7/24	Tue 24/8/6	Wed 24/7/24	Tue 24/8/6	Wed 24/7/24	Tue 24/8/6	15 days	1	33F5-2 days
35	Excavation and Lateral Support [A]	20 days	Mon 24/8/5	Sat 24/8/24	Mon 24/8/5	Sat 24/8/24	Mon 24/8/5	Sat 24/8/24	15 days	2	33F5-2 days
36	Drain Laying	20 days	Wed 24/8/23	Wed 24/9/11	Wed 24/8/23	Wed 24/9/11	Wed 24/8/23	Wed 24/9/11	15 days	2	33F5-2 days
37	Bedding and Backfilling	16 days	Tue 24/9/10	Wed 24/9/25	Tue 24/9/10	Wed 24/9/25	Tue 24/9/10	Wed 24/9/25	15 days	0	37F5-2 days
38	Reinstatement	12 days	Tue 24/9/24	Sat 24/10/5	Tue 24/9/24	Sat 24/10/5	Tue 24/9/24	Sat 24/10/5	15 days	0	37F5-2 days

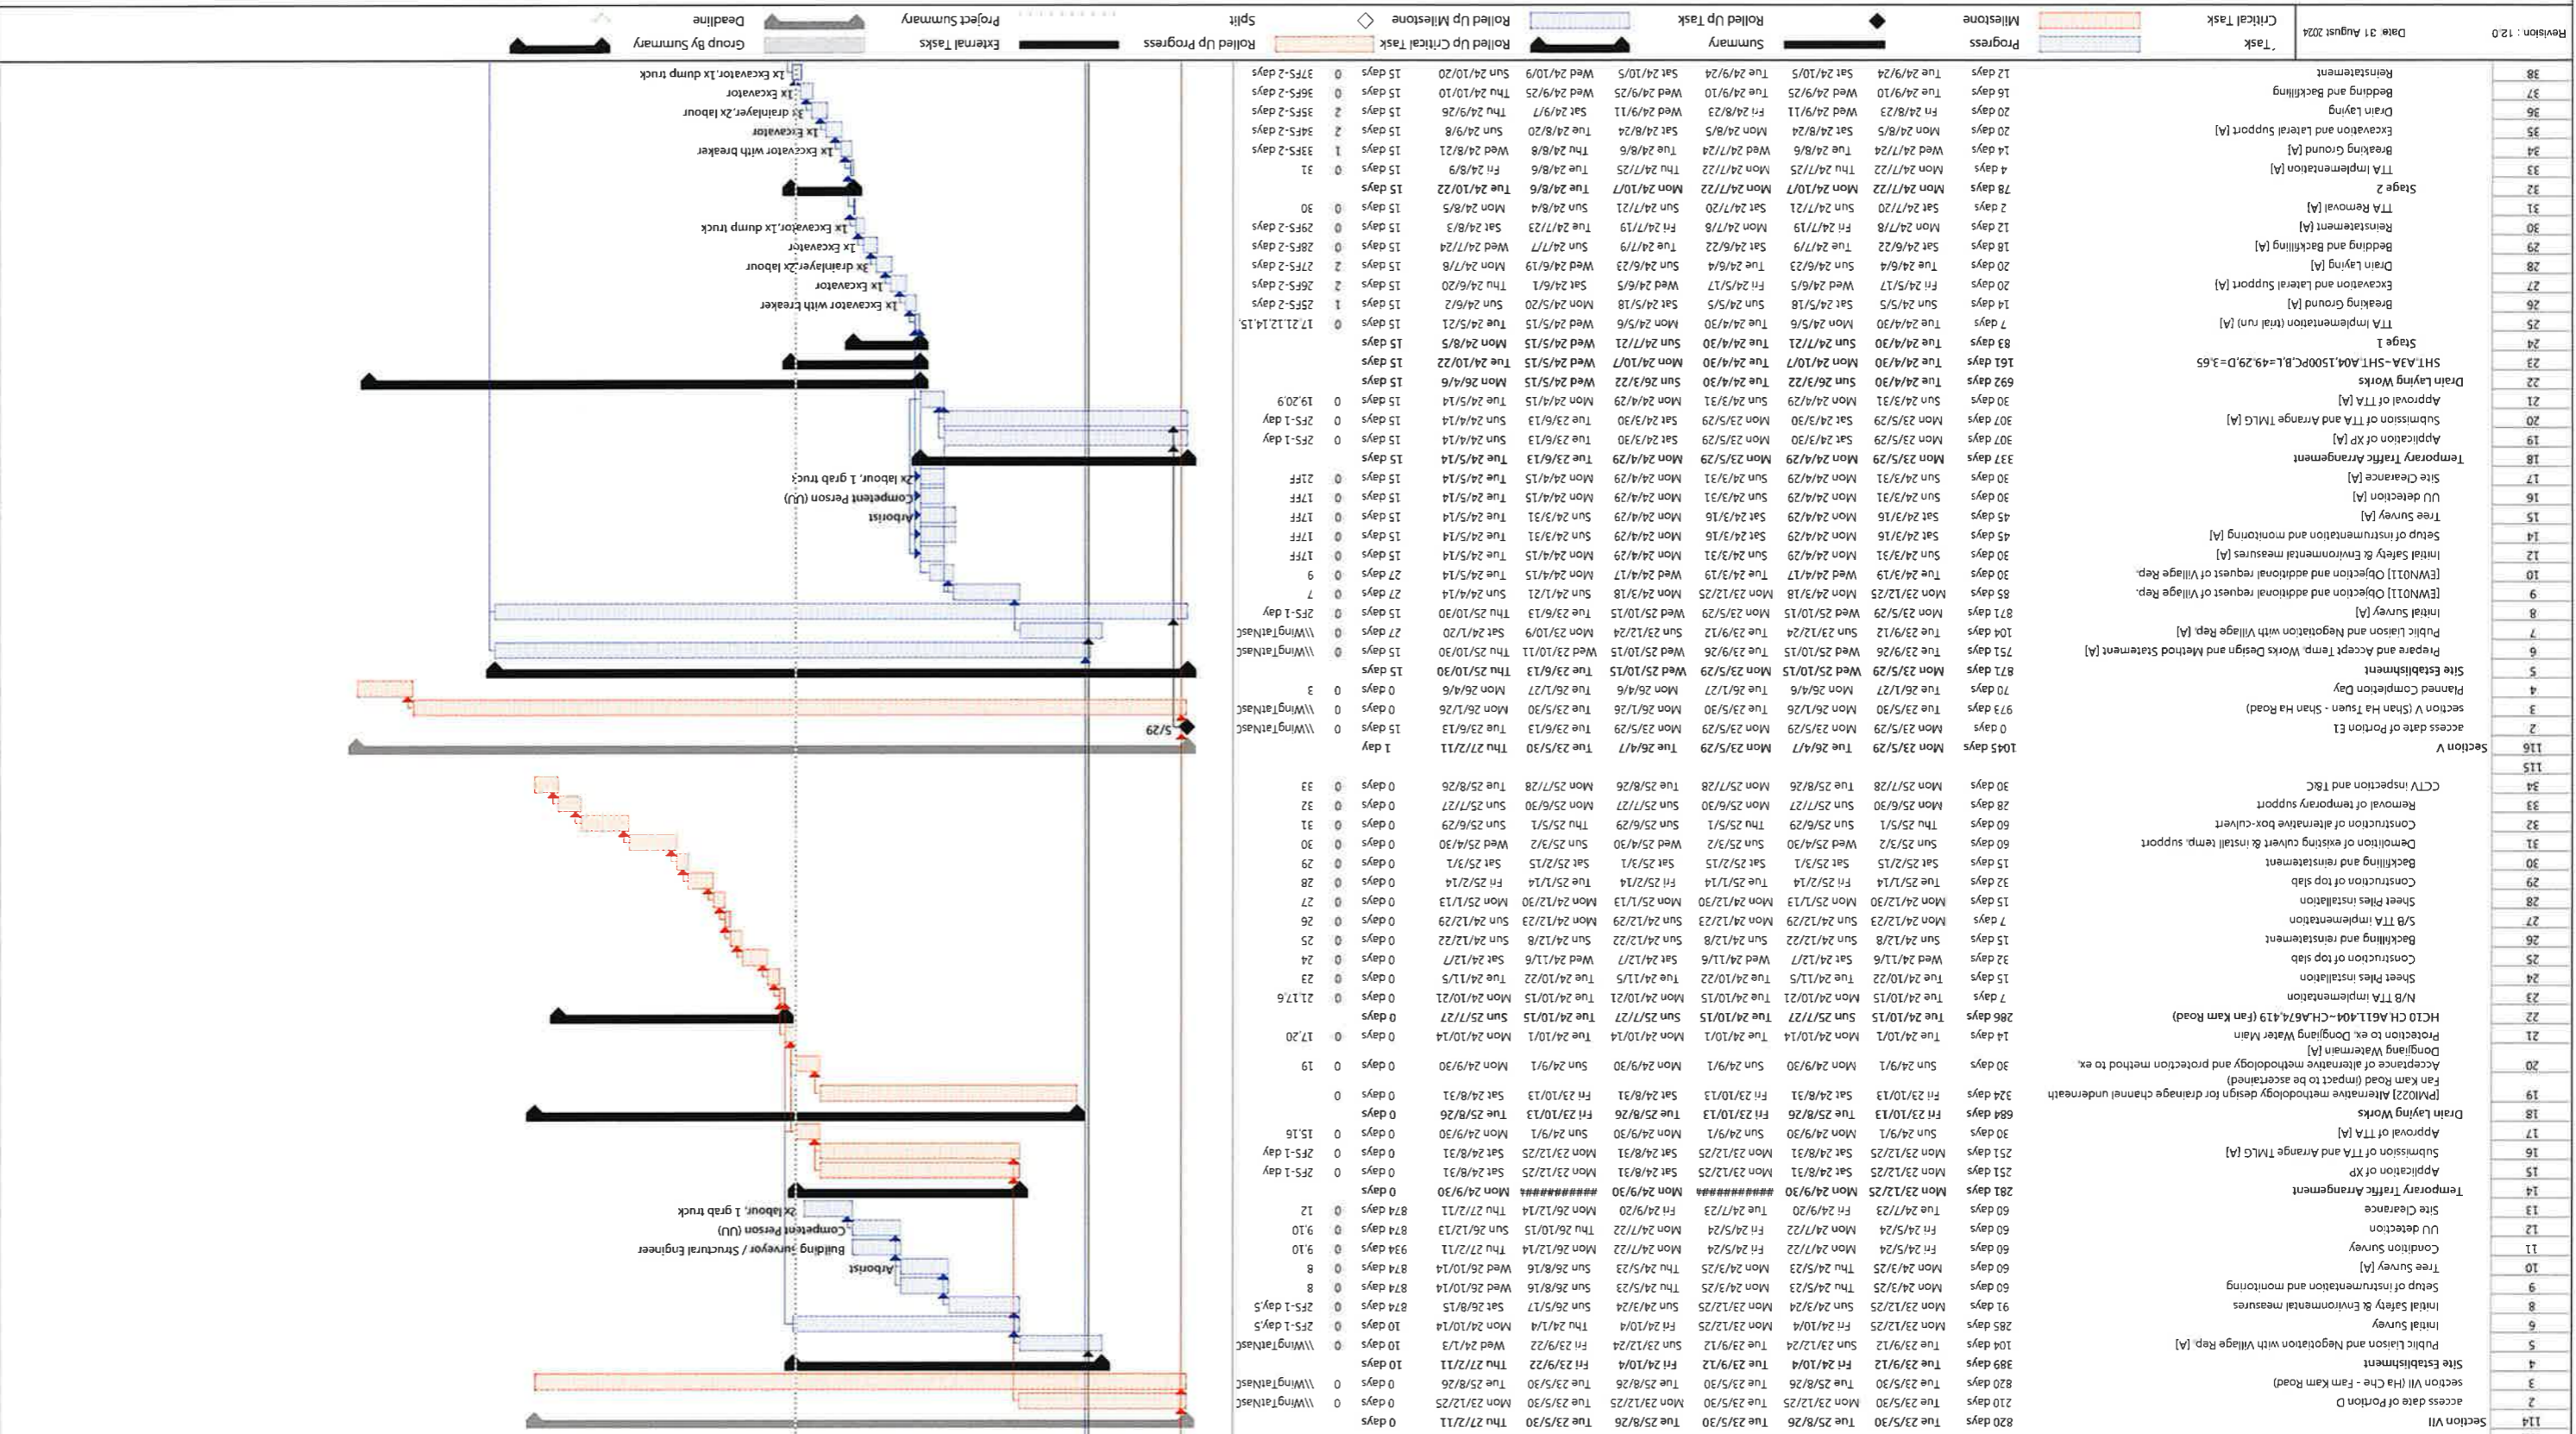

ID	Task Name	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	Predecessors
39	SHT A05-SHT A06A.1500PC.B.L=13.12.D=3.15 T1A Removal	Sun 24/10/6	Sun 24/10/6	Sun 24/10/6	Sun 24/10/6	Sun 24/10/6	Sun 24/10/6	0	38
40	SHT A05-SHT A06A.1500PC.B.L=13.12.D=3.15 T1A Implementation	Thu 24/10/8	Thu 24/12/12	Thu 24/10/8	Thu 24/12/12	Thu 24/10/8	Thu 24/12/12	15 days	39
41	T1A Implementation	Thu 24/10/8	Thu 24/10/11	Thu 24/10/8	Thu 24/10/11	Thu 24/10/8	Thu 24/10/11	3 days	39
42	Breaking Ground	Thu 24/10/10	Thu 24/10/10	Thu 24/10/10	Thu 24/10/10	Thu 24/10/10	Thu 24/10/10	0 days	41
43	Excavation and Lateral Support	Thu 24/10/22	Thu 24/11/6	Thu 24/10/22	Thu 24/11/6	Thu 24/10/22	Thu 24/11/6	15 days	41
44	Drain Laying	Thu 24/11/5	Mon 24/11/18	Thu 24/11/5	Mon 24/11/18	Thu 24/11/5	Mon 24/11/18	14 days	44
45	Bedding and Backfilling	Mon 24/11/7	Mon 24/11/24	Mon 24/11/7	Mon 24/11/24	Mon 24/11/7	Mon 24/11/24	17 days	45
46	Manhole Construction	Mon 24/11/23	Mon 24/12/2	Mon 24/11/23	Mon 24/12/2	Mon 24/11/23	Mon 24/12/2	10 days	46
47	Reinstatement	Thu 24/12/3	Thu 24/12/3	Thu 24/12/3	Thu 24/12/3	Thu 24/12/3	Thu 24/12/3	0 days	47
48	T1A Removal	Wed 24/12/11	Thu 24/12/11	Thu 24/12/11	Thu 24/12/11	Thu 24/12/11	Thu 24/12/11	2 days	48
49	SHT A03-SHT A03A.1500PC.B.L=8.59.D=3.65 T1A Implementation	Thu 24/12/15	Mon 24/12/15	Thu 24/12/15	Mon 24/12/15	Thu 24/12/15	Mon 24/12/15	14 days	49
50	T1A Implementation	Mon 24/12/13	Mon 24/12/13	Mon 24/12/13	Mon 24/12/13	Mon 24/12/13	Mon 24/12/13	0 days	50
51	Breaking Ground	Mon 24/12/16	Mon 24/12/16	Mon 24/12/16	Mon 24/12/16	Mon 24/12/16	Mon 24/12/16	0 days	48
52	Excavation and Lateral Support	Mon 24/12/28	Mon 25/1/12	Mon 24/12/28	Mon 25/1/12	Mon 24/12/28	Mon 25/1/12	15 days	51
53	Drain Laying	Mon 25/1/12	Mon 25/1/25	Mon 25/1/12	Mon 25/1/25	Mon 25/1/12	Mon 25/1/25	14 days	53
54	Bedding and Backfilling	Mon 25/1/24	Mon 25/2/2	Mon 25/1/24	Mon 25/2/2	Mon 25/1/24	Mon 25/2/2	10 days	54
55	Manhole Construction	Thu 25/2/20	Thu 25/2/20	Thu 25/2/20	Thu 25/2/20	Thu 25/2/20	Thu 25/2/20	0 days	55
56	Reinstatement	Mon 25/3/2	Mon 25/3/2	Mon 25/3/2	Mon 25/3/2	Mon 25/3/2	Mon 25/3/2	0 days	56
57	T1A Removal	Mon 25/3/3	Mon 25/3/3	Mon 25/3/3	Mon 25/3/3	Mon 25/3/3	Mon 25/3/3	0 days	57
58	SHT A02-SHT A03.1500PC.L1=32.82.D=3.6 T1A Implementation	Wed 25/3/5	Thu 25/6/19	Wed 25/3/5	Thu 25/6/19	Wed 25/3/5	Thu 25/6/19	107 days	58
59	T1A Implementation	Wed 25/3/5	Mon 25/4/28	Wed 25/3/5	Mon 25/4/28	Wed 25/3/5	Mon 25/4/28	55 days	59
60	Breaking Ground	Wed 25/3/5	Thu 25/3/8	Wed 25/3/5	Thu 25/3/8	Wed 25/3/5	Thu 25/3/8	4 days	60
61	Excavation and Lateral Support	Sun 25/3/16	Sun 25/3/16	Sun 25/3/16	Sun 25/3/16	Sun 25/3/16	Sun 25/3/16	0 days	61
62	Excavation and Lateral Support	Wed 25/3/26	Wed 25/3/26	Wed 25/3/26	Wed 25/3/26	Wed 25/3/26	Wed 25/3/26	0 days	62
63	Drain Laying	Thu 25/4/4	Thu 25/4/4	Thu 25/4/4	Thu 25/4/4	Thu 25/4/4	Thu 25/4/4	0 days	63
64	Bedding and Backfilling	Thu 25/4/10	Thu 25/4/10	Thu 25/4/10	Thu 25/4/10	Thu 25/4/10	Thu 25/4/10	0 days	64
65	Manhole Construction	Wed 25/4/9	Thu 25/4/18	Thu 25/4/18	Thu 25/4/18	Thu 25/4/18	Thu 25/4/18	10 days	65
66	Reinstatement	Sat 25/4/19	Sat 25/4/19	Sat 25/4/19	Sat 25/4/19	Sat 25/4/19	Sat 25/4/19	0 days	66
67	T1A Removal	Mon 25/4/27	Mon 25/4/27	Mon 25/4/27	Mon 25/4/27	Mon 25/4/27	Mon 25/4/27	0 days	67
68	T1A Implementation	Thu 25/4/29	Thu 25/4/29	Thu 25/4/29	Thu 25/4/29	Thu 25/4/29	Thu 25/4/29	0 days	68
69	Breaking Ground	Thu 25/5/10	Thu 25/5/10	Thu 25/5/10	Thu 25/5/10	Thu 25/5/10	Thu 25/5/10	0 days	70
70	Excavation and Lateral Support	Mon 25/5/18	Mon 25/5/18	Mon 25/5/18	Mon 25/5/18	Mon 25/5/18	Mon 25/5/18	0 days	70
71	Drain Laying	Mon 25/5/26	Mon 25/5/26	Mon 25/5/26	Mon 25/5/26	Mon 25/5/26	Mon 25/5/26	0 days	71
72	Excavation and Lateral Support	Sun 25/6/1	Sun 25/6/1	Sun 25/6/1	Sun 25/6/1	Sun 25/6/1	Sun 25/6/1	0 days	72
73	Bedding and Backfilling	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	Mon 25/6/9	0 days	73
74	Manhole Construction	Mon 25/6/15	Mon 25/6/15	Mon 25/6/15	Mon 25/6/15	Mon 25/6/15	Mon 25/6/15	0 days	74
75	Reinstatement	Wed 25/6/17	Wed 25/6/17	Wed 25/6/17	Wed 25/6/17	Wed 25/6/17	Wed 25/6/17	0 days	75
76	T1A Removal	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	Thu 25/6/19	0 days	76
77	SHT A04-SHT A05.1500PC.B.L=81.31.D=3.44 T1A Implementation	Mon 25/6/20	Mon 25/6/20	Mon 25/6/20	Mon 25/6/20	Mon 25/6/20	Mon 25/6/20	0 days	77
78	T1A Implementation	Mon 25/6/20	Mon 25/6/20	Mon 25/6/20	Mon 25/6/20	Mon 25/6/20	Mon 25/6/20	0 days	78
79	Breaking Ground	Mon 25/6/22	Mon 25/6/22	Mon 25/6/22	Mon 25/6/22	Mon 25/6/22	Mon 25/6/22	0 days	79
80	Excavation and Lateral Support	Thu 25/7/15	Thu 25/7/15	Thu 25/7/15	Thu 25/7/15	Thu 25/7/15	Thu 25/7/15	0 days	80
81	Excavation and Lateral Support	Mon 25/7/18	Mon 25/7/18	Mon 25/7/18	Mon 25/7/18	Mon 25/7/18	Mon 25/7/18	0 days	81
82	Drain Laying	Mon 25/7/24	Mon 25/7/24	Mon 25/7/24	Mon 25/7/24	Mon 25/7/24	Mon 25/7/24	0 days	82
83	Bedding and Backfilling	Thu 25/8/8	Thu 25/8/8	Thu 25/8/8	Thu 25/8/8	Thu 25/8/8	Thu 25/8/8	0 days	83
84	Manhole Construction	Wed 25/7/30	Thu 25/8/8	Thu 25/8/8	Thu 25/8/8	Thu 25/8/8	Thu 25/8/8	10 days	84
85	Reinstatement	Sat 25/8/9	Sat 25/8/9	Sat 25/8/9	Sat 25/8/9	Sat 25/8/9	Sat 25/8/9	0 days	85
86	T1A Removal	Mon 25/8/18	Mon 25/8/18	Mon 25/8/18	Mon 25/8/18	Mon 25/8/18	Mon 25/8/18	0 days	86
87	Stage 2 T1A Implementation	Wed 25/8/19	Wed 25/8/19	Wed 25/8/19	Wed 25/8/19	Wed 25/8/19	Wed 25/8/19	0 days	87
88	T1A Implementation	Thu 25/8/19	Thu 25/8/19	Thu 25/8/19	Thu 25/8/19	Thu 25/8/19	Thu 25/8/19	0 days	88
89	Breaking Ground	Thu 25/8/21	Thu 25/8/21	Thu 25/8/21	Thu 25/8/21	Thu 25/8/21	Thu 25/8/21	0 days	89
90	Excavation and Lateral Support	Thu 25/8/29	Thu 25/8/29	Thu 25/8/29	Thu 25/8/29	Thu 25/8/29	Thu 25/8/29	0 days	90
91	Drain Laying	Wed 25/9/10	Wed 25/9/10	Wed 25/9/10	Wed 25/9/10	Wed 25/9/10	Wed 25/9/10	0 days	91
92	Bedding and Backfilling	Sat 25/9/21	Sat 25/9/21	Sat 25/9/21	Sat 25/9/21	Sat 25/9/21	Sat 25/9/21	0 days	92
93	Manhole Construction	Sun 25/9/25	Sun 25/9/25	Sun 25/9/25	Sun 25/9/25	Sun 25/9/25	Sun 25/9/25	0 days	93
94	Reinstatement	Mon 25/10/6	Mon 25/10/6	Mon 25/10/6	Mon 25/10/6	Mon 25/10/6	Mon 25/10/6	0 days	94
95	T1A Removal	Thu 25/10/14	Thu 25/10/14	Thu 25/10/14	Thu 25/10/14	Thu 25/10/14	Thu 25/10/14	0 days	95
96	Stage 3 T1A Implementation	Thu 25/10/16	Thu 25/10/16	Thu 25/10/16	Thu 25/10/16	Thu 25/10/16	Thu 25/10/16	0 days	96
97	T1A Implementation	Thu 25/10/16	Thu 25/10/16	Thu 25/10/16	Thu 25/10/16	Thu 25/10/16	Thu 25/10/16	0 days	97
98	Breaking Ground	Mon 25/10/27	Sat 25/10/18	Mon 25/10/27	Sat 25/10/18	Mon 25/10/27	Sat 25/10/18	15 days	98
99	Excavation and Lateral Support	Sun 25/10/26	Sat 25/11/8	Mon 25/11/8	Sun 25/10/26	Mon 25/11/8	Sun 25/10/26	15 days	99
100	Drain Laying	Sat 25/11/17	Mon 25/11/24	Mon 25/11/24	Mon 25/11/24	Mon 25/11/24	Mon 25/11/24	8 days	100
101	Bedding and Backfilling	Mon 25/11/22	Tue 25/12/2	Mon 25/11/22	Tue 25/12/2	Mon 25/11/22	Tue 25/12/2	15 days	101
102	Manhole Construction	Mon 25/11/23	Tue 25/12/2	Mon 25/11/23	Tue 25/12/2	Mon 25/11/23	Tue 25/12/2	15 days	102
103	Reinstatement	Wed 25/12/3	Thu 25/12/10	Wed 25/12/3	Thu 25/12/10	Wed 25/12/3	Thu 25/12/10	8 days	103
104	T1A Removal	Thu 25/12/11	Fri 25/12/12	Thu 25/12/11	Fri 25/12/12	Thu 25/12/11	Fri 25/12/12	2 days	104
105	Connection of ex. 900pipe to SHT A05	Sat 25/12/13	Sun 26/1/1	Sat 25/12/13	Sun 26/1/1	Sat 25/12/13	Sun 26/1/1	30 days	105
106	Connection of ex. 900pipe to SHT A06A	Tue 26/1/12	Tue 26/1/12	Tue 26/1/12	Tue 26/1/12	Tue 26/1/12	Tue 26/1/12	0 days	106
107	CCTV Inspection	Wed 26/3/2	Wed 26/3/2	Wed 26/3/2	Wed 26/3/2	Wed 26/3/2	Wed 26/3/2	0 days	107
108	Reinstatement	Wed 26/3/22	Wed 26/3/22	Wed 26/3/22	Wed 26/3/22	Wed 26/3/22	Wed 26/3/22	0 days	108
109	access date of Portion E2	Mon 26/1/26	Fri 25/5/2	Mon 26/1/26	Fri 25/5/2	Mon 26/1/26	Fri 25/5/2	703 days	109
110	section V (Shan Hai Tsuen)	Mon 26/1/26	Tue 23/5/30	Mon 26/1/26	Tue 23/5/30	Mon 26/1/26	Tue 23/5/30	0 days	110
111	Planned Completion Day	Mon 26/4/6	Tue 26/4/6	Mon 26/4/6	Tue 26/4/6	Mon 26/4/6	Tue 26/4/6	0 days	111
112	Early Access (partial) [A]	Mon 26/4/6	Tue 23/5/30	Mon 26/4/6	Tue 23/5/30	Mon 26/4/6	Tue 23/5/30	205 days	112
113	Site Establishment	Mon 25/1/21	Tue 23/9/12	Mon 25/1/21	Tue 23/9/12	Mon 25/1/21	Tue 23/9/12	812 days	113
114	Prepare and Accept Temp. Works Design and Method Statement [A]	Mon 25/1/21	Mon 25/1/21	Mon 25/1/21	Mon 25/1/21	Mon 25/1/21	Mon 25/1/21	0 days	114
115	Public Liaison and Negotiation with Village Rep.	Mon 25/1/21	Tue 23/9/12	Mon 25/1/21	Tue 23/9/12	Mon 25/1/21	Tue 23/9/12	798 days	115
116	[NCEXX] Objection and additional request of local landlord	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	Tue 23/9/12	0 days	116
117	Initial Survey [A]	Mon 25/1/21	Mon 25/1/21	Mon 25/1/21	Mon 25/1/21	Mon 25/1/21	Mon 25/1/21	0 days	117
118	Initial Safety & Environmental measures [A]	Thu 24/3/14	Fri 24/3/14	Thu 24/3/14	Fri 24/3/14	Thu 24/3/14	Fri 24/3/14	21 days	118
119	Setup of instrumentation and monitoring [A]	Thu 24/3/14	Fri 24/3/14	Thu 24/3/14	Fri 24/3/14	Thu 24/3/14	Fri 24/3/14	21 days	119
120		Thu 27/1/15	Fri 27/1/15	Thu 27/1/15	Fri 27/1/15	Thu 27/1/15	Fri 27/1/15	1036 days	120

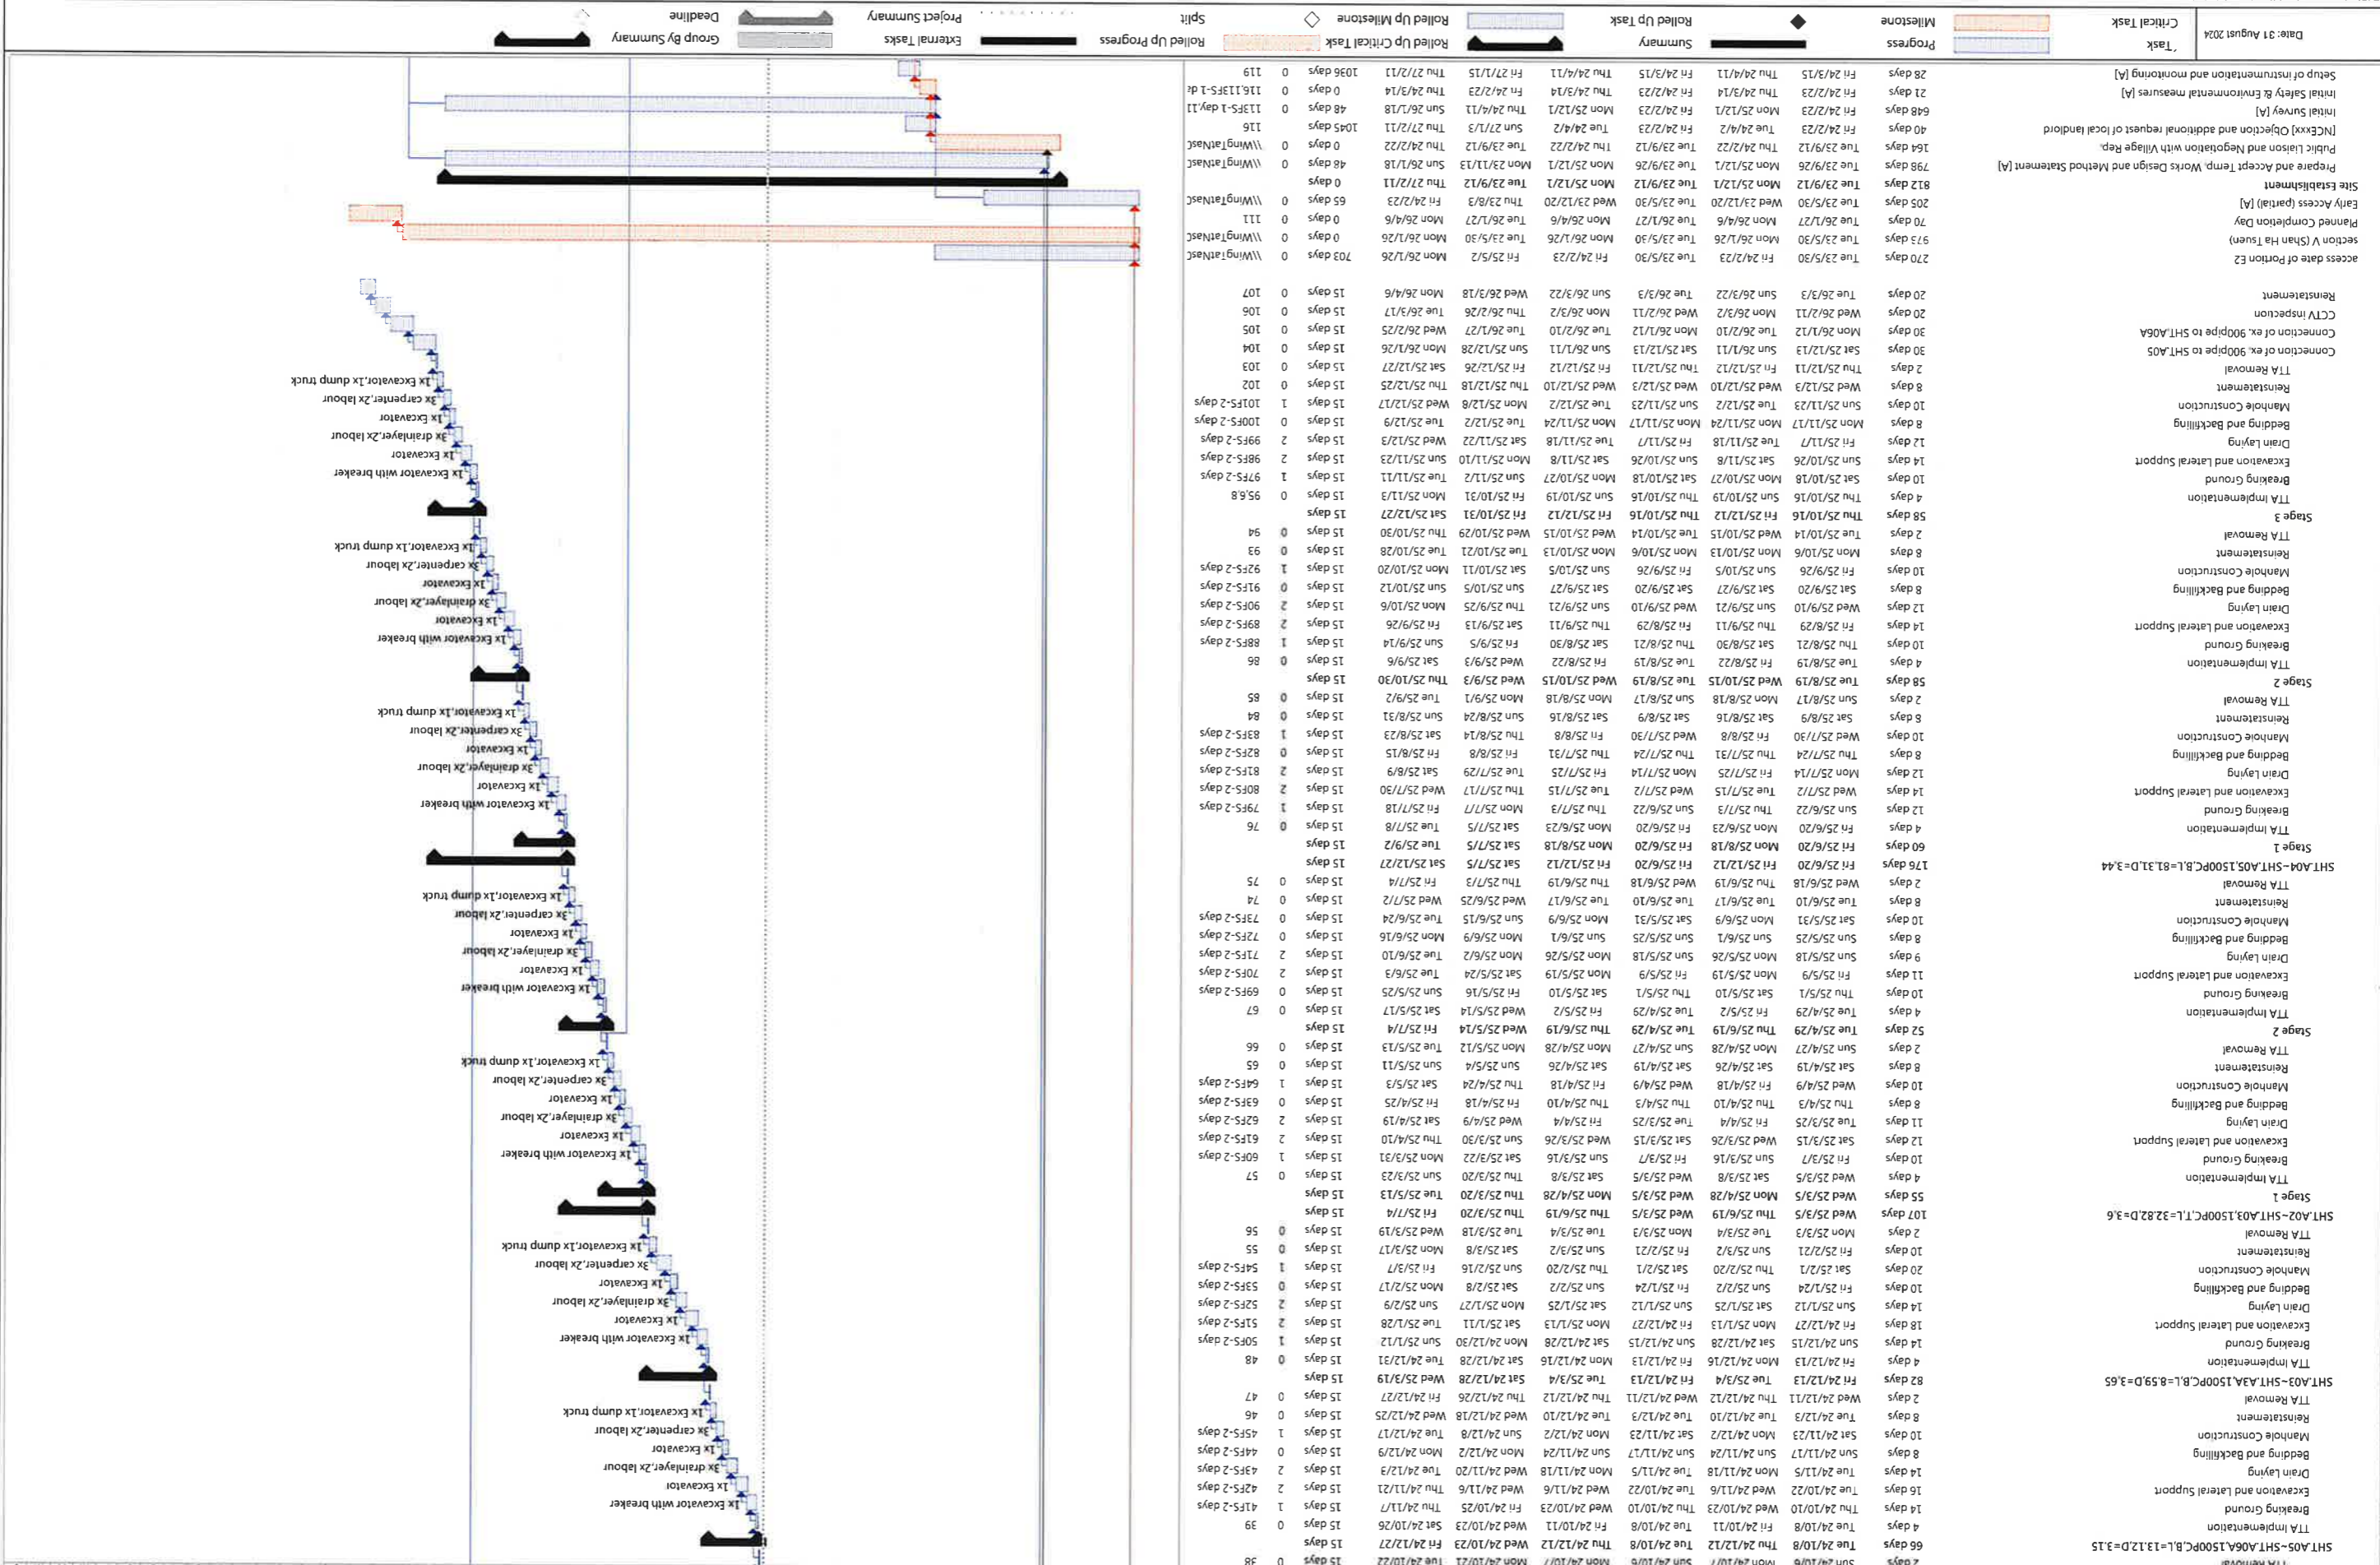


ID	Task Name	Start	Finish	Early Start	Early Finish	Late Start	Late Finish	Total Slack	TR	Predecessors
121	Condition Survey [A]	Thu 24/3/15	Thu 24/4/11	Thu 24/3/15	Thu 24/4/11	Thu 24/3/15	Thu 24/4/11	0 days	0	119
122	Tree Survey [A]	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	Fri 24/3/15	Thu 24/4/11	0 days	0	119
123	Built Heritage Survey [A]	Mon 24/3/20	Mon 24/3/30	Fri 24/3/15	Mon 24/3/30	Mon 24/3/20	Mon 24/3/30	86d	0	119
124	UI detection [A]	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	Thu 24/3/15	0 days	0	121,122
125	Site Clearance [A]	Fri 24/3/15	Thu 24/3/30	Fri 24/3/15	Thu 24/3/30	Fri 24/3/15	Thu 24/3/30	0 days	0	124,125
126	Drain Laying Works (West)	Fri 24/3/15	Sun 26/3/22	Fri 24/3/15	Sun 26/3/22	Fri 24/3/15	Sun 26/3/22	0 days	0	125
127	SHT1802-SHT1803,900PC,B,L=36.94,D=1.72	Fri 24/3/15	Wed 24/7/10	Fri 24/3/15	Wed 24/7/10	Fri 24/3/15	Wed 24/7/10	0 days	0	126
128	TTA Implementation [A]	Mon 24/6/3	Mon 24/6/3	Mon 24/6/3	Mon 24/6/3	Mon 24/6/3	Mon 24/6/3	0 days	0	127
129	TTA Implementation [A]	Fri 24/5/31	Mon 24/6/3	Fri 24/5/31	Mon 24/6/3	Fri 24/5/31	Mon 24/6/3	0 days	0	128
130	Breaking pavement [A]	Thu 24/6/2	Fri 24/6/7	Thu 24/6/2	Fri 24/6/7	Thu 24/6/2	Fri 24/6/7	0 days	0	129
131	Excavation and Lateral Support [A]	Thu 24/6/6	Thu 24/6/19	Thu 24/6/6	Thu 24/6/19	Thu 24/6/6	Thu 24/6/19	0 days	0	130
132	Manhole bedding construction [A]	Sun 24/6/18	Sun 24/6/23	Sun 24/6/18	Sun 24/6/23	Sun 24/6/18	Sun 24/6/23	0 days	0	131
133	Drain Laying [A]	Sat 24/6/22	Thu 24/6/27	Sat 24/6/22	Thu 24/6/27	Sat 24/6/22	Thu 24/6/27	0 days	0	132
134	Manhole construction [A]	Mon 24/7/1	Mon 24/7/1	Mon 24/7/1	Mon 24/7/1	Mon 24/7/1	Mon 24/7/1	0 days	0	133
135	Backfilling and Compaction [A]	Sun 24/6/30	Thu 24/7/4	Sun 24/6/30	Thu 24/7/4	Sun 24/6/30	Thu 24/7/4	0 days	0	134
136	TTA removal [A]	Wed 24/7/10	Wed 24/7/10	Wed 24/7/10	Wed 24/7/10	Wed 24/7/10	Wed 24/7/10	0 days	0	135
137	TTA Implementation [A]	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	Thu 24/7/11	0 days	0	136
138	Stage 2	Thu 24/7/11	Thu 24/8/20	Thu 24/7/11	Thu 24/8/20	Thu 24/7/11	Thu 24/8/20	0 days	0	137
139	TTA Implementation [A]	Sun 24/7/13	Thu 24/7/18	Sun 24/7/13	Thu 24/7/18	Sun 24/7/13	Thu 24/7/18	0 days	0	138
140	Breaking pavement [A]	Thu 24/7/13	Thu 24/7/13	Thu 24/7/13	Thu 24/7/13	Thu 24/7/13	Thu 24/7/13	0 days	0	139
141	Excavation and Lateral Support [A]	Wed 24/7/17	Thu 24/7/30	Wed 24/7/17	Thu 24/7/30	Wed 24/7/17	Thu 24/7/30	0 days	0	140
142	Manhole bedding construction [A]	Mon 24/7/23	Mon 24/7/23	Mon 24/7/23	Mon 24/7/23	Mon 24/7/23	Mon 24/7/23	0 days	0	141
143	Drain Laying [A]	Fri 24/8/7	Fri 24/8/7	Fri 24/8/7	Fri 24/8/7	Fri 24/8/7	Fri 24/8/7	0 days	0	142
144	Manhole construction [A]	Sun 24/8/6	Sun 24/8/11	Sun 24/8/6	Sun 24/8/11	Sun 24/8/6	Sun 24/8/11	0 days	0	143
145	Backfilling and Compaction [A]	Wed 24/8/14	Mon 24/8/19	Wed 24/8/14	Mon 24/8/19	Wed 24/8/14	Mon 24/8/19	0 days	0	144
146	TTA removal	Tue 24/8/20	Tue 24/8/20	Tue 24/8/20	Tue 24/8/20	Tue 24/8/20	Tue 24/8/20	0 days	0	145
147	SHT1801-SHT1802,900PC,B,L=61.6,D=1.59	Wed 24/8/21	Sat 24/8/24	Wed 24/8/21	Sat 24/8/24	Wed 24/8/21	Sat 24/8/24	0 days	0	146
148	TTA Implementation [A]	Wed 24/8/21	Sat 24/8/24	Wed 24/8/21	Sat 24/8/24	Wed 24/8/21	Sat 24/8/24	0 days	0	147
150	Breaking pavement [A]	Wed 24/8/23	Fri 24/8/28	Wed 24/8/23	Fri 24/8/28	Wed 24/8/23	Fri 24/8/28	0 days	0	148
151	Excavation and Lateral Support [A]	Tue 24/8/27	Sat 24/9/7	Tue 24/8/27	Sat 24/9/7	Tue 24/8/27	Sat 24/9/7	0 days	0	149
152	Manhole bedding construction [A]	Fri 24/9/6	Fri 24/9/6	Fri 24/9/6	Fri 24/9/6	Fri 24/9/6	Fri 24/9/6	0 days	0	150
153	Drain Laying	Tue 24/9/10	Sun 24/9/15	Tue 24/9/10	Sun 24/9/15	Tue 24/9/10	Sun 24/9/15	0 days	0	151
154	Manhole construction [A]	Sat 24/9/14	Thu 24/9/19	Sat 24/9/14	Thu 24/9/19	Sat 24/9/14	Thu 24/9/19	0 days	0	152
155	Backfilling and Compaction	Wed 24/9/18	Sun 24/9/22	Wed 24/9/18	Sun 24/9/22	Wed 24/9/18	Sun 24/9/22	0 days	0	153
156	Reinstatement	Mon 24/9/23	Fri 24/9/27	Mon 24/9/23	Fri 24/9/27	Mon 24/9/23	Fri 24/9/27	0 days	0	154
157	TTA removal	Sat 24/9/28	Sat 24/9/28	Sat 24/9/28	Sat 24/9/28	Sat 24/9/28	Sat 24/9/28	0 days	0	155
158	SHT1801-SHT1802,900PC,B,L=61.6,D=1.59	Wed 24/9/29	Sun 24/9/29	Wed 24/9/29	Sun 24/9/29	Wed 24/9/29	Sun 24/9/29	0 days	0	156
159	Stage 1	Mon 24/9/29	Mon 24/11/4	Mon 24/9/29	Mon 24/11/4	Mon 24/9/29	Mon 24/11/4	0 days	0	157
160	TTA Implementation	Wed 24/10/2	Sun 24/9/29	Wed 24/10/2	Sun 24/9/29	Wed 24/10/2	Sun 24/9/29	0 days	0	158
161	Breaking pavement	Tue 24/10/1	Sun 24/10/6	Tue 24/10/1	Sun 24/10/6	Tue 24/10/1	Sun 24/10/6	0 days	0	159
162	Excavation and Lateral Support	Mon 24/10/5	Mon 24/10/14	Mon 24/10/5	Mon 24/10/14	Mon 24/10/5	Mon 24/10/14	0 days	0	160
163	Manhole bedding construction	Fri 24/10/13	Mon 24/10/18	Fri 24/10/13	Mon 24/10/18	Fri 24/10/13	Mon 24/10/18	0 days	0	161
164	Drain Laying	Thu 24/10/17	Thu 24/10/22	Thu 24/10/17	Thu 24/10/22	Thu 24/10/17	Thu 24/10/22	0 days	0	162
165	Manhole construction	Mon 24/10/26	Mon 24/10/26	Mon 24/10/26	Mon 24/10/26	Mon 24/10/26	Mon 24/10/26	0 days	0	163
166	Backfilling and Compaction	Tue 24/10/25	Fri 24/10/29	Tue 24/10/25	Fri 24/10/29	Tue 24/10/25	Fri 24/10/29	0 days	0	164
167	Reinstatement	Sun 24/10/30	Wed 24/10/30	Sun 24/10/30	Wed 24/10/30	Sun 24/10/30	Wed 24/10/30	0 days	0	165
168	TTA removal	Mon 24/11/4	Mon 24/11/4	Mon 24/11/4	Mon 24/11/4	Mon 24/11/4	Mon 24/11/4	0 days	0	166
169	Stage 2	Tue 24/11/5	Wed 24/12/11	Tue 24/11/5	Wed 24/12/11	Tue 24/11/5	Wed 24/12/11	0 days	0	167
170	TTA Implementation	Fri 24/11/8	Tue 24/11/8	Fri 24/11/8	Tue 24/11/8	Fri 24/11/8	Tue 24/11/8	0 days	0	168
171	Breaking pavement	Thu 24/11/7	Thu 24/11/7	Thu 24/11/7	Thu 24/11/7	Thu 24/11/7	Thu 24/11/7	0 days	0	169
172	Excavation and Lateral Support	Mon 24/11/20	Mon 24/11/20	Mon 24/11/20	Mon 24/11/20	Mon 24/11/20	Mon 24/11/20	0 days	0	170
173	Manhole bedding construction	Sun 24/11/19	Thu 24/11/24	Sun 24/11/19	Thu 24/11/24	Sun 24/11/19	Thu 24/11/24	0 days	0	171
174	Drain Laying	Thu 24/11/23	Thu 24/11/23	Thu 24/11/23	Thu 24/11/23	Thu 24/11/23	Thu 24/11/23	0 days	0	172
175	Manhole construction	Mon 24/11/27	Mon 24/12/2	Mon 24/11/27	Mon 24/12/2	Mon 24/11/27	Mon 24/12/2	0 days	0	173
176	Backfilling and Compaction	Sun 24/12/1	Thu 24/12/5	Sun 24/12/1	Thu 24/12/5	Sun 24/12/1	Thu 24/12/5	0 days	0	174
177	Reinstatement	Thu 24/12/10	Fri 24/12/6	Thu 24/12/10	Fri 24/12/6	Thu 24/12/10	Fri 24/12/6	0 days	0	175
178	TTA removal	Wed 24/12/11	Wed 24/12/11	Wed 24/12/11	Wed 24/12/11	Wed 24/12/11	Wed 24/12/11	0 days	0	176
179	SHT1CP2-SHT1801,900PC,B,L=10.36,D=1.59	Thu 24/12/12	Sat 24/12/12	Thu 24/12/12	Sat 24/12/12	Thu 24/12/12	Sat 24/12/12	0 days	0	177
180	TTA Implementation	Thu 24/12/12	Sat 24/12/12	Thu 24/12/12	Sat 24/12/12	Thu 24/12/12	Sat 24/12/12	0 days	0	178
181	Breaking pavement	Fri 24/12/13	Wed 24/12/18	Fri 24/12/13	Wed 24/12/18	Fri 24/12/13	Wed 24/12/18	0 days	0	179
182	Excavation and Lateral Support	Thu 24/12/17	Thu 24/12/26	Thu 24/12/17	Thu 24/12/26	Thu 24/12/17	Thu 24/12/26	0 days	0	180
183	Manhole bedding construction	Mon 24/12/25	Mon 24/12/30	Mon 24/12/25	Mon 24/12/30	Mon 24/12/25	Mon 24/12/30	0 days	0	181
184	Drain Laying	Fri 25/1/3	Fri 25/1/3	Fri 25/1/3	Fri 25/1/3	Fri 25/1/3	Fri 25/1/3	0 days	0	182
185	Manhole construction	Thu 25/1/8	Thu 25/1/8	Thu 25/1/8	Thu 25/1/8	Thu 25/1/8	Thu 25/1/8	0 days	0	183
186	Backfilling and Compaction	Sat 25/1/11	Tue 25/1/7	Sat 25/1/11	Tue 25/1/7	Sat 25/1/11	Tue 25/1/7	0 days	0	184
187	Reinstatement	Sun 25/1/12	Thu 25/1/16	Sun 25/1/12	Thu 25/1/16	Sun 25/1/12	Thu 25/1/16	0 days	0	185
188	TTA removal	Fri 25/1/17	Fri 25/1/17	Fri 25/1/17	Fri 25/1/17	Fri 25/1/17	Fri 25/1/17	0 days	0	186
189	SHT1804-SHT1A1A,900PC,B,L=13.155D=2.06	Tue 25/4/15	Thu 25/4/30	Tue 25/4/15	Thu 25/4/30	Tue 25/4/15	Thu 25/4/30	0 days	0	187
190	TTA Implementation	Tue 25/4/15	Thu 25/4/15	Tue 25/4/15	Thu 25/4/15	Tue 25/4/15	Thu 25/4/15	0 days	0	188
191	Breaking pavement	Mon 25/4/16	Mon 25/4/21	Mon 25/4/16	Mon 25/4/21	Mon 25/4/16	Mon 25/4/21	0 days	0	189
192	Excavation and Lateral Support	Sun 25/4/20	Thu 25/5/1	Sun 25/4/20	Thu 25/5/1	Sun 25/4/20	Thu 25/5/1	0 days	0	190
193	Manhole bedding construction	Wed 25/4/30	Wed 25/4/30	Wed 25/4/30	Wed 25/4/30	Wed 25/4/30	Wed 25/4/30	0 days	0	191
194	Drain Laying	Mon 25/5/6	Tue 25/5/13	Mon 25/5/6	Tue 25/5/13	Mon 25/5/6	Tue 25/5/13	0 days	0	192
195	Manhole construction	Mon 25/5/12	Mon 25/5/19	Mon 25/5/12	Mon 25/5/19	Mon 25/5/12	Mon 25/5/19	0 days	0	193
196	Backfilling and Compaction	Sun 25/5/18	Fri 25/5/23	Sun 25/5/18	Fri 25/5/23	Sun 25/5/18	Fri 25/5/23	0 days	0	194
197	Reinstatement	Thu 25/5/24	Thu 25/5/29	Thu 25/5/24	Thu 25/5/29	Thu 25/5/24	Thu 25/5/29	0 days	0	195
198	TTA removal	Fri 25/5/30	Fri 25/5/30	Fri 25/5/30	Fri 25/5/30	Fri 25/5/30	Fri 25/5/30	0 days	0	196
199	Connection of ex. UC to SHT1A1A	Sat 25/5/31	Fri 25/6/7	Sat 25/5/31	Fri 25/6/7	Sat 25/5/31	Fri 25/6/7	0 days	0	197
200	SHT1CP1-SHT1A1A,550PC,B,L=4.16,D=2.06	Tue 25/6/28	Sun 25/7/13	Tue 25/6/28	Sun 25/7/13	Tue 25/6/28	Sun 25/7/13	0 days	0	198
201	TTA Implementation	Sat 25/6/28	Mon 25/6/30	Sat 25/6/28	Mon 25/6/30	Sat 25/6/28	Mon 25/6/30	0 days	0	199
202	Breaking pavement	Sun 25/6/29	Fri 25/7/4	Sun 25/6/29	Fri 25/7/4	Sun 25/6/29	Fri 25/7/4	0 days	0	200

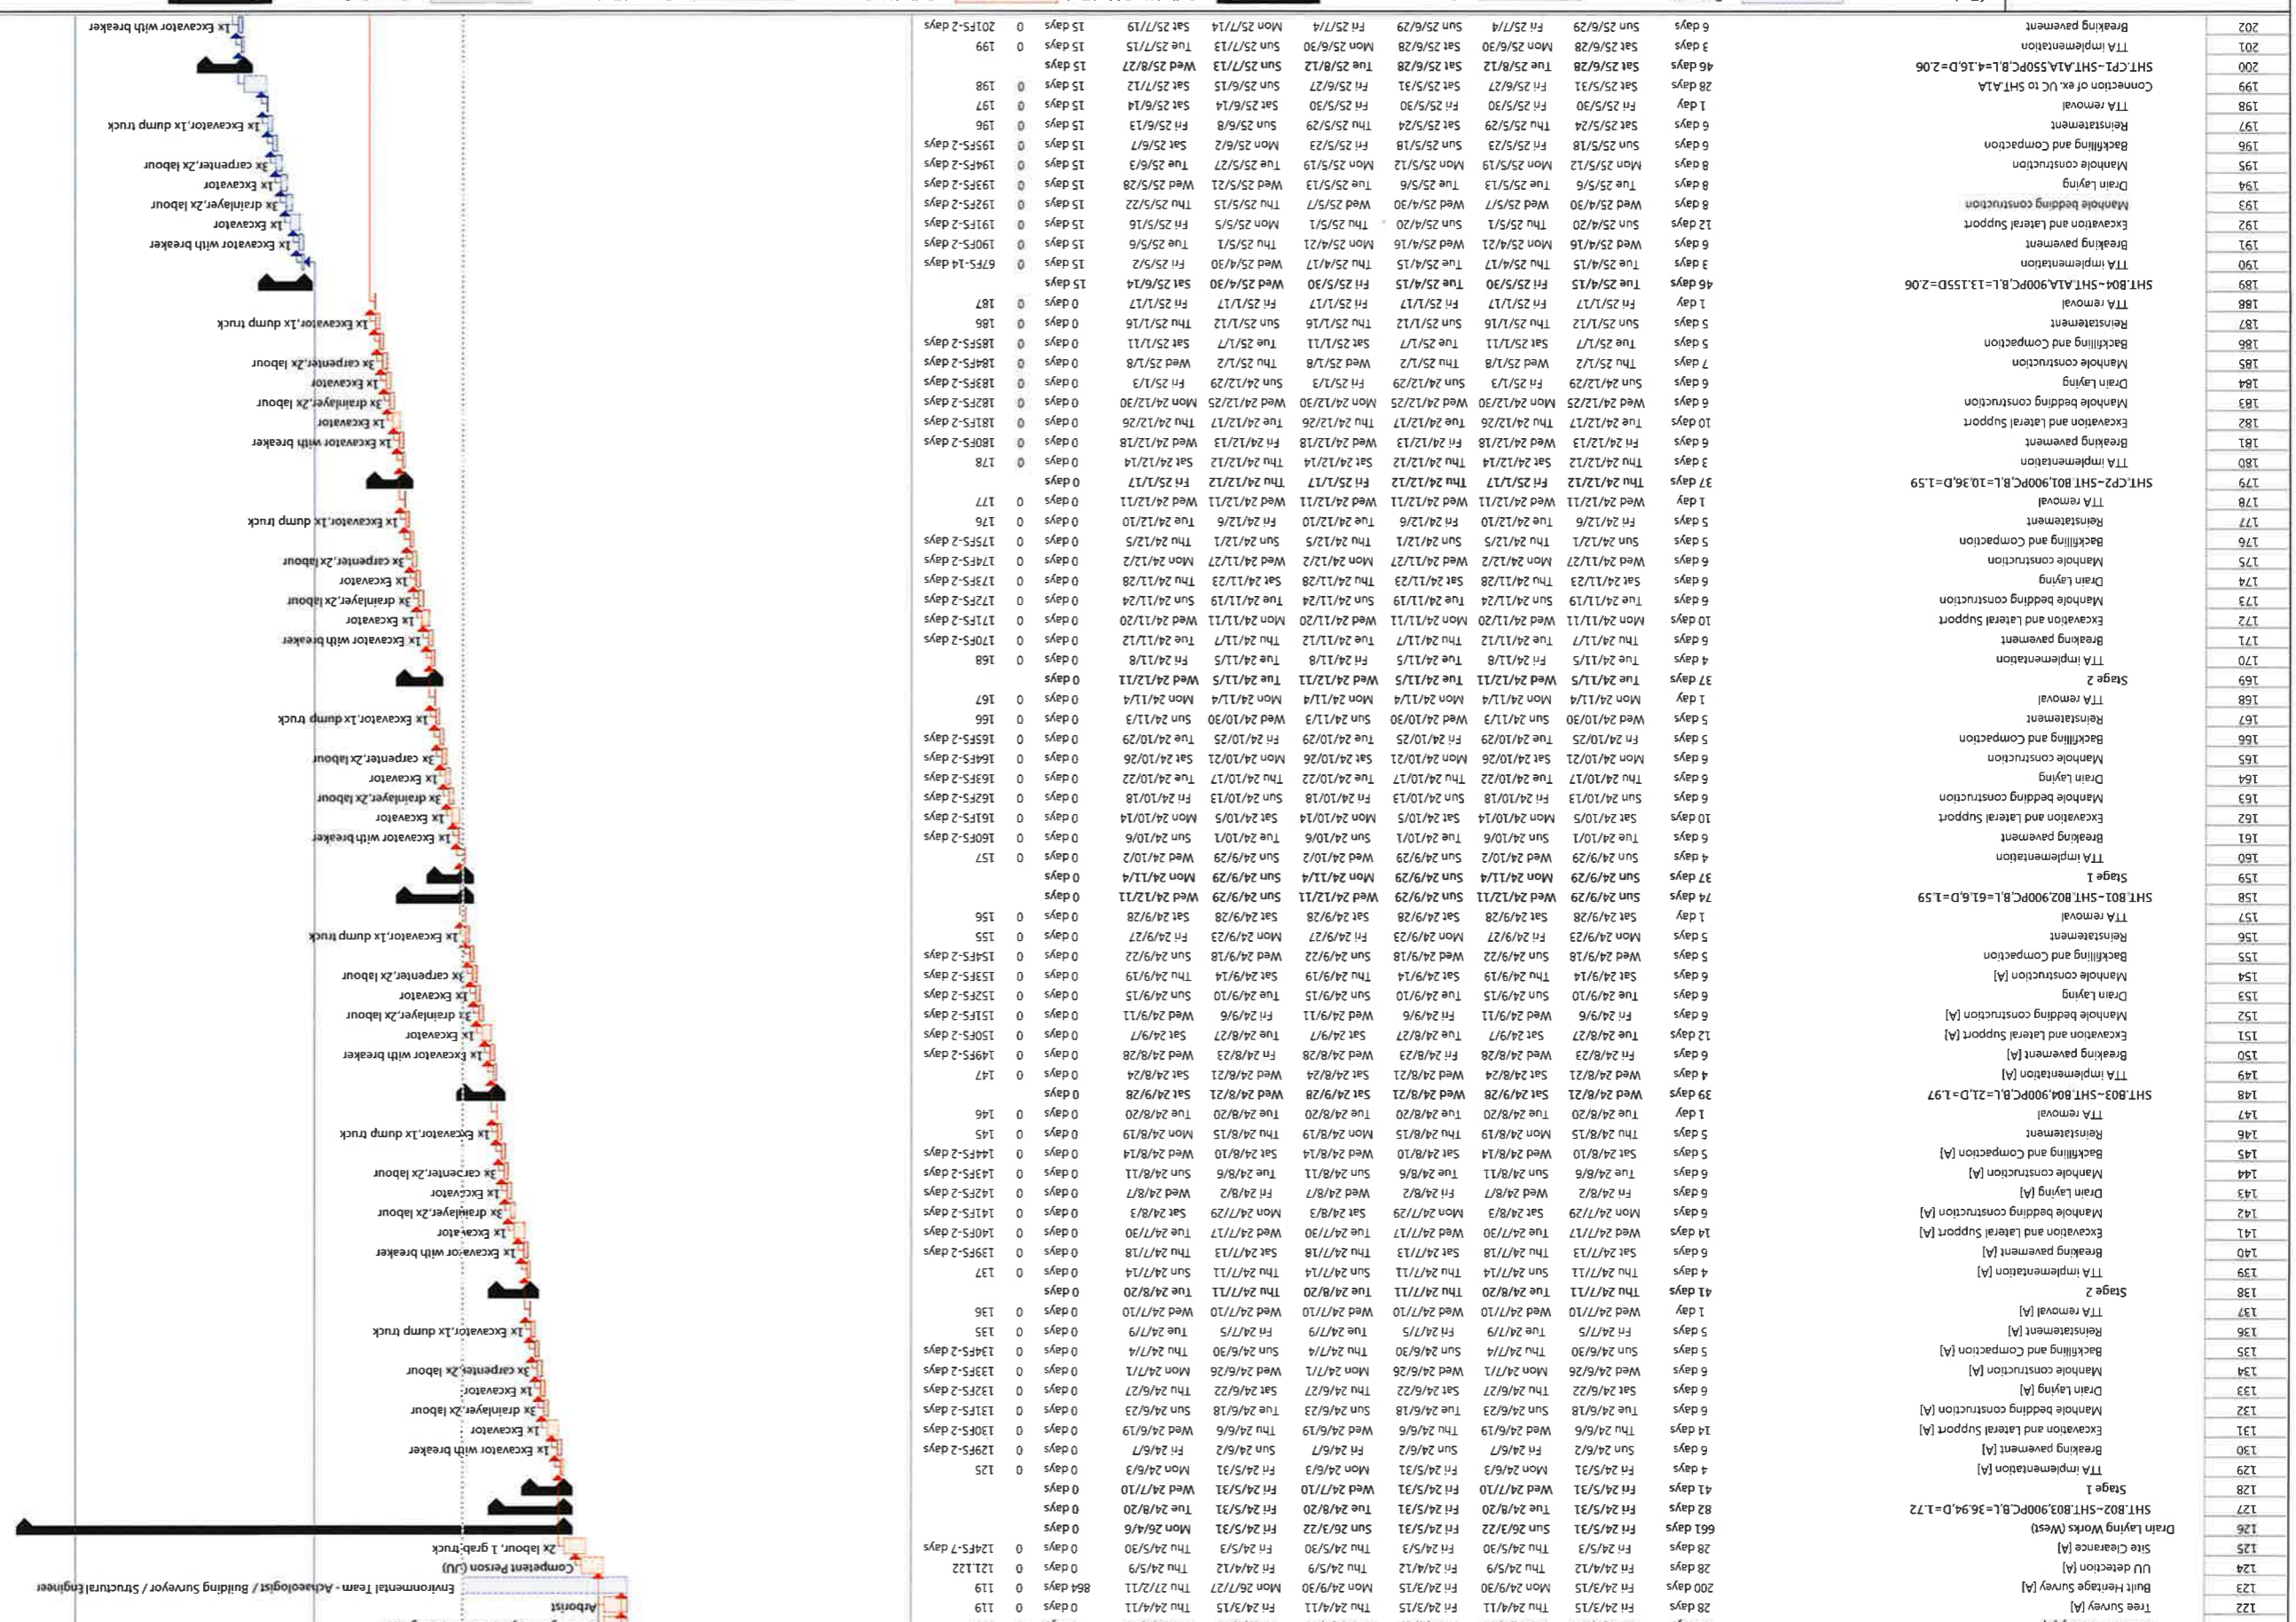

Task	Summary	Progress	Milestone	Critical Task	Task
202	Breaking pavement				202
201	TTA Implementation				201
200	SHT1CP1-SHT1A1A,550PC,B,L=4.16,D=2.06				200
199	Connection of ex. UC to SHT1A1A				199
198	TTA removal				198

ID	Task Name	Start	Finish	Duration	Task	Progress	Summary	Rollled Up Critical Task	Rollled Up Progress	External Tasks	Group By Summary	Deadline
		Early Start	Late Start	Total Slack	RA	Predecessors	Half 1	Half 2	Half 1	Half 2	Half 1	Half 2
203	Excavation and Lateral Support	Mon 25/7/24	Mon 25/7/24	15 days	0	202FS-2 days						
204	Manhole bedding construction	Sun 25/7/24	Mon 25/7/24	15 days	0	203FS-2 days						
205	Drain Laying	Sat 25/7/24	Sun 25/7/24	15 days	0	204FS-2 days						
206	Manhole construction	Fri 25/8/1	Fri 25/8/1	15 days	0	205FS-2 days						
207	Backfilling and Compaction	Tue 25/7/31	Tue 25/8/5	6 days	0	206FS-2 days						
208	Restoration	Mon 25/8/6	Mon 25/8/6	15 days	0	207FS-2 days						
209	Manhole bedding construction	Mon 25/8/6	Mon 25/8/6	15 days	0	208FS-2 days						
210	Connection of ex. 550pipe to SHT-CP1	Tue 25/8/13	Tue 25/8/13	15 days	0	209						
211	Connection of ex. 550pipe to SHT-CP1	Wed 25/8/13	Tue 25/8/13	15 days	0	208						
212	Manhole bedding construction	Wed 25/8/13	Tue 25/8/13	15 days	0	209						
213	Breakfast pavement	Wed 25/8/13	Tue 25/8/13	15 days	0	210						
214	Excavation and Lateral Support	Tue 25/9/16	Fri 25/9/26	12 days	0	213FS-2 days						
215	Manhole bedding construction	Fri 25/9/26	Fri 25/9/26	15 days	0	214FS-2 days						
216	Drain laying	Thu 25/10/2	Thu 25/10/2	15 days	0	215FS-2 days						
217	Manhole construction	Wed 25/10/8	Thu 25/10/2	15 days	0	216FS-2 days						
218	Backfilling and Compaction	Tue 25/10/14	Wed 25/10/29	15 days	0	217FS-2 days						
219	Restoration	Mon 25/10/20	Mon 25/10/29	10 days	0	218						
220	Connection of ex. Pipe to SHT-A01	Sun 25/10/27	Mon 25/10/27	15 days	0	219						
221	Connection of ex. Pipe to SHT-A01	Sun 25/10/27	Mon 25/10/27	15 days	0	220						
222	SHT-A01-SHT-A02,1500C.P.L.=8.39,D=3.6	Mon 25/11/24	Sun 25/11/24	42 days	0	221						
223	Breakfast pavement	Mon 25/11/24	Mon 25/11/24	15 days	0	222						
224	Excavation and Lateral Support	Wed 25/11/26	Mon 25/12/2	5 days	0	223FS-2 days						
225	Excavation and Lateral Support	Sat 25/11/29	Tue 25/12/2	12 days	0	224FS-2 days						
226	Drain laying	Thu 25/12/9	Sun 25/12/29	6 days	0	225FS-2 days						
227	Bedding and Backfilling	Sat 25/12/13	Thu 25/12/18	6 days	0	226FS-2 days						
228	Manhole construction	Wed 25/12/17	Thu 25/12/18	8 days	0	227FS-2 days						
229	Backfilling and Compaction	Tue 25/12/23	Sun 25/12/28	6 days	0	228FS-2 days						
230	Restoration	Mon 25/12/29	Sat 26/1/3	6 days	0	229						
231	TTA removal	Sun 26/1/4	Sun 26/1/4	15 days	0	230						
232	Temporary decking over ex. UC	Mon 26/1/15	Mon 26/1/15	15 days	0	231						
233	CCTV inspection	Mon 26/1/19	Mon 26/1/19	15 days	0	232						
234	Restoration	Mon 26/1/26	Mon 26/1/26	15 days	0	233						
235	U-Channel Works (West)	Sat 25/1/18	Tue 26/4/7	44 days	0	234						
236	End-ex. U-450UC(G).L=70	Sat 25/1/18	Thu 25/5/8	111 days	0	235						
237	Stage 1	Sat 25/1/18	Sat 25/2/15	29 days	0	236						
238	Excavation and Lateral Support [A]	Sat 25/1/18	Sat 25/2/15	29 days	0	237						
239	Formwork Erection [A]	Sun 25/1/26	Thu 25/2/6	12 days	0	238						
240	Catchpit construction [A]	Wed 25/2/5	Sat 25/2/15	11 days	0	239FS-2 days						
241	Concrete [A]	Fri 25/2/14	Fri 25/2/14	1 day	0	240FS-2 days						
242	Stage 2	Sat 25/2/15	Sat 25/2/15	29 days	0	241						
243	Excavation and Lateral Support [A]	Mon 25/2/24	Mon 25/2/24	10 days	0	242						
244	Formwork Erection	Wed 25/3/5	Sat 25/3/15	11 days	0	243FS-2 days						
245	Catchpit construction	Mon 25/3/15	Wed 25/3/15	11 days	0	244FS-2 days						
246	Concrete	Fri 25/3/14	Fri 25/3/14	1 day	0	245FS-2 days						
247	Stage 3	Sat 25/3/15	Sat 25/4/12	29 days	0	246						
248	Excavation and Lateral Support [A]	Mon 25/3/24	Mon 25/3/24	10 days	0	247						
249	Formwork Erection	Thu 25/4/3	Thu 25/4/3	12 days	0	248FS-2 days						
250	Catchpit construction	Sat 25/4/12	Sat 25/4/12	11 days	0	249FS-2 days						
251	Concrete	Fri 25/4/11	Fri 25/4/11	1 day	0	250FS-2 days						
252	Stage 4	Sat 25/4/12	Sat 25/4/12	27 days	0	251						
253	Excavation and Lateral Support	Mon 25/4/21	Sat 25/4/12	10 days	0	252						
254	Formwork Erection	Sun 25/4/20	Wed 25/4/30	11 days	0	253FS-2 days						
255	Catchpit construction	Thu 25/5/8	Thu 25/5/8	10 days	0	254FS-2 days						
256	Concrete	Thu 25/5/8	Thu 25/5/8	1 day	0	255FS-1 day						
257	SHT-CP2,5-SHT-CP2,300->900C(U).L=11.4	Fri 25/5/9	Fri 25/5/9	22 days	0	256						
258	Excavation and Lateral Support	Wed 25/5/14	Fri 25/5/14	6 days	0	257						
259	Formwork Erection	Tue 25/5/13	Fri 25/5/13	11 days	0	258FS-2 days						
260	Catchpit construction	Thu 25/5/22	Thu 25/5/30	9 days	0	259FS-2 days						
261	Concrete	Thu 25/5/29	Thu 25/5/29	1 day	0	260FS-2 days						
262	SHT-CP3-SHT-CP2,5,300->900C(U).L=66.5	Fri 25/5/30	Fri 25/5/30	70 days	0	261						
263	Stage 1	Fri 25/5/30	Fri 25/5/30	24 days	0	262						
264	Excavation and Lateral Support	Thu 25/6/5	Sat 25/6/14	10 days	0	263FS-2 days						
265	Formwork Erection	Fri 25/6/5	Sat 25/6/14	10 days	0	264FS-2 days						
266	Catchpit construction	Sun 25/6/22	Sun 25/6/22	10 days	0	265FS-2 days						
267	Concrete	Sat 25/6/21	Sat 25/6/21	1 day	0	266FS-2 days						
268	Stage 2	Sun 25/6/22	Sun 25/6/22	24 days	0	267						
269	Excavation and Lateral Support	Sun 25/6/22	Sun 25/6/22	8 days	0	268FS-2 days						
270	Formwork Erection	Mon 25/7/7	Mon 25/7/7	10 days	0	269FS-2 days						
271	Catchpit construction	Tue 25/7/15	Tue 25/7/15	10 days	0	270FS-2 days						
272	Concrete	Mon 25/7/14	Mon 25/7/14	1 day	0	271FS-2 days						
273	Stage 3	Thu 25/7/15	Thu 25/7/15	24 days	0	272						
274	Excavation and Lateral Support	Tue 25/7/22	Tue 25/7/22	8 days	0	273						
275	Formwork Erection	Mon 25/7/21	Wed 25/7/30	10 days	0	274FS-2 days						
276	Catchpit construction	Thu 25/7/29	Thu 25/7/29	10 days	0	275FS-2 days						
277	Concrete	Wed 25/8/6	Wed 25/8/6	1 day	0	276FS-2 days						
278	SHT-CP3-SHT-CP3,300->450C(U).L=54.5	Thu 25/8/7	Tue 25/10/21	76 days	0	277						
279	Excavation and Lateral Support	Thu 25/8/7	Thu 25/8/7	24 days	0	278						
280	Formwork Erection	Thu 25/8/14	Thu 25/8/14	8 days	0	279						
281	Formwork Erection	Wed 25/8/13	Wed 25/8/13	10 days	0	280FS-2 days						
282	Catchpit construction	Sat 25/8/20	Thu 25/8/21	10 days	0	281FS-2 days						
283	Concrete	Fri 25/8/29	Fri 25/8/29	1 day	0	282FS-2 days						
284	Stage 2	Sat 25/8/30	Sat 25/8/30	27 days	0	283						

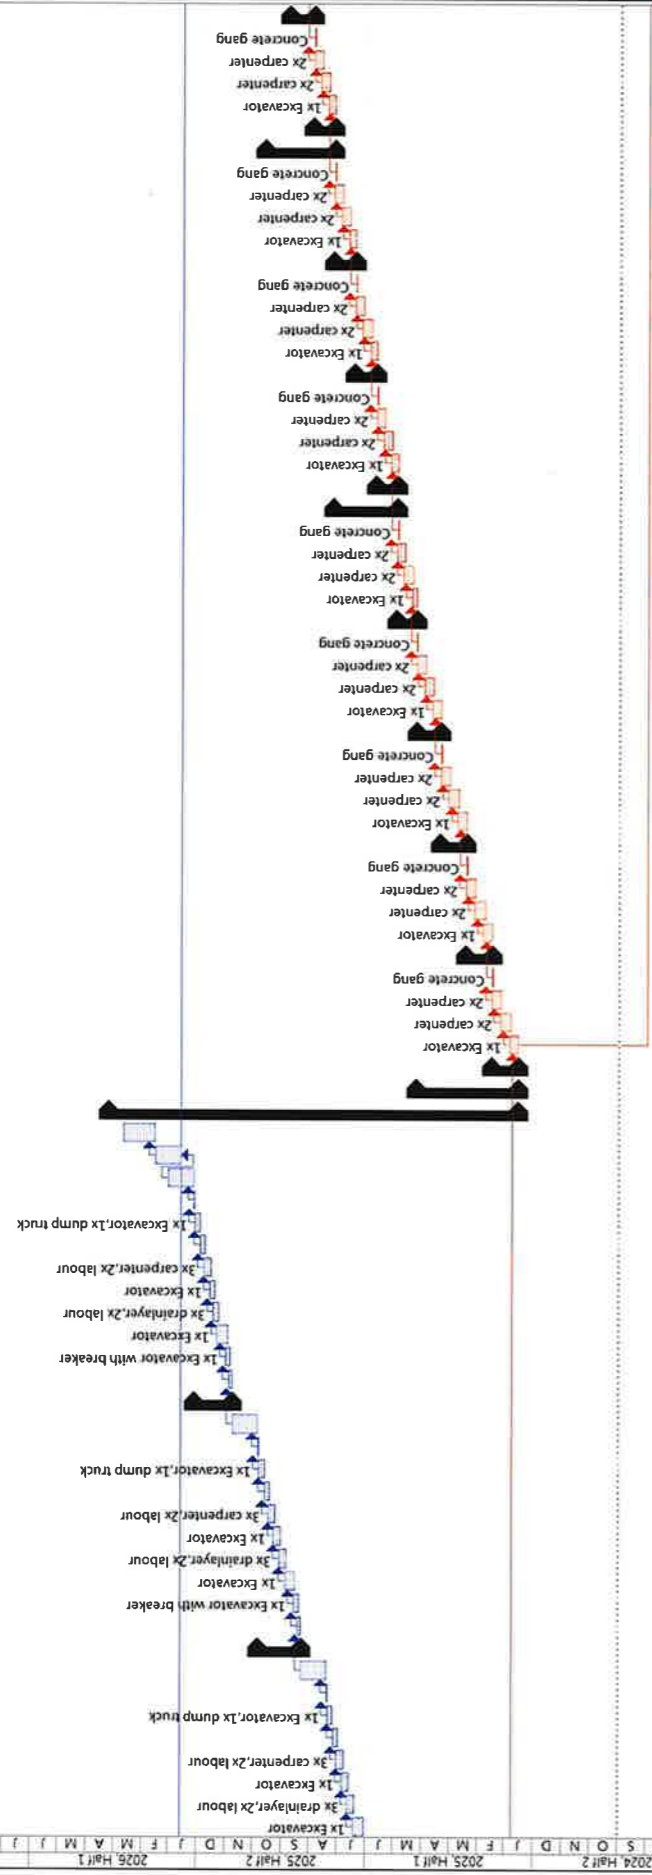

ID	Task Name	Start	Finish	Duration	Task	Progress	Summary	Rolled Up Task	Rolled Up Milestone	Split	External Tasks	Group By Summary	Deadline
285	Excavation and Lateral Support	Sat 25/8/30	Sat 25/9/6	8 days	Excavation and Lateral Support	0 days	Sat 25/8/30	Sat 25/9/6	Sat 25/8/30	Sat 25/9/6	0 days	Lx Excavator	0 days
286	Formwork Erection	Fri 25/9/5	Fri 25/9/5	12 days	Formwork Erection	0 days	Fri 25/9/5	Fri 25/9/5	Fri 25/9/5	Fri 25/9/5	0 days	Zx carpenter	0 days
287	Catchpit construction	Mon 25/9/15	Thu 25/9/25	11 days	Catchpit construction	0 days	Mon 25/9/15	Thu 25/9/25	Mon 25/9/15	Thu 25/9/25	0 days	Lx Excavator	0 days
288	Concrete	Wed 25/9/24	Wed 25/9/24	1 day	Concrete	0 days	Wed 25/9/24	Wed 25/9/24	Wed 25/9/24	Wed 25/9/24	0 days	Concrete gang	0 days
289	Excavation and Lateral Support	Thu 25/9/25	Thu 25/10/21	27 days	Excavation and Lateral Support	0 days	Thu 25/9/25	Thu 25/10/21	Thu 25/9/25	Thu 25/10/21	0 days	Lx Excavator	0 days
290	Excavation and Lateral Support	Thu 25/9/25	Thu 25/10/2	8 days	Excavation and Lateral Support	0 days	Thu 25/9/25	Thu 25/10/2	Thu 25/9/25	Thu 25/10/2	0 days	Lx Excavator	0 days
291	Formwork Erection	Wed 25/10/1	Wed 25/10/12	12 days	Formwork Erection	0 days	Wed 25/10/1	Wed 25/10/12	Wed 25/10/1	Wed 25/10/12	0 days	Zx carpenter	0 days
292	Catchpit construction	Sat 25/10/11	Sat 25/10/21	11 days	Catchpit construction	0 days	Sat 25/10/11	Sat 25/10/21	Sat 25/10/11	Sat 25/10/21	0 days	Zx carpenter	0 days
293	Concrete	Mon 25/10/20	Mon 25/10/20	1 day	Concrete	0 days	Mon 25/10/20	Mon 25/10/20	Mon 25/10/20	Mon 25/10/20	0 days	Concrete gang	0 days
294	End-SHT,CP3.5,300->450CU(G).L=107.7	Thu 25/10/21	Thu 25/12/16	57 days	End-SHT,CP3.5,300->450CU(G).L=107.7	0 days	Thu 25/10/21	Thu 25/12/16	Thu 25/10/21	Thu 25/12/16	0 days	Lx Excavator	0 days
295	Excavation and Lateral Support	Thu 25/10/21	Thu 25/11/18	29 days	Excavation and Lateral Support	0 days	Thu 25/10/21	Thu 25/11/18	Thu 25/10/21	Thu 25/11/18	0 days	Lx Excavator	0 days
296	Excavation and Lateral Support	Thu 25/10/21	Thu 25/10/30	10 days	Excavation and Lateral Support	0 days	Thu 25/10/21	Thu 25/10/30	Thu 25/10/21	Thu 25/10/30	0 days	Lx Excavator	0 days
297	Formwork Erection	Wed 25/10/29	Sun 25/11/9	12 days	Formwork Erection	0 days	Wed 25/10/29	Sun 25/11/9	Wed 25/10/29	Sun 25/11/9	0 days	Zx carpenter	0 days
298	Catchpit construction	Sat 25/11/8	Thu 25/11/18	12 days	Catchpit construction	0 days	Sat 25/11/8	Thu 25/11/18	Sat 25/11/8	Thu 25/11/18	0 days	Lx Excavator	0 days
299	Concrete	Mon 25/11/17	Mon 25/11/17	1 day	Concrete	0 days	Mon 25/11/17	Mon 25/11/17	Mon 25/11/17	Mon 25/11/17	0 days	Concrete gang	0 days
300	Stage 2	Mon 25/11/17	Mon 25/11/17	29 days	Stage 2	0 days	Mon 25/11/17	Mon 25/11/17	Mon 25/11/17	Mon 25/11/17	0 days	Lx Excavator	0 days
301	Excavation and Lateral Support	Thu 25/11/27	Thu 25/11/27	10 days	Excavation and Lateral Support	0 days	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	Thu 25/11/27	0 days	Lx Excavator	0 days
302	Formwork Erection	Wed 25/11/26	Sun 25/12/7	12 days	Formwork Erection	0 days	Wed 25/11/26	Sun 25/12/7	Wed 25/11/26	Sun 25/12/7	0 days	Zx carpenter	0 days
303	Catchpit construction	Thu 25/12/6	Thu 25/12/6	11 days	Catchpit construction	0 days	Thu 25/12/6	Thu 25/12/6	Thu 25/12/6	Thu 25/12/6	0 days	Lx Excavator	0 days
304	Concrete	Mon 25/12/15	Mon 25/12/15	1 day	Concrete	0 days	Mon 25/12/15	Mon 25/12/15	Mon 25/12/15	Mon 25/12/15	0 days	Concrete gang	0 days
305	End-SHT,CP3.5,300->450CU(G).L=107.7	Thu 25/12/16	Thu 25/12/16	113 days	End-SHT,CP3.5,300->450CU(G).L=107.7	0 days	Thu 25/12/16	Thu 25/12/16	Thu 25/12/16	Thu 25/12/16	0 days	Lx Excavator	0 days
306	Excavation and Lateral Support	Thu 25/12/16	Thu 25/12/25	10 days	Excavation and Lateral Support	0 days	Thu 25/12/16	Thu 25/12/25	Thu 25/12/16	Thu 25/12/25	0 days	Lx Excavator	0 days
307	Formwork Erection	Wed 25/12/16	Thu 25/12/24	12 days	Formwork Erection	0 days	Wed 25/12/16	Thu 25/12/24	Wed 25/12/16	Thu 25/12/24	0 days	Zx carpenter	0 days
308	Formwork Erection	Sat 26/1/4	Sun 26/1/4	12 days	Formwork Erection	0 days	Sat 26/1/4	Sun 26/1/4	Sat 26/1/4	Sun 26/1/4	0 days	Lx Excavator	0 days
309	Catchpit construction	Thu 26/1/3	Thu 26/1/3	11 days	Catchpit construction	0 days	Thu 26/1/3	Thu 26/1/3	Thu 26/1/3	Thu 26/1/3	0 days	Lx Excavator	0 days
310	Concrete	Mon 26/1/12	Mon 26/1/12	1 day	Concrete	0 days	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	Mon 26/1/12	0 days	Concrete gang	0 days
311	Stage 2	Thu 26/1/13	Thu 26/2/10	29 days	Stage 2	0 days	Thu 26/1/13	Thu 26/2/10	Thu 26/1/13	Thu 26/2/10	0 days	Lx Excavator	0 days
312	Excavation and Lateral Support	Thu 26/1/13	Thu 26/1/22	10 days	Excavation and Lateral Support	0 days	Thu 26/1/13	Thu 26/1/22	Thu 26/1/13	Thu 26/1/22	0 days	Lx Excavator	0 days
313	Formwork Erection	Wed 26/1/21	Sun 26/2/1	12 days	Formwork Erection	0 days	Wed 26/1/21	Sun 26/2/1	Wed 26/1/21	Sun 26/2/1	0 days	Zx carpenter	0 days
314	Catchpit construction	Thu 26/2/10	Thu 26/2/10	11 days	Catchpit construction	0 days	Thu 26/2/10	Thu 26/2/10	Thu 26/2/10	Thu 26/2/10	0 days	Lx Excavator	0 days
315	Concrete	Mon 26/2/9	Mon 26/2/9	1 day	Concrete	0 days	Mon 26/2/9	Mon 26/2/9	Mon 26/2/9	Mon 26/2/9	0 days	Concrete gang	0 days
316	Stage 3	Thu 26/2/10	Thu 26/3/10	29 days	Stage 3	0 days	Thu 26/2/10	Thu 26/3/10	Thu 26/2/10	Thu 26/3/10	0 days	Lx Excavator	0 days
317	Excavation and Lateral Support	Thu 26/2/10	Thu 26/2/19	10 days	Excavation and Lateral Support	0 days	Thu 26/2/10	Thu 26/2/19	Thu 26/2/10	Thu 26/2/19	0 days	Lx Excavator	0 days
318	Formwork Erection	Wed 26/2/18	Sun 26/3/1	12 days	Formwork Erection	0 days	Wed 26/2/18	Sun 26/3/1	Wed 26/2/18	Sun 26/3/1	0 days	Zx carpenter	0 days
319	Catchpit construction	Thu 26/3/10	Thu 26/3/10	11 days	Catchpit construction	0 days	Thu 26/3/10	Thu 26/3/10	Thu 26/3/10	Thu 26/3/10	0 days	Lx Excavator	0 days
320	Concrete	Mon 26/3/9	Mon 26/3/9	1 day	Concrete	0 days	Mon 26/3/9	Mon 26/3/9	Mon 26/3/9	Mon 26/3/9	0 days	Concrete gang	0 days
321	Stage 4	Thu 26/3/10	Thu 26/4/7	19 days	Stage 4	0 days	Thu 26/3/10	Thu 26/4/7	Thu 26/3/10	Thu 26/4/7	0 days	Lx Excavator	0 days
322	Excavation and Lateral Support	Thu 26/3/10	Thu 26/3/19	10 days	Excavation and Lateral Support	0 days	Thu 26/3/10	Thu 26/3/19	Thu 26/3/10	Thu 26/3/19	0 days	Lx Excavator	0 days
323	Formwork Erection	Wed 26/3/18	Sun 26/3/29	12 days	Formwork Erection	0 days	Wed 26/3/18	Sun 26/3/29	Wed 26/3/18	Sun 26/3/29	0 days	Zx carpenter	0 days
324	Catchpit construction	Thu 26/4/7	Thu 26/4/7	11 days	Catchpit construction	0 days	Thu 26/4/7	Thu 26/4/7	Thu 26/4/7	Thu 26/4/7	0 days	Lx Excavator	0 days
325	Concrete	Mon 26/4/6	Mon 26/4/6	1 day	Concrete	0 days	Mon 26/4/6	Mon 26/4/6	Mon 26/4/6	Mon 26/4/6	0 days	Concrete gang	0 days
326	U-Channel Works (East)	Sat 26/4/6	Sat 26/4/6	30 days	U-Channel Works (East)	0 days	Sat 26/4/6	Sat 26/4/6	Sat 26/4/6	Sat 26/4/6	0 days	Lx Excavator	0 days
327	Excavation and Lateral Support	Sat 26/4/13	Sun 26/4/13	11 days	Excavation and Lateral Support	0 days	Sat 26/4/13	Sun 26/4/13	Sat 26/4/13	Sun 26/4/13	0 days	Lx Excavator	0 days
328	Excavation and Lateral Support	Thu 26/9/24	Thu 26/9/24	11 days	Excavation and Lateral Support	0 days	Thu 26/9/24	Thu 26/9/24	Thu 26/9/24	Thu 26/9/24	0 days	Lx Excavator	0 days
329	Formwork Erection	Fri 26/10/4	Mon 26/10/23	12 days	Formwork Erection	0 days	Fri 26/10/4	Mon 26/10/23	Fri 26/10/4	Mon 26/10/23	0 days	Zx carpenter	0 days
330	Catchpit construction	Thu 26/10/3	Thu 26/10/3	11 days	Catchpit construction	0 days	Thu 26/10/3	Thu 26/10/3	Thu 26/10/3	Thu 26/10/3	0 days	Lx Excavator	0 days
331	Concrete	Sat 26/10/12	Sat 26/10/12	1 day	Concrete	0 days	Sat 26/10/12	Sat 26/10/12	Sat 26/10/12	Sat 26/10/12	0 days	Concrete gang	0 days
332	SHT,CP10E-SHT,CP10D,750CU(HD-G).L=23.7	Sun 26/10/13	Sun 26/10/13	36 days	SHT,CP10E-SHT,CP10D,750CU(HD-G).L=23.7	0 days	Sun 26/10/13	Sun 26/10/13	Sun 26/10/13	Sun 26/10/13	0 days	Lx Excavator	0 days
333	Excavation and Lateral Support	Fri 26/10/25	Fri 26/10/25	13 days	Excavation and Lateral Support	0 days	Fri 26/10/25	Fri 26/10/25	Fri 26/10/25	Fri 26/10/25	0 days	Lx Excavator	0 days
334	Formwork Erection	Wed 26/10/24	Thu 26/11/6	14 days	Formwork Erection	0 days	Wed 26/10/24	Thu 26/11/6	Wed 26/10/24	Thu 26/11/6	0 days	Zx carpenter	0 days
335	Catchpit construction	Thu 26/11/7	Thu 26/11/7	13 days	Catchpit construction	0 days	Thu 26/11/7	Thu 26/11/7	Thu 26/11/7	Thu 26/11/7	0 days	Lx Excavator	0 days
336	Concrete	Sat 26/11/16	Sat 26/11/16	1 day	Concrete	0 days	Sat 26/11/16	Sat 26/11/16	Sat 26/11/16	Sat 26/11/16	0 days	Concrete gang	0 days
337	SHT,CP10D-SHT,CP10C,750CU(HD-G).L=11.9	Sun 26/11/17	Sun 26/11/17	24 days	SHT,CP10D-SHT,CP10C,750CU(HD-G).L=11.9	0 days	Sun 26/11/17	Sun 26/11/17	Sun 26/11/17	Sun 26/11/17	0 days	Lx Excavator	0 days
338	Excavation and Lateral Support	Sun 26/11/24	Sun 26/11/24	8 days	Excavation and Lateral Support	0 days	Sun 26/11/24	Sun 26/11/24	Sun 26/11/24	Sun 26/11/24	0 days	Lx Excavator	0 days
339	Formwork Erection	Mon 26/12/3	Mon 26/12/3	10 days	Formwork Erection	0 days	Mon 26/12/3	Mon 26/12/3	Mon 26/12/3	Mon 26/12/3	0 days	Zx carpenter	0 days
340	Catchpit construction	Sun 26/12/1	Sun 26/12/1	10 days	Catchpit construction	0 days	Sun 26/12/1	Sun 26/12/1	Sun 26/12/1	Sun 26/12/1	0 days	Lx Excavator	0 days
341	Concrete	Mon 26/12/9	Mon 26/12/9	1 day	Concrete	0 days	Mon 26/12/9	Mon 26/12/9	Mon 26/12/9	Mon 26/12/9	0 days	Concrete gang	0 days
342	SHT,CP10C-SHT,CP10B,750CU(HD-G).L=6.5	Thu 26/12/10	Thu 26/12/10	17 days	SHT,CP10C-SHT,CP10B,750CU(HD-G).L=6.5	0 days	Thu 26/12/10	Thu 26/12/10	Thu 26/12/10	Thu 26/12/10	0 days	Lx Excavator	0 days
343	Excavation and Lateral Support	Sun 26/12/15	Sun 26/12/15	6 days	Excavation and Lateral Support	0 days	Sun 26/12/15	Sun 26/12/15	Sun 26/12/15	Sun 26/12/15	0 days	Lx Excavator	0 days
344	Formwork Erection	Sat 26/12/21	Sat 26/12/21	7 days	Formwork Erection	0 days	Sat 26/12/21	Sat 26/12/21	Sat 26/12/21	Sat 26/12/21	0 days	Zx carpenter	0 days
345	Catchpit construction	Thu 26/12/26	Thu 26/12/26	7 days	Catchpit construction	0 days	Thu 26/12/26	Thu 26/12/26	Thu 26/12/26	Thu 26/12/26	0 days	Lx Excavator	0 days
346	Concrete	Wed 26/12/25	Wed 26/12/25	1 day	Concrete	0 days	Wed 26/12/25	Wed 26/12/25	Wed 26/12/25	Wed 26/12/25	0 days	Concrete gang	0 days
347	SHT,CP10B-SHT,CP10A,750CU(HD-G).L=6.4	Thu 26/12/26	Thu 26/12/26	17 days	SHT,CP10B-SHT,CP10A,750CU(HD-G).L=6.4	0 days	Thu 26/12/26	Thu 26/12/26	Thu 26/12/26	Thu 26/12/26	0 days	Lx Excavator	0 days
348	Excavation and Lateral Support	Tue 26/12/31	Tue 26/12/31	6 days	Excavation and Lateral Support	0 days	Tue 26/12/31	Tue 26/12/31	Tue 26/12/31	Tue 26/12/31	0 days	Lx Excavator	0 days
349	Formwork Erection	Mon 26/1/6	Mon 26/1/6	8 days	Formwork Erection	0 days	Mon 26/1/6	Mon 26/1/6	Mon 26/1/6	Mon 26/1/6	0 days	Zx carpenter	0 days
350	Catchpit construction	Sun 25/1/5	Sat 25/1/11	7 days	Catchpit construction	0 days	Sun 25/1/5	Sat 25/1/11	Sun 25/1/5	Sat 25/1/11	0 days	Lx Excavator	0 days
351	Concrete	Fri 25/1/10	Fri 25/1/10	1 day	Concrete	0 days	Fri 25/1/10	Fri 25/1/10	Fri 25/1/10	Fri 25/1/10	0 days	Concrete gang	0 days
352	SHT,CP10A-SHT,CP10,750CU(HD-G).L=26.7	Tue 25/1/11	Tue 25/1/11	39 days	SHT,CP10A-SHT,CP10,750CU(HD-G).L=26.7	0 days	Tue 25/1/11	Tue 25/1/11	Tue 25/1/11	Tue 25/1/11	0 days	Lx Excavator	0 days
353	Excavation and Lateral Support	Sat 25/1/24	Fri 25/1/24	14 days	Excavation and Lateral Support	0 days	Sat 25/1/24	Fri 25/1/24	Sat 25/1/24	Fri 25/1/24	0 days	Lx Excavator	0 days
354	Formwork Erection	Thu 25/2/3	Thu 25/2/3	15 days	Formwork Erection	0 days	Thu 25/2/3	Thu 25/2/3	Thu 25/2/3	Thu 25/2/3	0 days	Zx carpenter	0 days
355	Catchpit construction	Tue 25/2/5	Tue 25/2/5	14 days	Catchpit construction	0 days	Tue 25/2/5	Tue 25/2/5	Tue 25/2/5	Tue 25/2/5	0 days	Lx Excavator	0 days
356	Concrete	Mon 25/2/17	Mon 25/2/17	1 day	Concrete	0 days	Mon 25/2/17	Mon 25/2/17	Mon 25/2/17	Mon 25/2/17	0 days	Concrete gang	0 days
357	SHT,CP10-SHT,CP9,750CU(HD-G).L=4.3	Tue 25/2/18	Tue 25/2/18	17 days	SHT,CP10-SHT,CP9,750CU(HD-G).L=4.3	0 days	Tue 25/2/18	Tue 25/2/18	Tue 25/2/18	Tue 25/2/18	0 days	Lx Excavator	0 days
358	Excavation and Lateral Support	Tue 25/2/18	Sun 25/2/23	6 days	Excavation and Lateral Support	0 days	Tue 25/2/18	Sun 25/2/23	Tue 25/2/18	Sun 25/2/23	0 days	Lx Excavator	0 days
359	Formwork Erection	Sat 25/2/22	Sat 25/3/1	8 days	Formwork Erection	0 days	Sat 25/2/22	Sat 25/3/1	Sat 25/2/22	Sat 25/3/1	0 days	Zx carpenter	0 days
360	Catchpit construction	Thu 25/2/28	Thu 25/3/6	7 days	Catchpit construction	0 days	Thu 25/2/28	Thu 25/3/6	Thu 25/2/28	Thu 25/3/6	0 days	Lx Excavator	0 days
361	Concrete	Wed 25/3/5	Wed 25/3/5	1 day	Concrete								

Calendar grid showing months from 2022 Half 1 to 2026 Half 2.

Main project schedule table with columns for ID, Task Name, Duration, Start, Early Start, Late Start, Late Finish, Total Slack, TR, Predecessors, and various task status metrics.



Summary of project metrics: Revision: 1.20, Date: 31 August 2024, and a legend for task types including Milestone, Progress, and Critical Task.
