

WING TAT CIVIL ENGINEERING CO LTD

CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2

PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Total Slack	Predecessors
1	Starting date	Mon 23/5/29	Earlier Than	1 day	Mon 23/5/29	Mon 23/5/29	-5 days	
2	Access date	NA	As Possible	270 days	Mon 23/5/29	Fri 24/2/23	1132 days	
3	Portion A	NA	As Possible	270 days	Tue 23/5/30	Fri 24/2/23	1132 days	1
4	Portion B	NA	As Possible	210 days	Tue 23/5/30	Mon 23/12/25	1192 days	1
5	Portion C1 & C2	NA	As Possible	270 days	Tue 23/5/30	Fri 24/2/23	1132 days	1
6	Portion C3	NA	As Possible	0 days	Mon 23/5/29	Mon 23/5/29	1402 days	1
7	Portion D	NA	As Possible	210 days	Tue 23/5/30	Mon 23/12/25	1192 days	1
8	Portion E1	NA	As Possible	0 days	Mon 23/5/29	Mon 23/5/29	1402 days	1
9	Portion E2	NA	As Possible	270 days	Tue 23/5/30	Fri 24/2/23	1132 days	1
10	Completion Date (Extended as accepted)	NA	As Possible	1166.5 days	Tue 23/5/30	Sat 26/8/8	-5 days	
11	Section I - Drainage Improvement Works at Sung Shan New Village	Thu 26/5/28	Later Than	1095 days	Tue 23/5/30	Thu 26/5/28	0 days	1
12	Section II - Drainage Improvement Works at Tai Wo	Tue 25/8/26	Later Than	820 days	Tue 23/5/30	Tue 25/8/26	0 days	1
13	Section III - Drainage Improvement Works at Lin Fa Tei (except flood wall construction and drainage improvement works along Kam Sheung Road)	NA	As Soon As Possible	1166.5 days	Tue 23/5/30	Sat 26/8/8	-3 days	
14	Original	NA	As Possible	1155 days	Tue 23/5/30	Mon 26/7/27	-3 days	1
15	EOT - Indement weather Cl. 60.1(13)(iv)(v)	Sat 26/8/8	Later Than	11.5 days	Tue 26/7/28	Sat 26/8/8	-3 days	14
16	Section IV - Drainage Improvement Works at Ha Che (except pipe laying works by trenchless method and pipe rehabilitation works across Fan Kam Road)	NA	As Soon As Possible	1108.5 days	Tue 23/5/30	Thu 26/6/11	-5 days	
17	Original	NA	As Possible	1095 days	Tue 23/5/30	Thu 26/5/28	-5 days	1
18	EOT - Indement weather Cl. 60.1(13)(iv)(v)	Thu 26/6/11	Later Than	13.5 days	Fri 26/5/29	Thu 26/6/11	-5 days	17
19	Section V - Drainage Improvement Works at Shan Ha Tsuen	NA	As Possible	982 days	Tue 23/5/30	Wed 26/2/4	-5 days	
20	Original	NA	As Possible	973 days	Tue 23/5/30	Mon 26/1/26	-5 days	1
21	EOT - Indement weather Cl. 60.1(13)(iv)(v)	Wed 26/2/4	Later Than	9 days	Tue 26/1/27	Wed 26/2/4	-5 days	20
22	Section VI - Flood Wall Construction and Drainage Improvement Works along Kam Sheung Road at Lin Fa Tei	Tue 25/8/26	Finish No Later Than	820 days	Tue 23/5/30	Tue 25/8/26	0 days	1
23	Section VII - Pipe Laying Works by Trenchless Method and Pipe Rehabilitation Works across Fan Kam Road and Upstream Channel and Downstream Box Culvert Construction Works (Chainage 626.224m - 678.859m) at Ha Che	Tue 25/8/26	Finish No Later Than	820 days	Tue 23/5/30	Tue 25/8/26	0 days	1
44	Planned Completion Day of whole of the works	NA	As Possible	582 days	Tue 25/8/26	Wed 27/3/31	0 days	
45	Section I - Drainage Improvement Works at Sung Shan New Village	NA	As Possible	280 days	Fri 26/5/29	Thu 27/3/4	0 days	
46	EOT - Indement weather (anticipated upto 31 Jul 2024)	Thu 26/8/6	Later Than	70 days	Fri 26/5/29	Thu 26/8/6	0 days	11
47	EOT - Uncharted/Retained Trees obstructing the works	Sun 27/1/3	Later Than	150 days	Fri 26/8/7	Sun 27/1/3	0 days	46
48	EOT - Obstruction to Sheet Piling at CHA50 - CHA280	Thu 27/3/4	Later Than	60 days	Mon 27/1/4	Thu 27/3/4	0 days	47
49	Section II - Drainage Improvement Works at Tai Wo	NA	As Possible	582 days	Wed 25/8/27	Wed 27/3/31	0 days	
50	EOT - Blockade of access by others	Wed 27/3/31	Later Than	582 days	Wed 25/8/27	Wed 27/3/31	0 days	12
51	Section III - Drainage Improvement Works at Lin Fa Tei (except flood wall construction and drainage improvement works along Kam Sheung Road)	NA	As Soon As Possible	615 days	Wed 26/8/5	Mon 26/10/5	0 days	
52	EOT - Indement weather (anticipated upto 31 Jul 2024)	Mon 26/10/5	Later Than	61.5 days	Wed 26/8/5	Mon 26/10/5	-3 days	13
53	Section IV - Drainage Improvement Works at Ha Che (except pipe laying works by trenchless method and pipe rehabilitation works across Fan Kam Road)	NA	As Soon As Possible	271.5 days	Sat 26/6/6	Thu 27/3/4	0 days	
54	EOT - Indement weather (anticipated upto 31 Jul 2024)	Thu 26/8/6	Later Than	61.5 days	Sat 26/6/6	Thu 26/8/6	-5 days	16
55	EOT - Additional request from landlord of HC06.07	Sun 27/1/3	Later Than	150 days	Fri 26/8/7	Sun 27/1/3	0 days	54
56	EOT - Additional Trees behind Arbutus of HC04	Thu 27/3/4	Later Than	60 days	Mon 27/1/4	Thu 27/3/4	0 days	55
57	Section V - Drainage Improvement Works at Shan Ha Tsuen	NA	As Possible	66 days	Sat 26/1/31	Mon 26/4/6	0 days	
58	EOT - Indement weather (anticipated upto 31 Jul 2024)	Mon 26/4/6	Later Than	66 days	Sat 26/1/31	Mon 26/4/6	-5 days	19
59	Section VI - Flood Wall Construction and Drainage Improvement Works along Kam Sheung Road at Lin Fa Tei	NA	As Soon As Possible	400 days	Wed 25/8/27	Wed 26/9/30	0 days	
60	EOT - Difficulty/infeasibility for construction of 1650mm dia. pipe at Kam Sheur	Wed 26/9/30	Later Than	400 days	Wed 25/8/27	Wed 26/9/30	0 days	22
61	Section VII - Pipe Laying Works by Trenchless Method and Pipe Rehabilitation Works across Fan Kam Road and Upstream Channel and Downstream Box Culvert Construction Works (Chainage 626.224m - 678.859m) at Ha Che	NA	As Soon As Possible	0 days	Tue 25/8/26	Tue 25/8/26	582 days	23
62								
63	Project establishment	NA	As Possible	307 days	Mon 23/5/15	Sat 24/3/16	0 days	
64	Project Manager's Accommodation	NA	As Possible	209 days	Mon 23/8/21	Sat 24/3/16	1110 days	1FS-1 day
65	PMI001 - Possession of Works Area at 22 Fan Kam road [A]	Fri 23/9/1	Earlier Than	1 day	Fri 23/9/1	Fri 23/9/1	1110 days	
66	Renovation and Certification of ex. PM accommodation	NA	As Possible	197 days	Sat 23/9/2	Sat 24/3/16	1110 days	
67	Inspection and review of ex. PM accommodation [A]	NA	As Possible	100 days	Sat 23/9/2	Sun 23/12/10	1110 days	65
68	Arranging time slot with RSS for power and server down [A]	NA	As Possible	83 days	Mon 23/12/11	Sat 24/3/2	1110 days	67
69	Issuance of check certificates [A]	NA	As Possible	14 days	Sun 24/3/3	Sat 24/3/16	1110 days	68
70	C11 Tendering procedure for EDMS & DWSS [A]	Mon 23/8/21	Earlier Than	30 days	Mon 23/8/21	Tue 23/9/19	1249 days	
71	Installation and commissioning of EDMS & DWSS [A]	NA	As Possible	40 days	Wed 23/9/20	Sun 23/10/29	1249 days	70
72	Environmental Team (ET) procurement	NA	As Possible	190 days	Tue 23/8/15	Tue 24/2/20	0 days	
73	C9 Tendering procedure [A]	Tue 23/8/15	Earlier Than	58 days	Tue 23/8/15	Wed 23/10/11	0 days	
74	Commencement for ET (Aurecon) [A]	NA	As Possible	1 day	Thu 23/10/12	Thu 23/10/12	0 days	73
75	Proposal and Acceptance of ET Members [A]	NA	As Possible	18 days	Fri 23/10/13	Mon 23/10/30	0 days	74
76	Updating and Acceptance of EM&A Manual [A]	NA	As Possible	23 days	Tue 23/10/31	Wed 23/11/22	0 days	75
77	Notice of Commencement of Construction to EPD [A]	NA	As Possible	90 days	Thu 23/11/23	Tue 24/2/20	0 days	76
78	Complete necessary submissions to EPD [A]	NA	As Possible	20 days	Thu 24/2/1	Tue 24/2/20	1135 days	77FF
83	Setup Public Liaison Team	NA	As Possible	120 days	Mon 23/5/15	Mon 23/9/11	0 days	
84	Recruitment of Public Liaison Officer [A]	NA	As Possible	90 days	Mon 23/5/15	Sat 23/8/12	0 days	
85	Appointment and Acceptance of Public Liaison Officer [A]	NA	As Possible	30 days	Sun 23/8/13	Mon 23/9/11	0 days	84
93	Works Area establishment	NA	As Possible	44 days	Fri 23/9/1	Sat 23/10/14	15 days	
94	PMI001 - Possession of Works Area at 22 Fan Kam road [A]	Fri 23/9/1	Earlier Than	1 day	Fri 23/9/1	Fri 23/9/1	15 days	
95	Establish concrete haul road and slab [A]	NA	As Possible	43 days	Sat 23/9/2	Sat 23/10/14	1264 days	94
96	Contractor's Accommodation (office and welfare facilities)	NA	As Possible	145 days	Sat 23/9/2	Wed 24/1/24	15 days	
97	Establish temporary site office (containers) [A]	NA	As Possible	24 days	Sat 23/9/2	Mon 23/9/25	15 days	94
105	C9 Tendering procedure for Contractor's Site Office [A]	NA	As Possible	28 days	Sat 23/9/2	Fri 23/9/29	1162 days	94
106	Proposal and Acceptance of Temp. Works Design and Method Statement [A]	NA	As Possible	35 days	Sat 23/9/30	Fri 23/11/3	1162 days	105
107	Construction of Footing [A]	NA	As Possible	15 days	Sat 23/11/4	Sat 23/11/18	1162 days	106
108	Construction of Structure [A]	NA	As Possible	45 days	Sun 23/11/19	Tue 24/1/2	1162 days	107
109	Interior furnishment and Furnitures [A]	NA	As Possible	15 days	Wed 24/1/3	Wed 24/1/17	1162 days	108
110	Move-in [A]	NA	As Possible	7 days	Thu 24/1/18	Wed 24/1/24	1162 days	109
111								
112	Section I	NA	As Possible	1375 days	Tue 23/5/30	Thu 27/3/4	0 days	
2	access date of Portion A	Fri 24/2/23	Later Than	270 days	Tue 23/5/30	Fri 24/2/23	0 days	\\WingTatNasC
3	Period of section I (Sung Shan New Village)	NA	As Possible	1095 days	Tue 23/5/30	Thu 26/5/28	0 days	\\WingTatNasC

Revision.: 18.0

Date: 28 February 2025

Task

Critical Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Critical Task

Rolled Up Milestone

Rolled Up Progress

Split

External Tasks

Project Summary

Group By Summary


Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)


U-Channel: {U/S}~{D/S},size+type,length(m)

Drainage Channel: {U/S}~{D/S}

Page 1

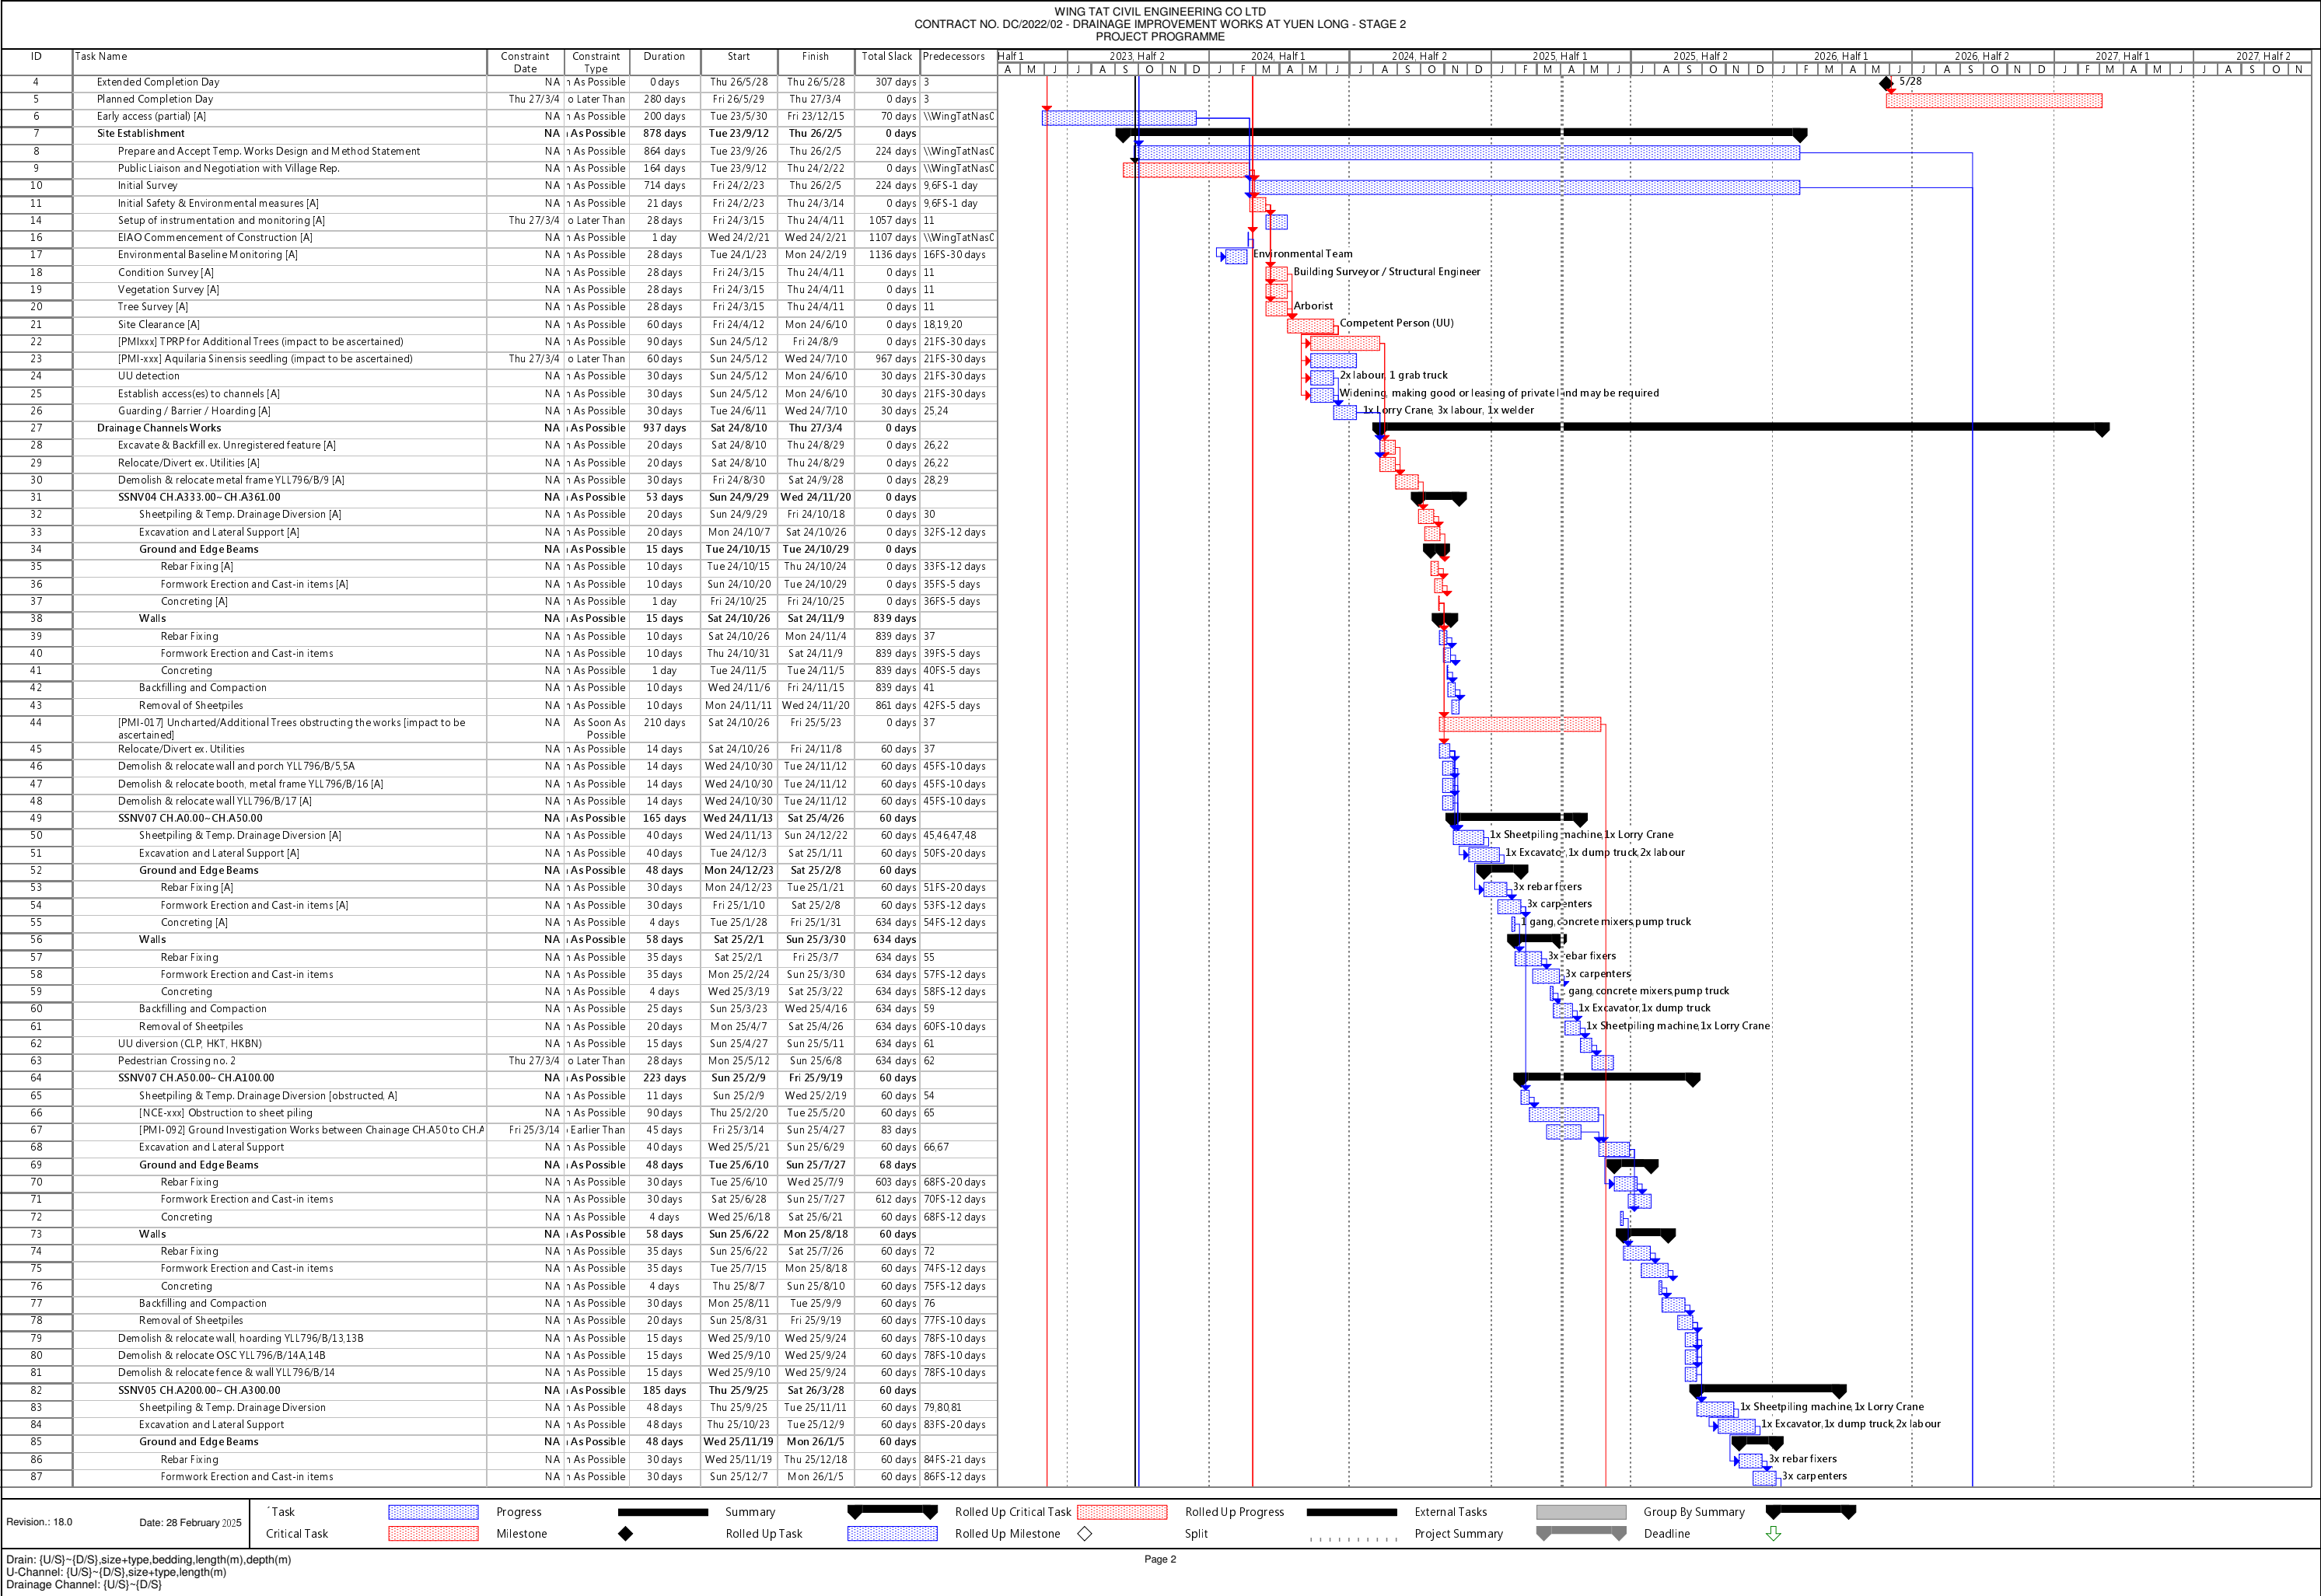

WING TAT CIVIL ENGINEERING CO.LTD																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
PROJECT PROGRAMME																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Total Slack	Predecessors	Half 1	2023 Half 2					2024 Half 1					2024 Half 2					2025 Half 1					2025 Half 2					2026 Half 1					2026 Half 2					2027 Half 1					2027 Half 2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
									A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
88	Concreting	NA	As Possible	4 days	Thu 25/12/25	Sun 25/12/28	60 days	87FS-12 days																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							

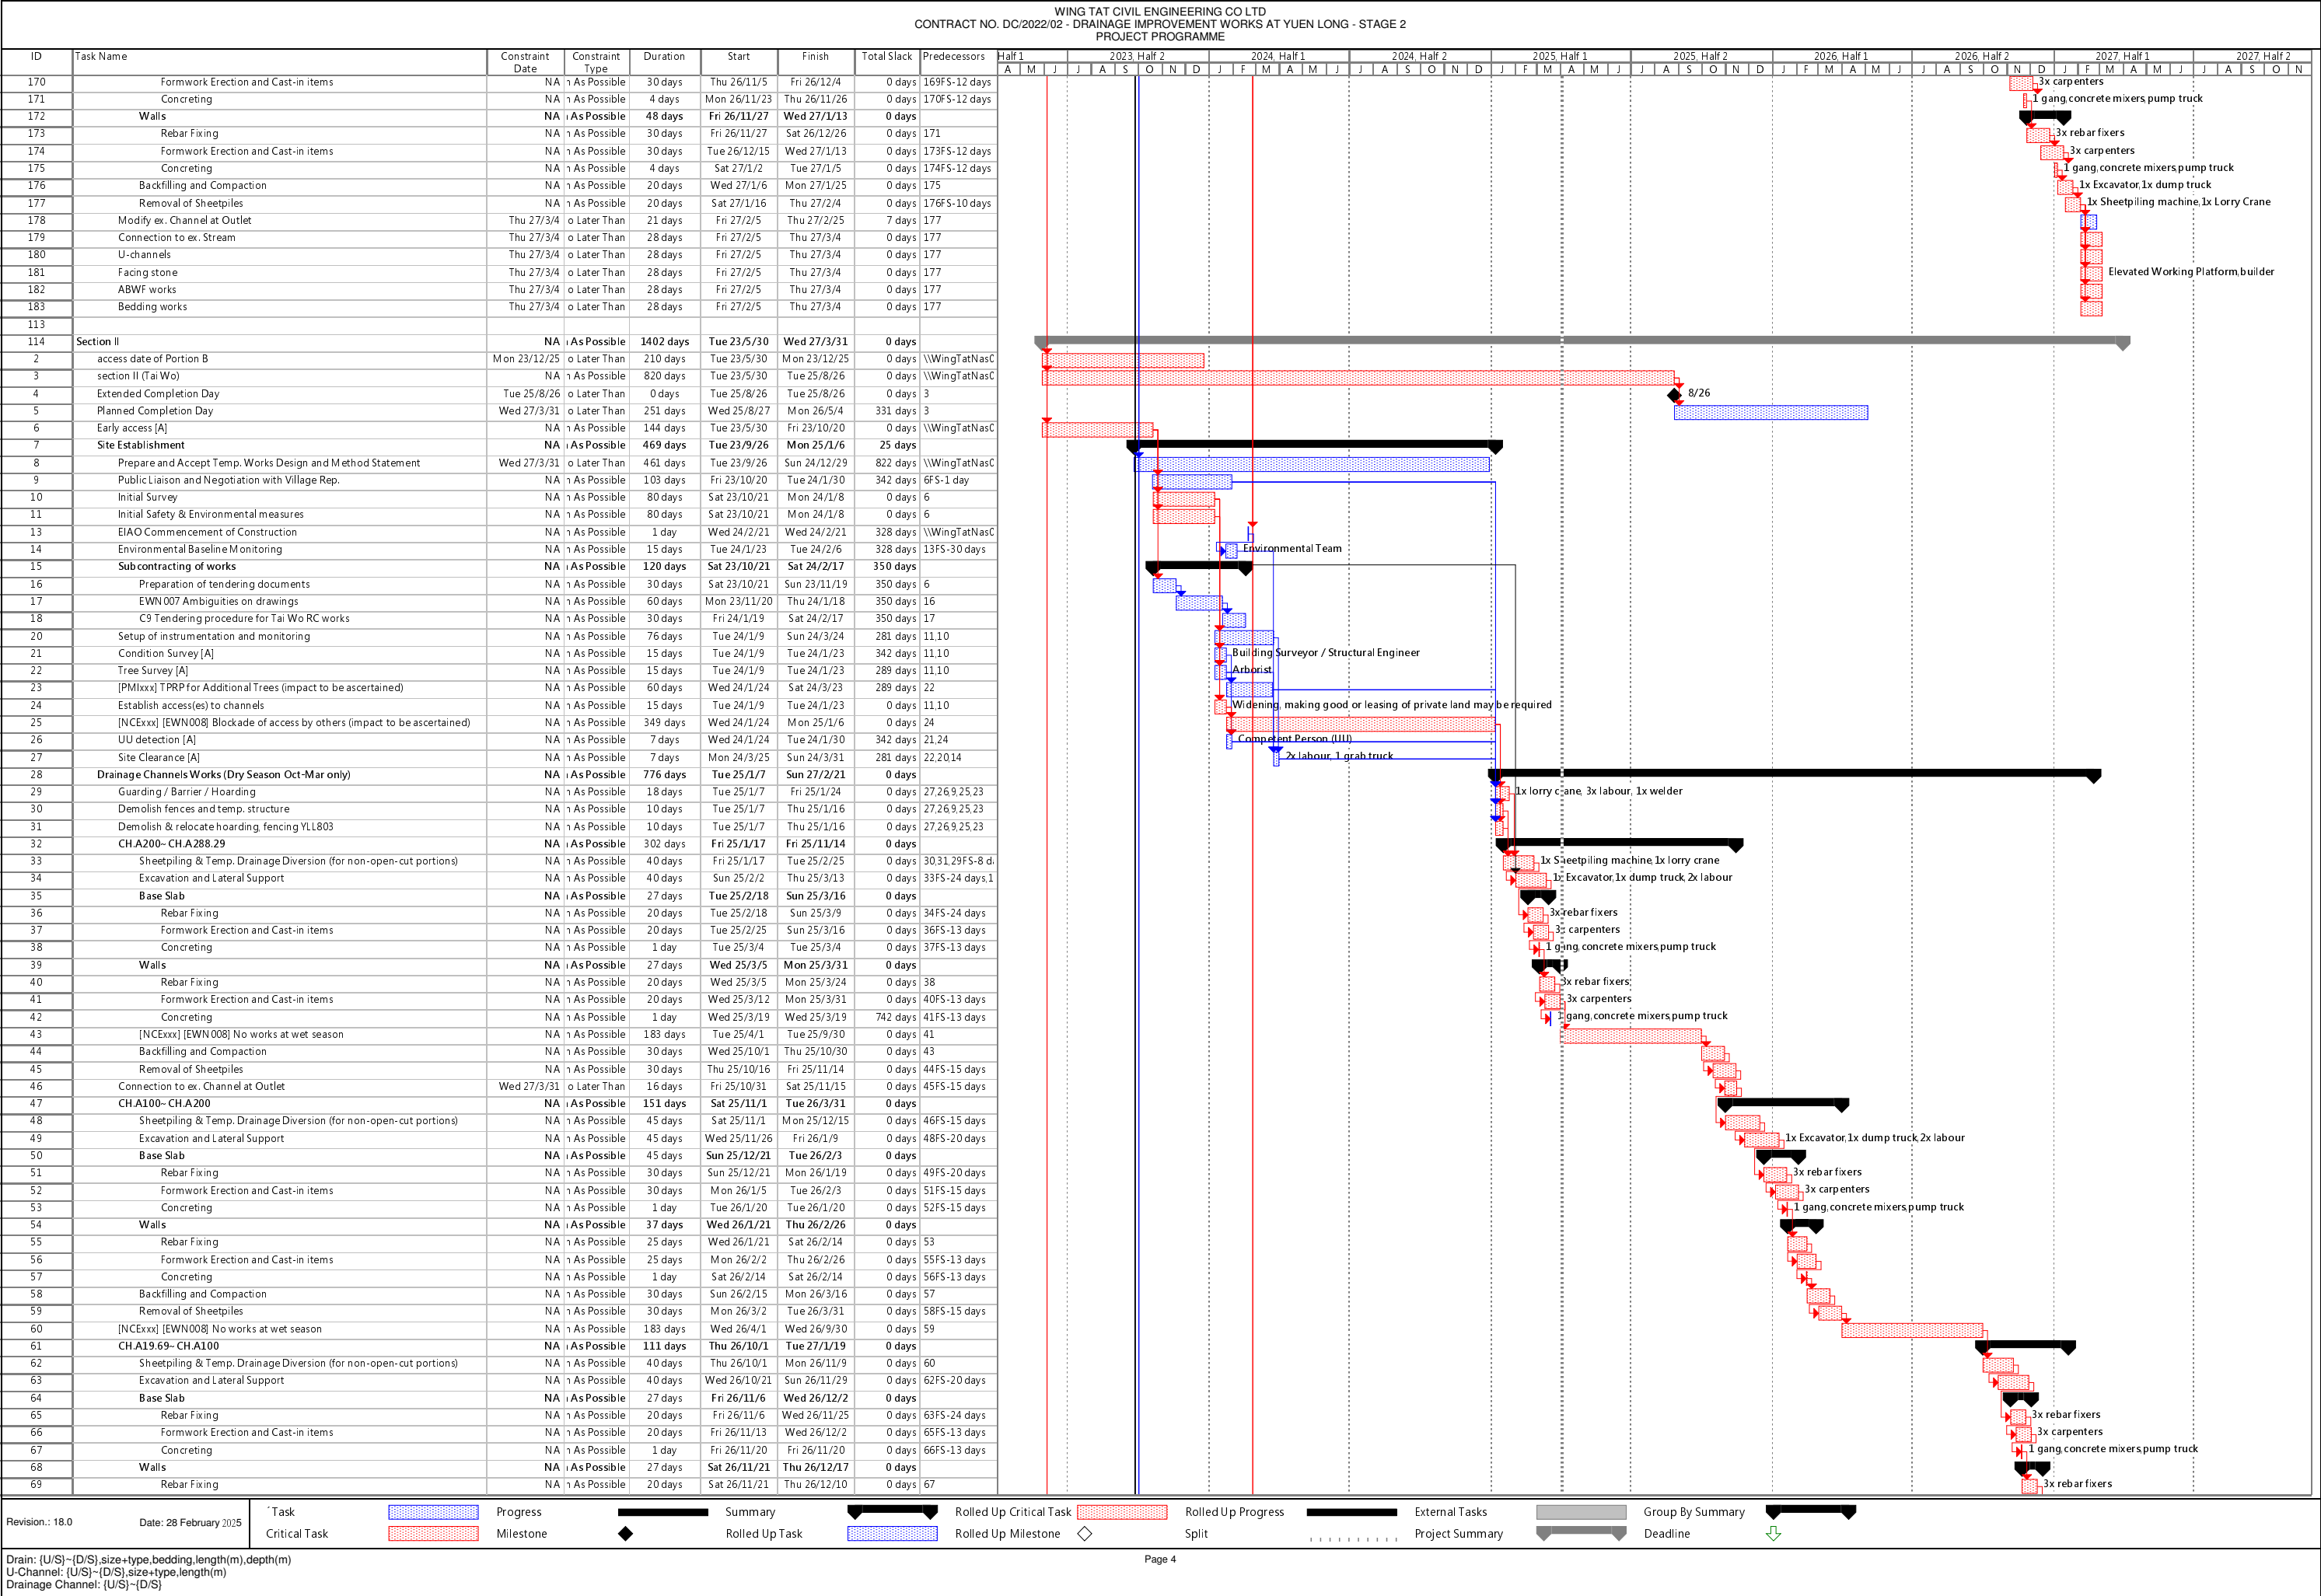

WING TAT CIVIL ENGINEERING CO LTD

CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2

PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Total Slack	Predecessors
70	Formwork Erection and Cast-in items	NA	As Possible	20 days	Sat 26/11/28	Thu 26/12/17	0 days	69FS-13 days
71	Concreting	NA	As Possible	1 day	Sat 26/12/5	Sat 26/12/5	0 days	70FS-13 days
72	Backfilling and Compaction	NA	As Possible	30 days	Sun 26/12/6	Mon 27/1/4	0 days	71
73	Removal of Sheetpiles	NA	As Possible	30 days	Mon 26/12/21	Tue 27/1/19	0 days	72FS-15 days
74	900pipewith flap valve	Wed 27/3/31	Later Than	14 days	Tue 27/1/5	Mon 27/1/18	0 days	73FS-15 days
75	Box Culvert & Pedestrian Crossing	Wed 27/3/31	Later Than	28 days	Thu 27/1/14	Wed 27/2/10	0 days	74FS-5 days
76	ABWF works	Wed 27/3/31	Later Than	21 days	Mon 27/2/1	Sun 27/2/21	38 days	75FS-10 days
77	Bedding works	Wed 27/3/31	Later Than	21 days	Mon 27/2/1	Sun 27/2/21	38 days	75FS-10 days
78	U-Channel Works	NA	As Possible	30 days	Mon 27/2/1	Tue 27/3/2	0 days	
79	CH.A0.00~CH.A16.40,900CU,L=16.40	NA	As Possible	30 days	Mon 27/2/1	Tue 27/3/2	0 days	
80	Excavation and Lateral Support	NA	As Possible	30 days	Mon 27/2/1	Tue 27/3/2	0 days	75FS-10 days
81	Channel Formwork Erection	NA	As Possible	14 days	Tue 27/2/16	Mon 27/3/1	0 days	80FS-15 days
82	Concreting	NA	As Possible	1 day	Mon 27/2/15	Mon 27/2/15	0 days	81FS-15 days
83	Drain Laying Works	NA	As Possible	44 days	Tue 27/2/16	Wed 27/3/31	0 days	
84	CH.A16.40~CH.A19.69,900PC,B,L=3.30,D=1.5	NA	As Possible	44 days	Tue 27/2/16	Wed 27/3/31	0 days	
85	Excavation and Lateral Support	NA	As Possible	30 days	Tue 27/2/16	Wed 27/3/17	0 days	82
86	Drain Laying	NA	As Possible	20 days	Wed 27/3/3	Mon 27/3/22	0 days	85FS-15 days
87	Bedding and Backfilling	NA	As Possible	14 days	Sat 27/3/13	Fri 27/3/26	0 days	86FS-10 days
88	Reinstatement	Wed 27/3/31	Later Than	10 days	Mon 27/3/22	Wed 27/3/31	0 days	87FS-5 days
115								
116	Section III	NA	As Possible	1225 days	Tue 23/5/30	Mon 26/10/5	0 days	
2	access date of Portion C1 & C2	Fri 24/2/23	Later Than	270 days	Tue 23/5/30	Fri 24/2/23	0 days	\\WingTatNasC
3	section III (Lin Fa Tei)	NA	As Possible	1155 days	Tue 23/5/30	Mon 26/7/27	0 days	\\WingTatNasC
4	Extended Completion Day	Sat 26/8/8	Later Than	11.5 days	Tue 26/7/28	Sat 26/8/8	0 days	3
5	Planned Completion Day	Mon 26/10/5	Later Than	70 days	Tue 26/7/28	Mon 26/10/5	0 days	3
6	Early access (partial) [A]	NA	As Possible	200 days	Tue 23/5/30	Fri 23/12/15	70 days	\\WingTatNasC
7	Site Establishment	NA	As Possible	989 days	Tue 23/9/12	Wed 26/5/27	0 days	
8	Prepare and Accept Temp. Works Design and Method Statement	NA	As Possible	975 days	Tue 23/9/26	Wed 26/5/27	35 days	\\WingTatNasC
9	Public Liaison and Negotiation with Village Rep. [A]	NA	As Possible	164 days	Tue 23/9/12	Thu 24/2/22	0 days	\\WingTatNasC
10	Initial Survey	NA	As Possible	825 days	Fri 24/2/23	Wed 26/5/27	35 days	9.6FS-1 day
12	Initial Safety & Environmental measures [A]	NA	As Possible	14 days	Fri 24/2/23	Thu 24/3/7	0 days	9.6FS-1 day
14	EIAO Commencement of Construction [A]	NA	As Possible	28 days	Wed 24/2/21	Tue 24/3/19	930 days	\\WingTatNasC
16	Environmental Baseline Monitoring [A]	NA	As Possible	15 days	Mon 24/2/19	Mon 24/3/4	1122 days	14FS-30 days
17	Subcontracting of works	Mon 26/10/5	Later Than	250 days	Sat 23/12/16	Wed 24/8/21	775 days	6
18	Setup of instrumentation and monitoring [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	0 days	12
19	Condition Survey [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	0 days	12
20	Freshwater Crab Translocation Plan [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	0 days	12
21	Archaeological Survey	NA	As Possible	300 days	Fri 24/3/8	Wed 25/1/1	333 days	12
22	Tree Survey [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	0 days	12
23	Vegetation Survey [A]	NA	As Possible	15 days	Fri 24/3/8	Fri 24/3/22	0 days	12
24	UU detection [A]	NA	As Possible	15 days	Sat 24/3/23	Sat 24/4/6	0 days	19,20
25	Site Clearance [A]	NA	As Possible	15 days	Sat 24/3/23	Sat 24/4/6	0 days	22,18,12,23
26	Establish access(es) to channels [A]	Mon 26/10/5	Later Than	25 days	Sun 24/4/7	Wed 24/5/1	0 days	25,24
27	Guarding / Barrier / Hoarding [A]	NA	As Possible	25 days	Sun 24/4/7	Wed 24/5/1	0 days	25,24
28	Drainage Channels Works	NA	As Possible	887 days	Thu 24/5/2	Mon 26/10/5	0 days	
29	Demolish & relocate retaining wall YLL795/A/4-5 [A]	NA	As Possible	30 days	Thu 24/5/2	Fri 24/5/31	0 days	27,26
30	Pedestrian & Vehicular Crossing no. 1 [A]	NA	As Possible	45 days	Sat 24/5/11	Mon 24/6/24	0 days	29FS-21 days
31	CLP Cable Trough	NA	As Possible	30 days	Tue 24/6/25	Wed 24/7/24	980 days	30
32	LFT06 CH.A173.5~CH.A227.75 (PVC1)	NA	As Possible	138 days	Tue 24/6/18	Sat 24/11/2	0 days	
33	Temp. Drainage Diversion / Sheetpiling [A]	NA	As Possible	40 days	Tue 24/6/18	Sat 24/7/27	0 days	30FS-7 days
34	Excavation and Lateral Support [A]	NA	As Possible	40 days	Sat 24/7/13	Wed 24/8/21	0 days	33FS-15 days
35	Ground and Edge Beams	NA	As Possible	41 days	Mon 24/8/5	Sat 24/9/14	0 days	
36	Install precast reinforcement cage (ground beam) [A]	NA	As Possible	28 days	Mon 24/8/5	Sun 24/9/1	0 days	34FS-17 days
37	Rebar Fixing [A]	NA	As Possible	25 days	Tue 24/8/13	Fri 24/9/6	0 days	36FS-20 days
38	Formwork Erection and Cast-in items [A]	NA	As Possible	25 days	Wed 24/8/21	Sat 24/9/14	0 days	37FS-17 days
39	Concreting [A]	NA	As Possible	1 day	Thu 24/8/29	Thu 24/8/29	0 days	38FS-17 days
40	Walls	NA	As Possible	43 days	Fri 24/8/30	Fri 24/10/11	710 days	
41	Rebar Fixing	NA	As Possible	30 days	Fri 24/8/30	Sat 24/9/28	710 days	39
42	Formwork Erection and Cast-in items	NA	As Possible	30 days	Thu 24/9/12	Fri 24/10/11	710 days	41FS-17 days
43	Concreting	NA	As Possible	1 day	Wed 24/9/25	Wed 24/9/25	710 days	42FS-17 days
44	Backfilling and Compaction	NA	As Possible	30 days	Thu 24/9/26	Fri 24/10/25	710 days	43
45	Removal of Sheetpiles	NA	As Possible	25 days	Wed 24/10/9	Sat 24/11/2	879 days	44FS-17 days
46	LFT07 CH.A227.5~CH.A300.75	NA	As Possible	109 days	Tue 24/9/24	Fri 25/1/10	0 days	
47	Temp. Drainage Diversion / Sheetpiling [A]	NA	As Possible	33 days	Tue 24/9/24	Sat 24/10/26	0 days	39FS+25 days
48	Excavation and Lateral Support [A]	NA	As Possible	33 days	Sat 24/10/12	Wed 24/11/13	0 days	47FS-15 days
49	Ground and Edge Beams	NA	As Possible	41 days	Mon 24/10/28	Sat 24/12/7	0 days	
50	Install precast reinforcement cage (ground beam) [A]	NA	As Possible	28 days	Mon 24/10/28	Sun 24/11/24	0 days	48FS-17 days
51	Rebar Fixing [A]	NA	As Possible	25 days	Tue 24/11/5	Fri 24/11/29	0 days	50FS-20 days
52	Formwork Erection and Cast-in items [A]	NA	As Possible	25 days	Wed 24/11/13	Sat 24/12/7	0 days	51FS-17 days
53	Concreting [A]	NA	As Possible	1 day	Thu 24/11/21	Thu 24/11/21	0 days	52FS-17 days
54	Walls	NA	As Possible	33 days	Fri 24/11/22	Tue 24/12/24	622 days	
55	Rebar Fixing	NA	As Possible	25 days	Fri 24/11/22	Mon 24/12/16	622 days	53
56	Formwork Erection and Cast-in items	NA	As Possible	25 days	Sat 24/11/30	Tue 24/12/24	622 days	55FS-17 days
57	Concreting	NA	As Possible	1 day	Sun 24/12/8	Sun 24/12/8	622 days	56FS-17 days
58	Backfilling and Compaction	NA	As Possible	25 days	Mon 24/12/9	Thu 25/1/2	622 days	57
59	Removal of Sheetpiles	NA	As Possible	25 days	Tue 24/12/17	Fri 25/1/10	622 days	58FS-17 days
60	Pedestrian & Vehicular Crossing no. 2	Mon 26/10/5	Later Than	28 days	Wed 24/12/25	Tue 25/1/21	622 days	59FS-17 days
61	LFT05 CH.A163.00~CH.A173.50	NA	As Possible	72 days	Wed 24/12/25	Thu 25/3/6	0 days	
62	Temp. Drainage Diversion / Sheetpiling [A]	NA	As Possible	27 days	Wed 24/12/25	Mon 25/1/20	0 days	53FS+33 days
63	Excavation and Lateral Support	NA	As Possible	27 days	Mon 25/1/6	Sat 25/2/1	0 days	62FS-15 days
64	Ground and Edge Beams	NA	As Possible	33 days	Thu 25/1/16	Mon 25/2/17	0 days	
65	Rebar Fixing [A]	NA	As Possible	25 days	Thu 25/1/16	Sun 25/2/9	0 days	63FS-17 days

Revision.: 18.0

Date: 28 February 2025

Task

Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Critical Task

Rolled Up Progress

Split

External Tasks

Project Summary

Group By Summary

Deadline


Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)

U-Channel: {U/S}~{D/S},size+type,length(m)


Drainage Channel: {U/S}~{D/S}


Page 5

WING TAT CIVIL ENGINEERING CO.LTD																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
PROJECT PROGRAMME																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Total Slack	Predecessors	Half 1		2023 Half 2							2024 Half 1							2024 Half 2							2025 Half 1							2025 Half 2							2026 Half 1							2026 Half 2							2027 Half 1							2027 Half 2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
									A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
66	Formwork Erection and Cast-in items [A]	NA	As Possible	25 days	Fri 25/1/24	Mon 25/2/17	0 days	65FS-17 days																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														

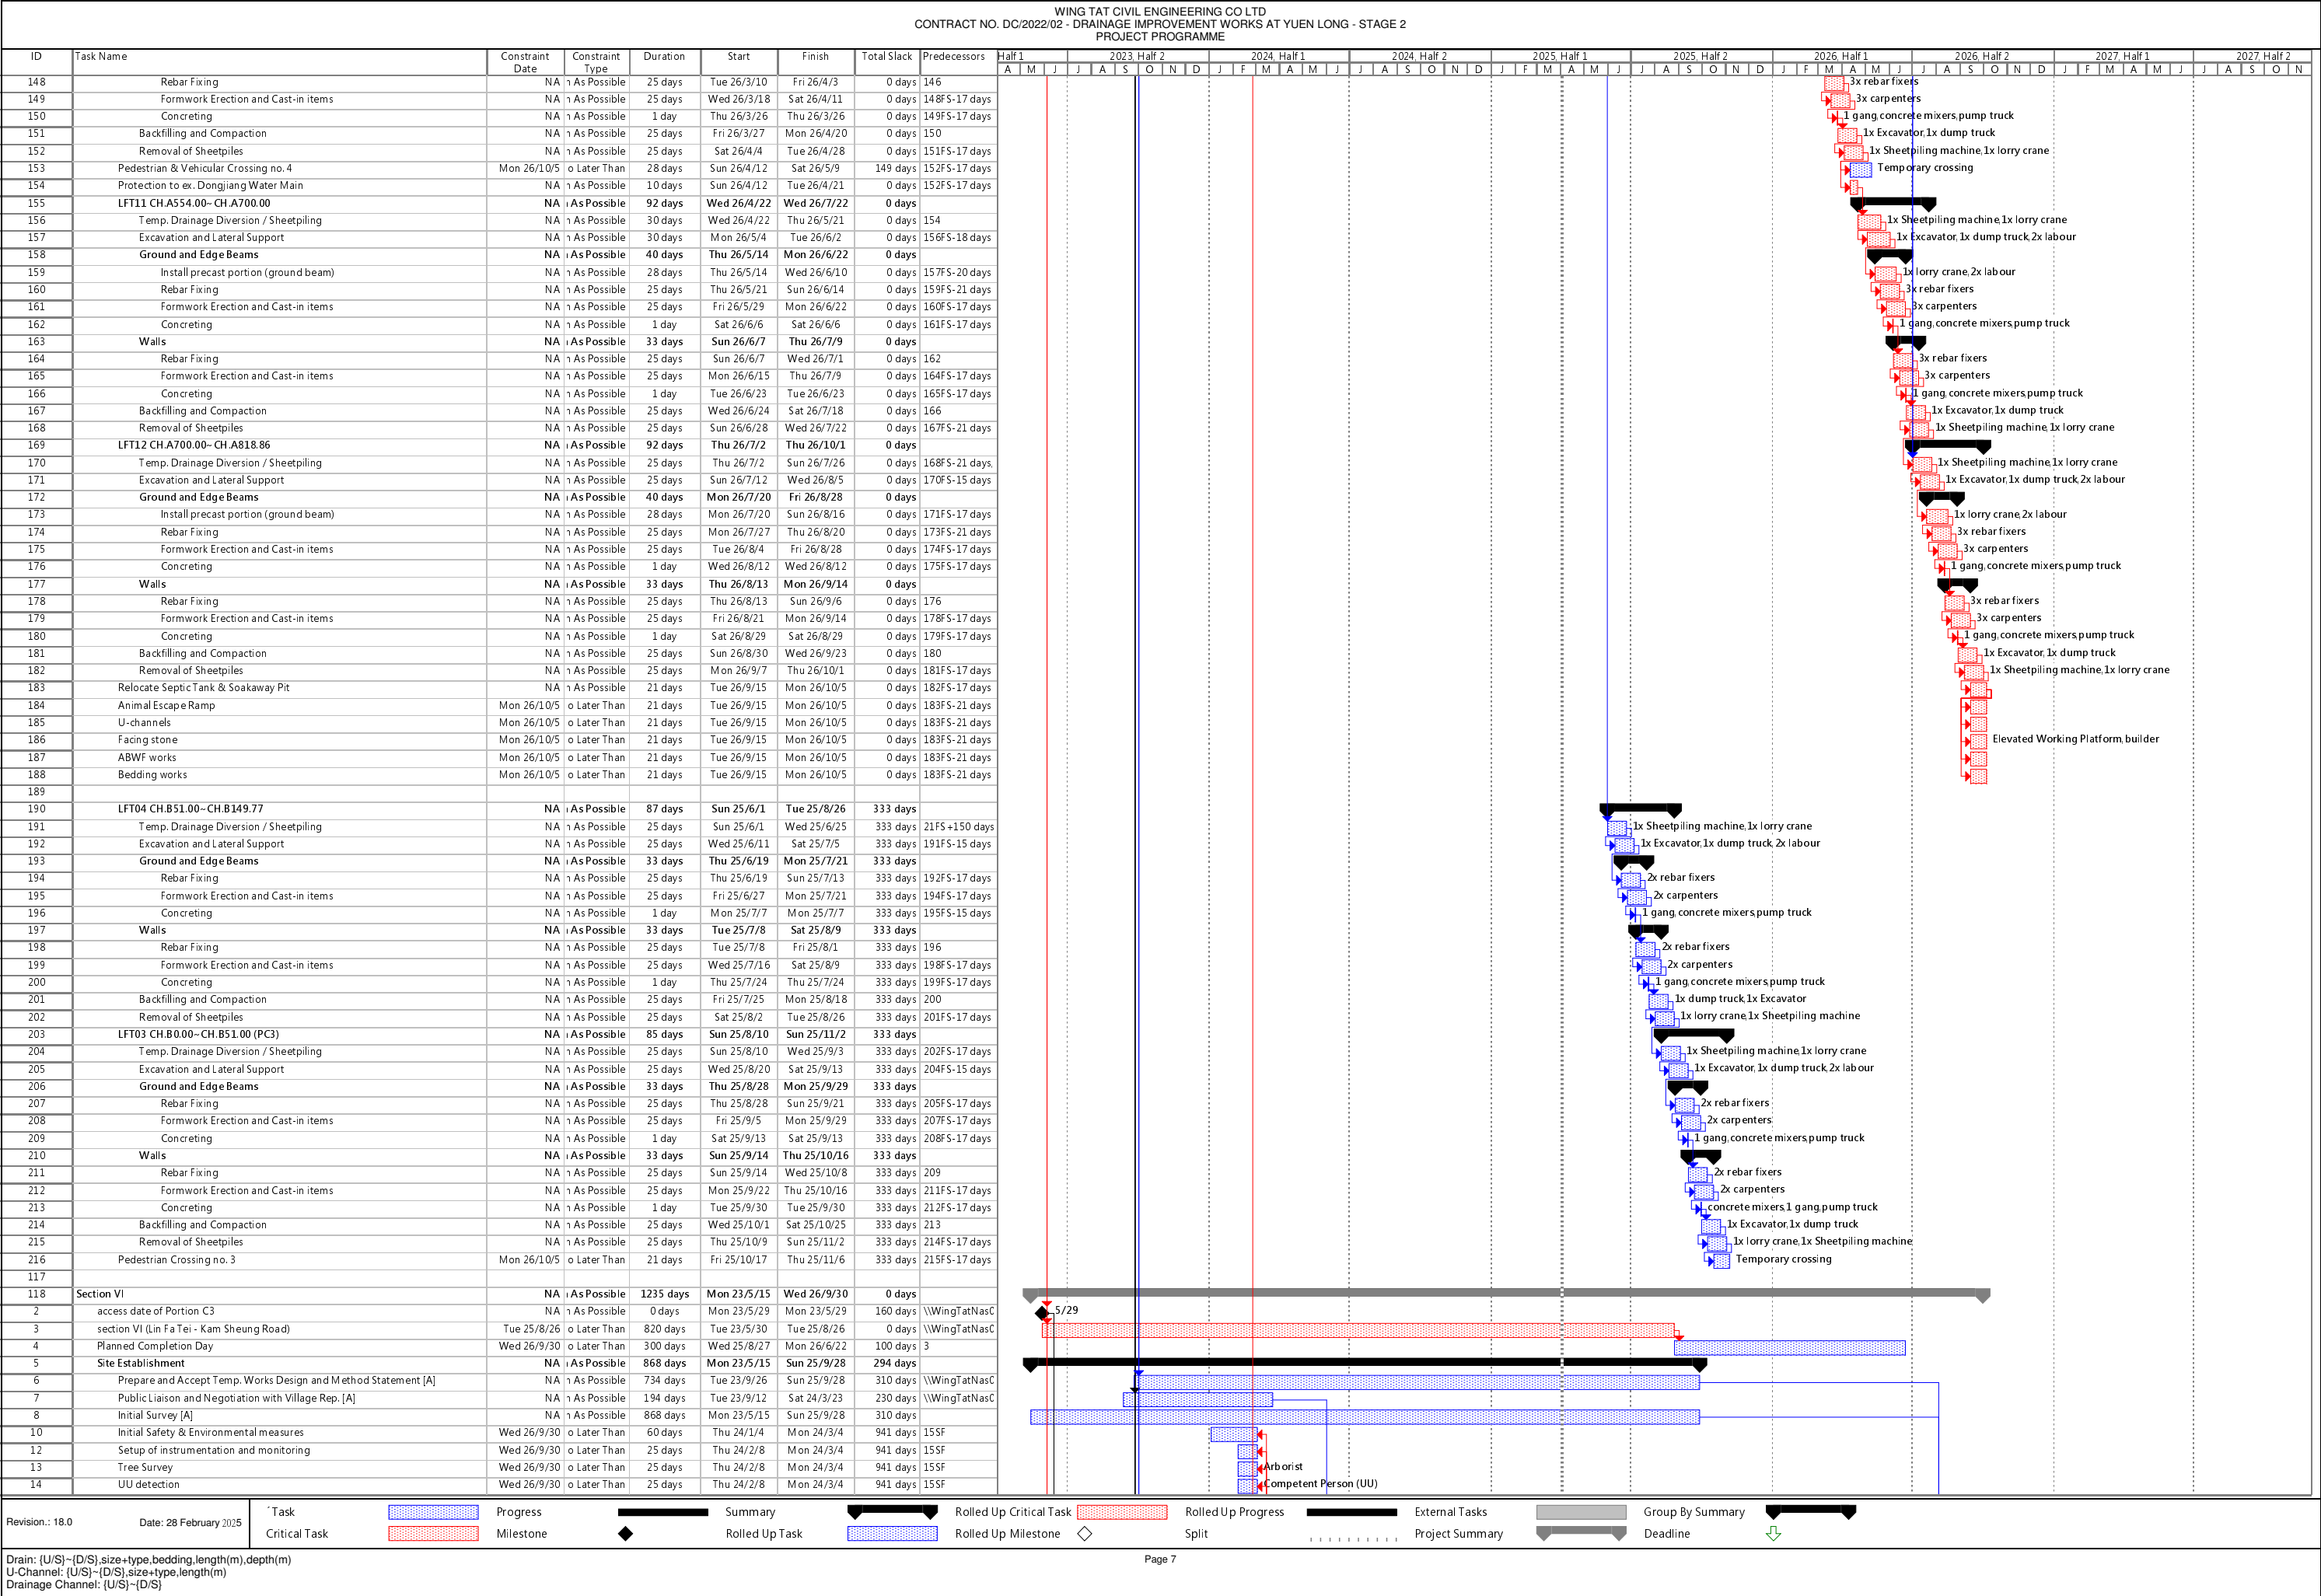

[illegible]

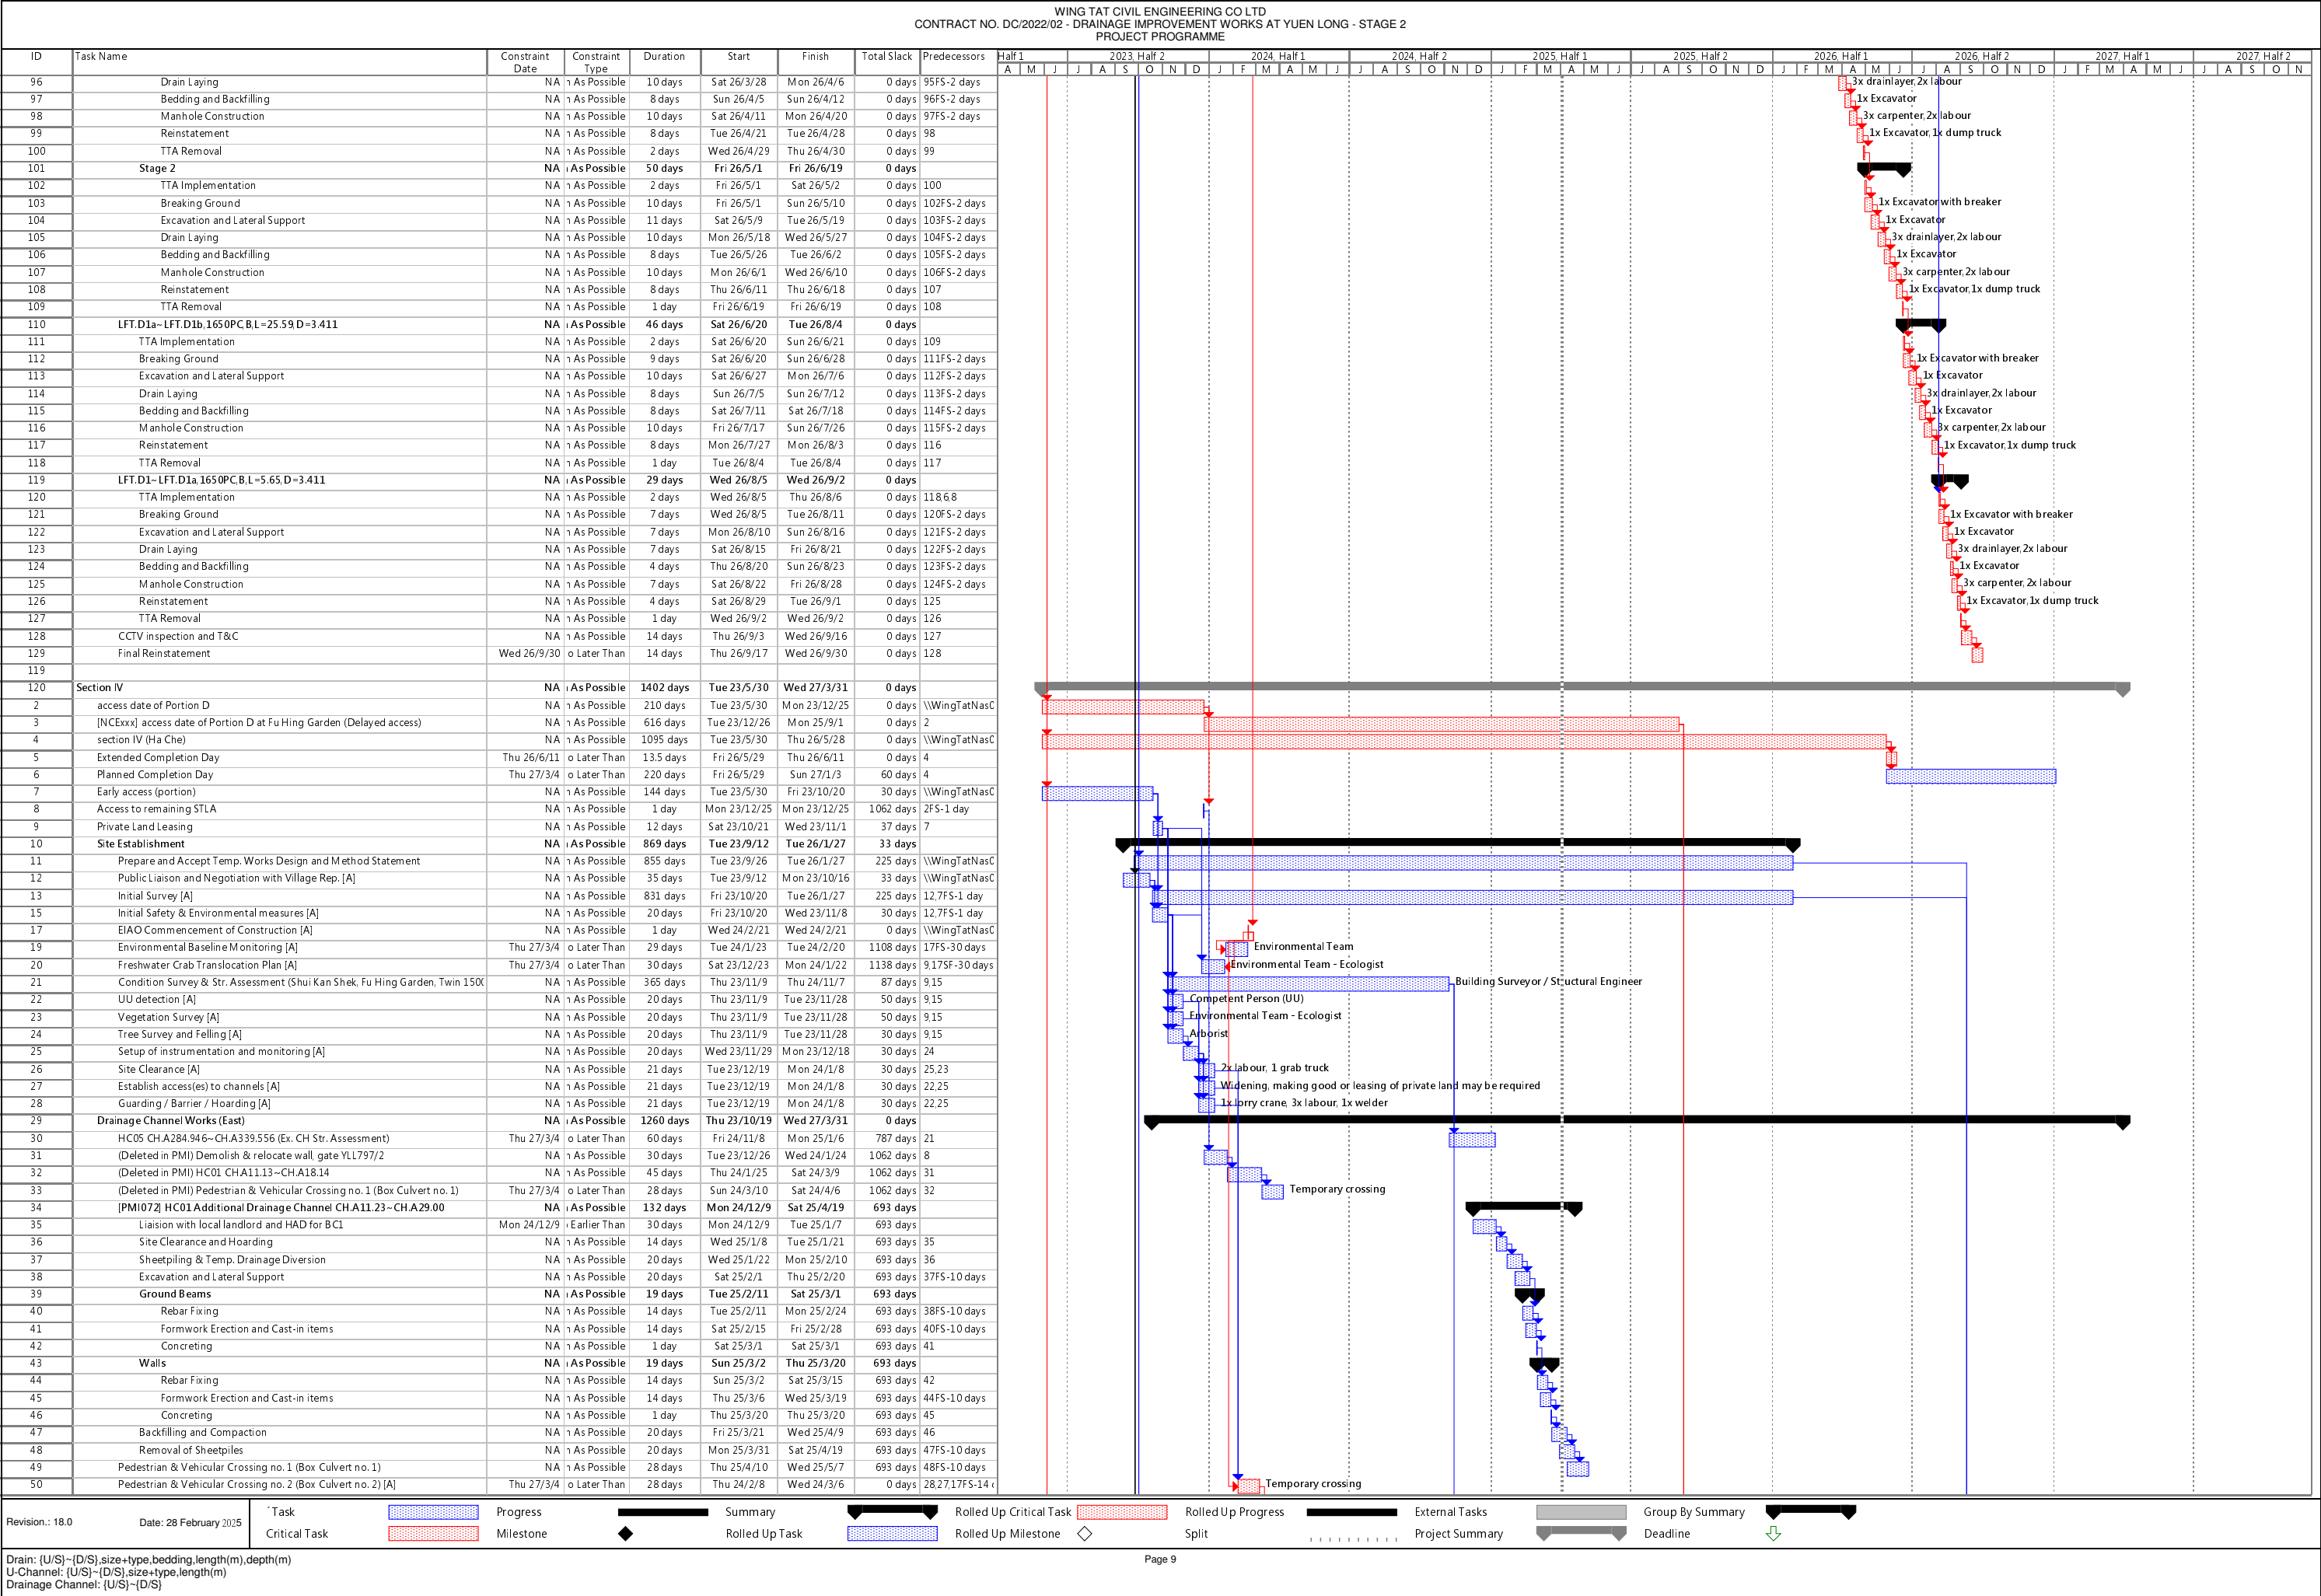

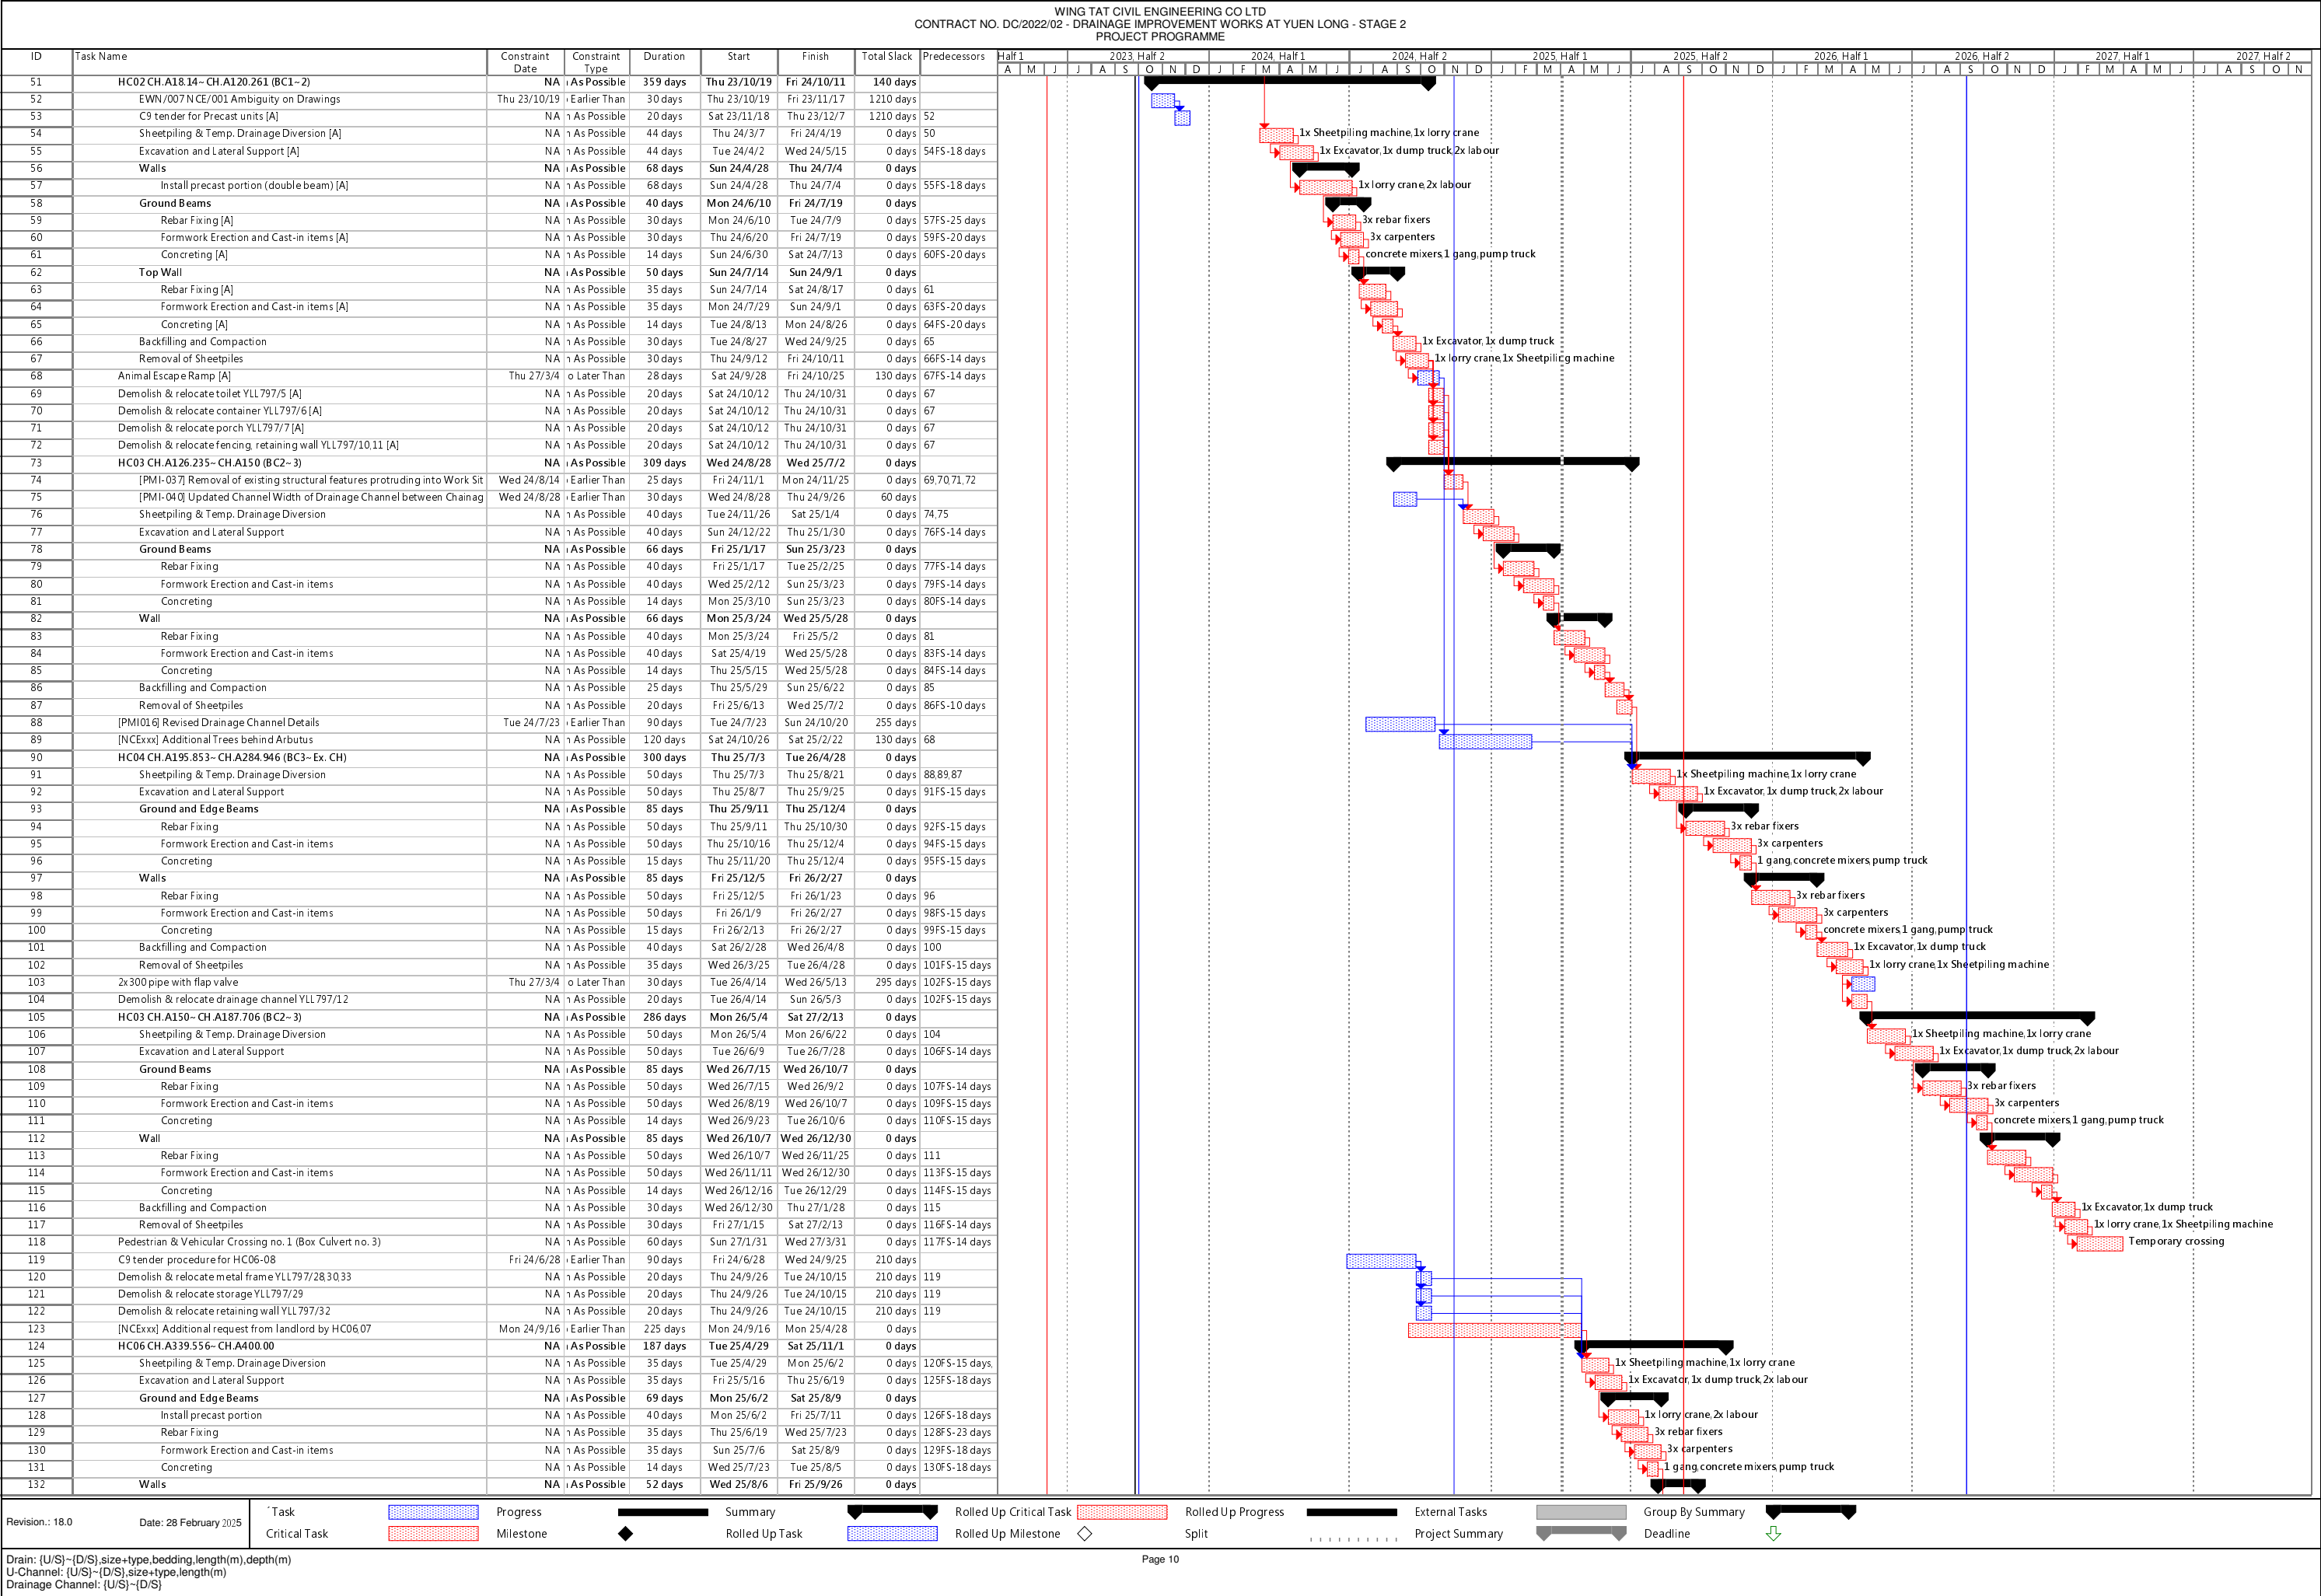


WING TAT CIVIL ENGINEERING CO LTD


CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2

PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Total Slack	Predecessors	Half 1	2023 Half 2					2024 Half 1					2024 Half 2					2025 Half 1					2025 Half 2					2026 Half 1					2026 Half 2					2027 Half 1					2027 Half 2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
									A	M	J	J	A	S	O	N	D	J	J	F	M	A	M	J	J	A	S	O	N	D	J	J	F	M	A	M	J	J	A	S	O	N	D	J	J	F	M	A	M	J	J	A	S	O	N	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
133	Rebar Fixing	NA	As Possible	35 days	Wed 25/8/6	Tue 25/9/9	0 days	131																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														</

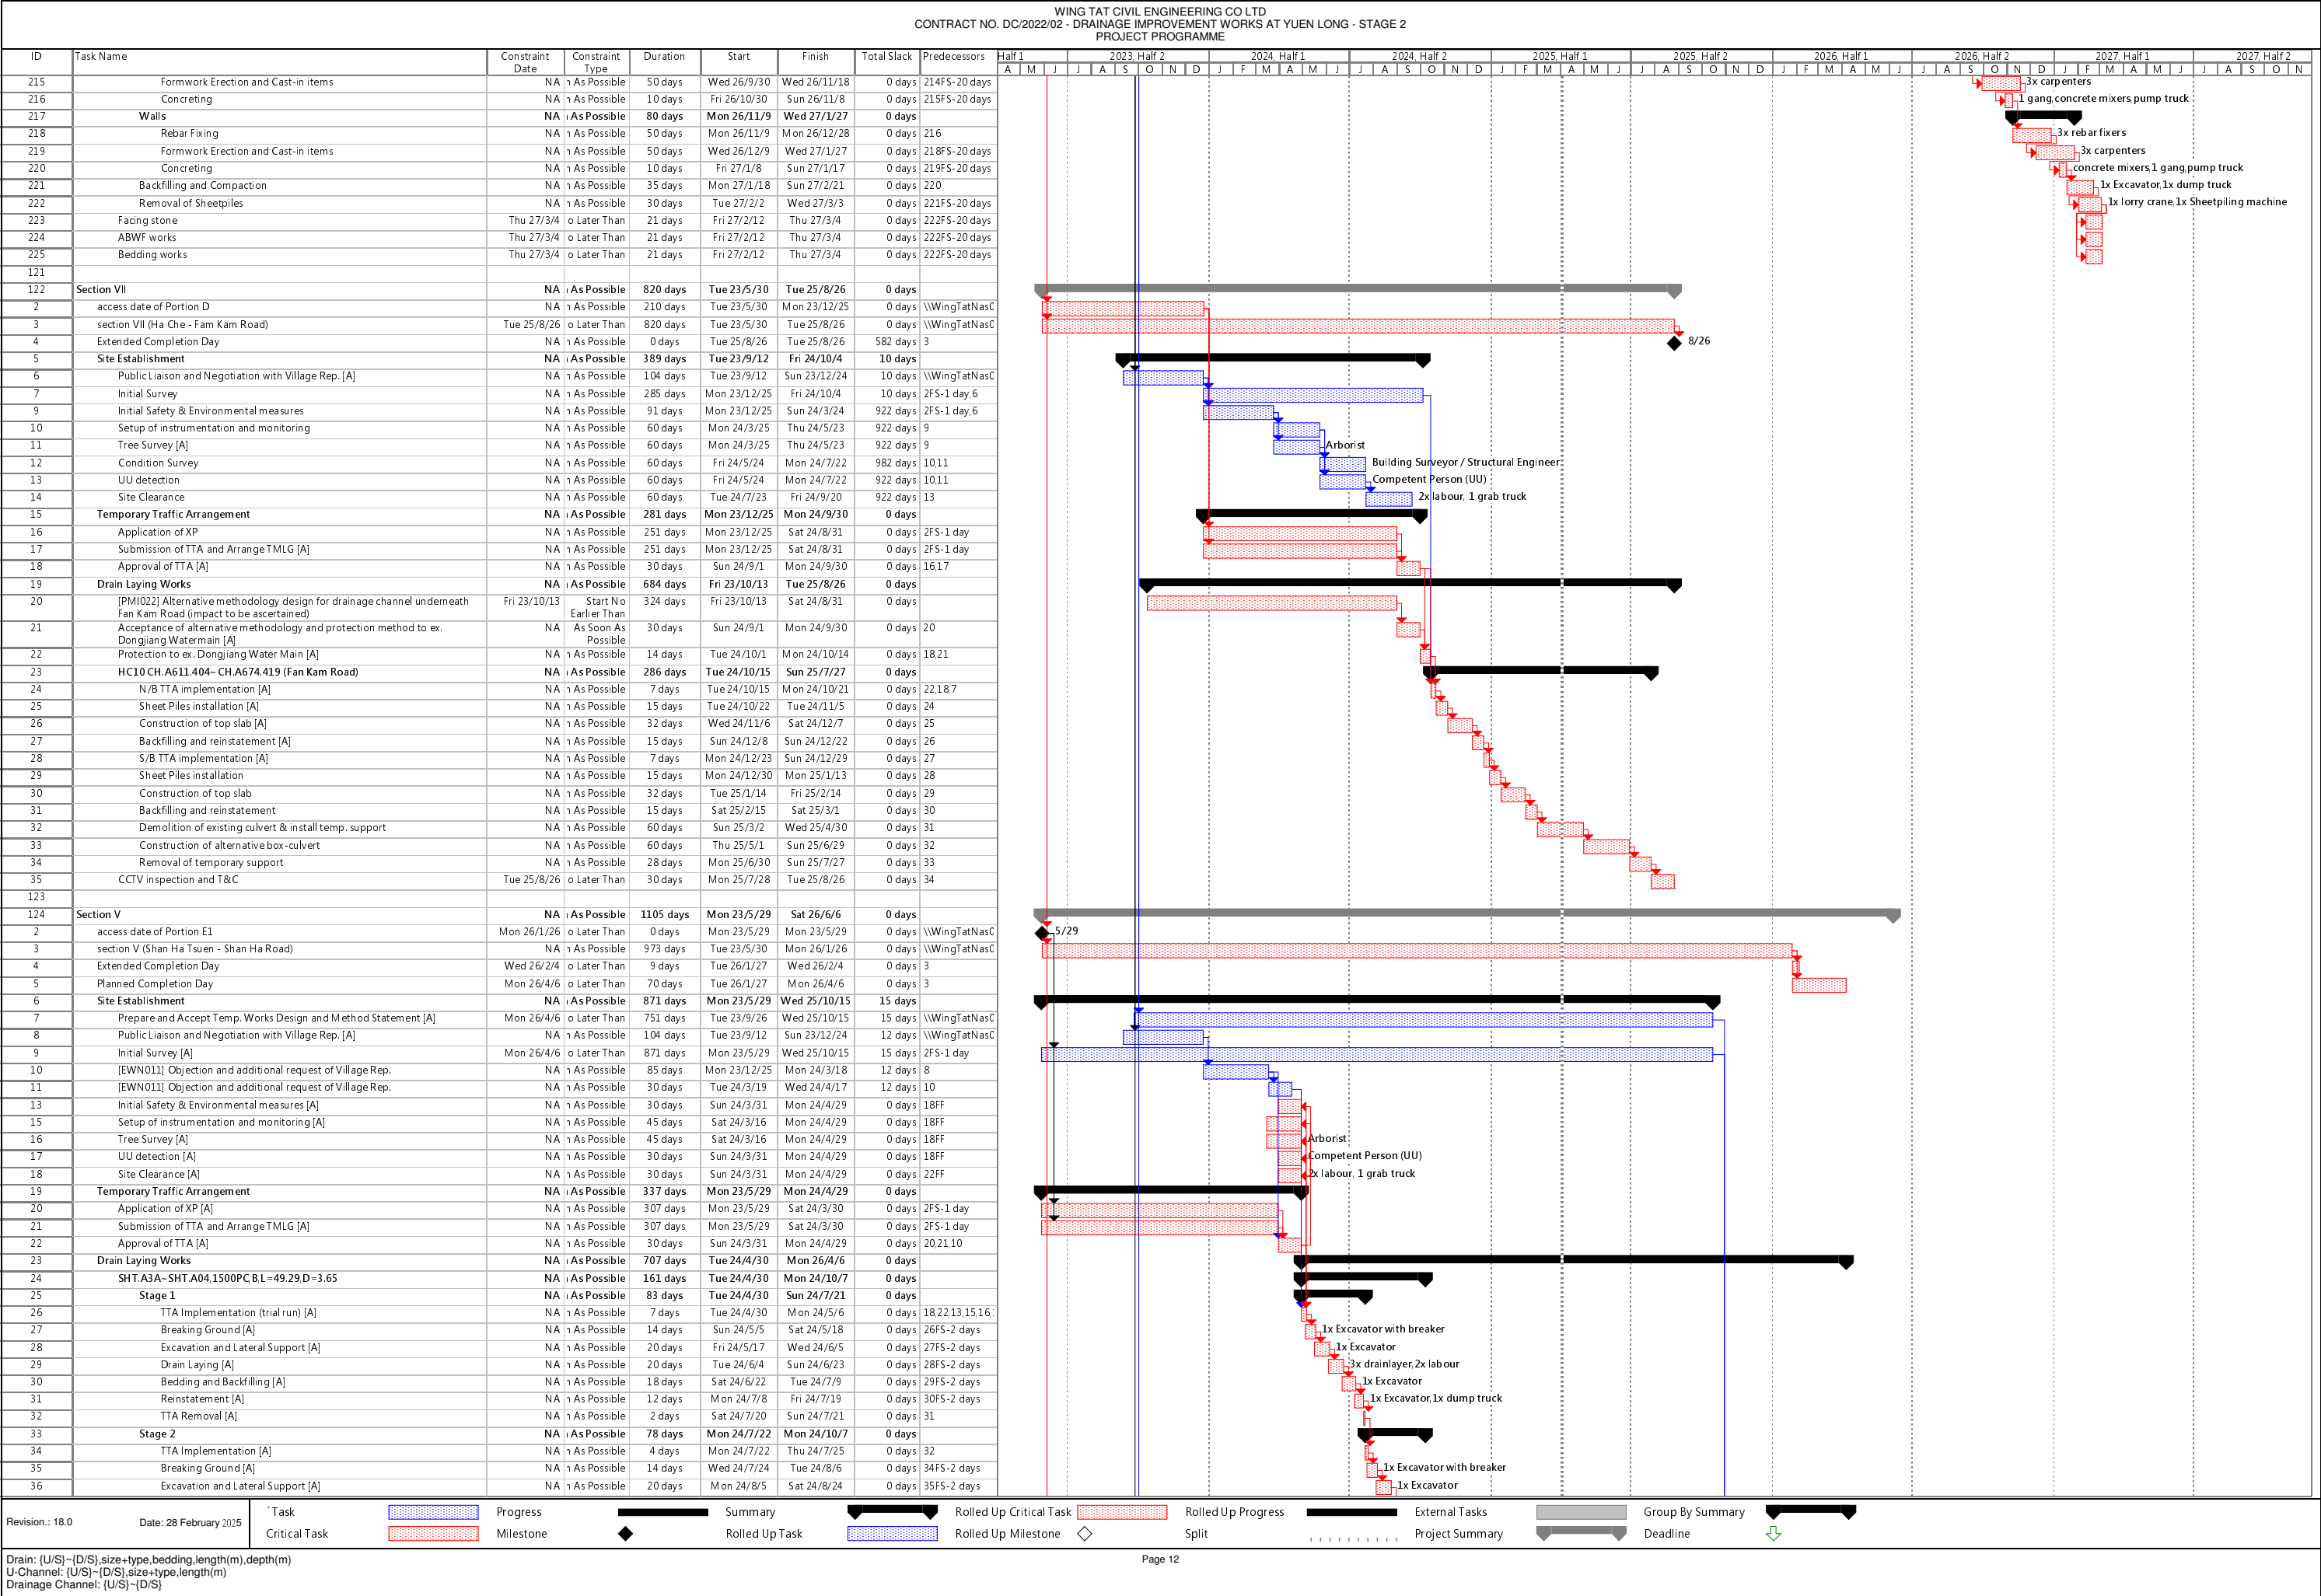

[illegible]

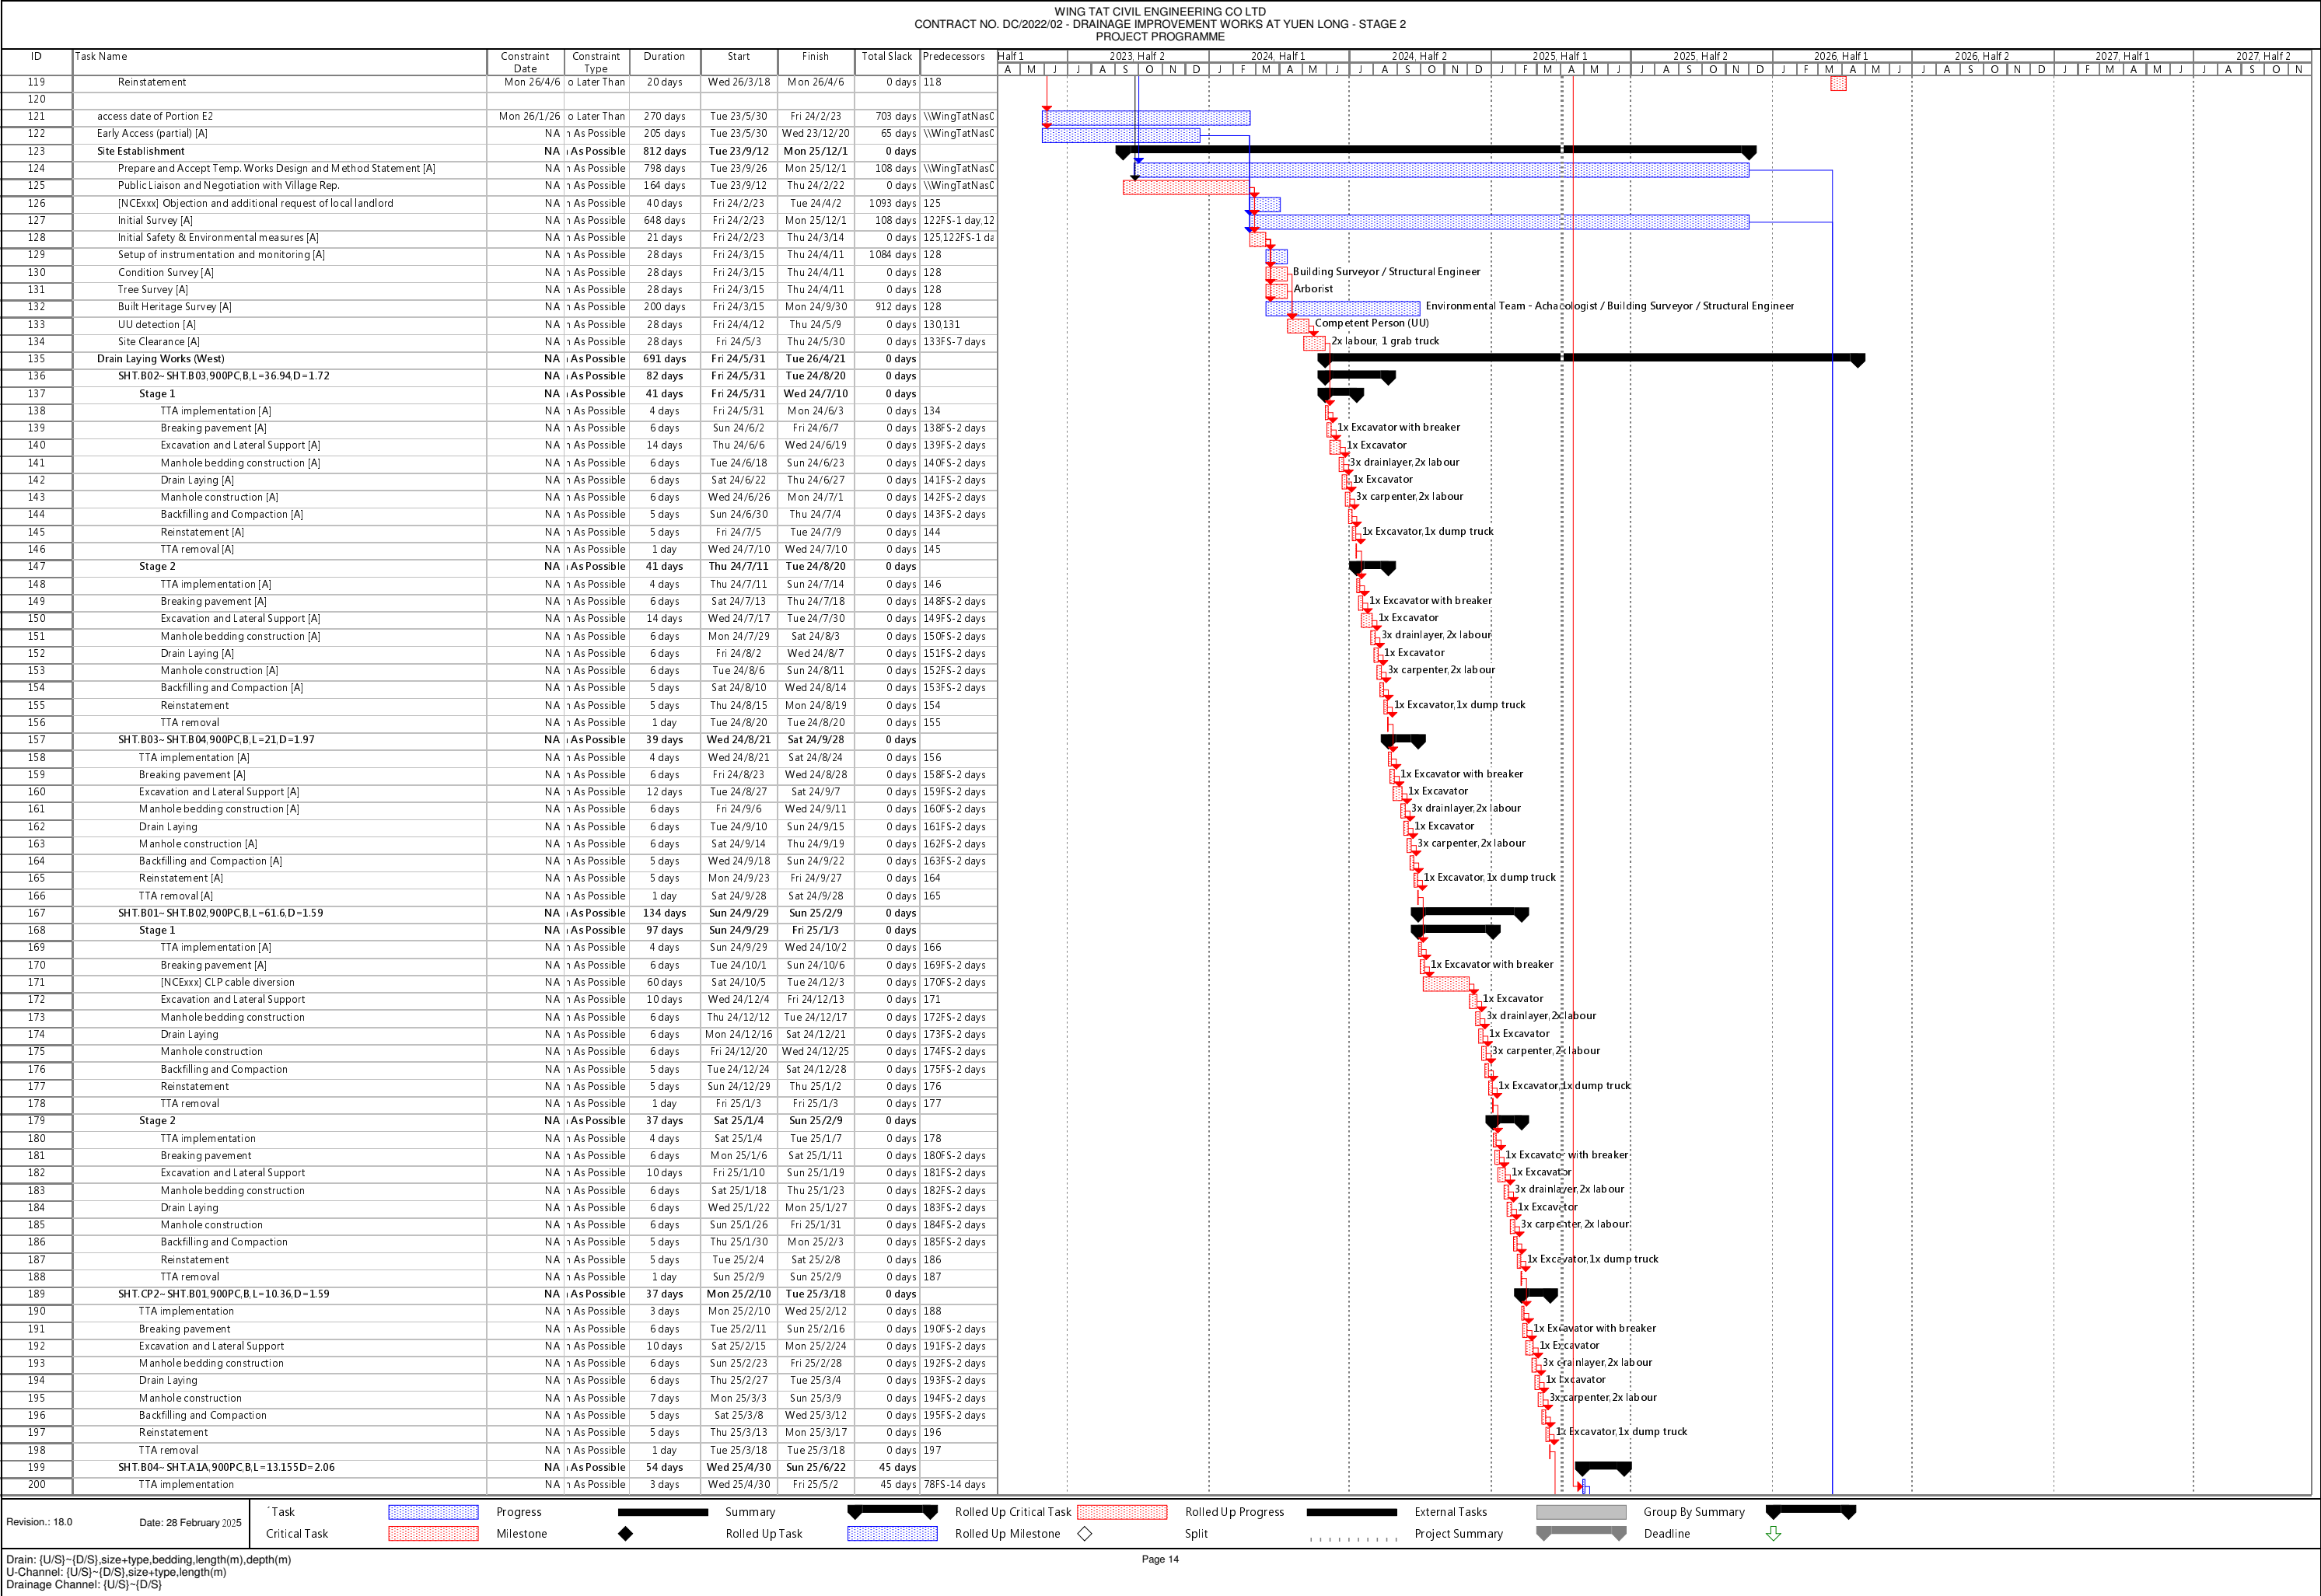

[illegible]

WING TAT CIVIL ENGINEERING CO.LTD CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2 PROJECT PROGRAMME																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Total Slack	Predecessors	Half 1	2023 Half 2					2024 Half 1					2025 Half 1					2025 Half 2					2026 Half 1					2026 Half 2					2027 Half 1					2027 Half 2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
									A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J

WING TAT CIVIL ENGINEERING CO LTD

CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2

PROJECT PROGRAMME

ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Total Slack	Predecessors	Half 1	2023 Half 2					2024 Half 1					2024 Half 2					2025 Half 1					2025 Half 2					2026 Half 1					2026 Half 2					2027 Half 1					2027 Half 2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
									A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
365	Catchpit construcion	NA	As Possible	14 days	Sun 25/4/6	Sat 25/4/19	0 days	364FS-2 days																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	

WING TAT CIVIL ENGINEERING CO.LTD CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2 PROJECT PROGRAMME																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
ID	Task Name	Constraint Date	Constraint Type	Duration	Start	Finish	Total Slack	Predecessors	Half 1	2023, Half 2					2024, Half 1					2024, Half 2					2025, Half 1					2025, Half 2					2026, Half 1					2026, Half 2					2027, Half 1					2027, Half 2																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
									A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
447	Excavation and Lateral Support	NA	As Possible	10 days	Wed 26/4/15	Fri 26/4/24	0 days	445																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

