


| WING TAT CIVIL ENGINEERING CO LTD<br>CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2<br>PROJECT PROGRAMME |                                                                                                                                                                                                                    |             |              |              |              |              |              |              |             |        |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
|---------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--------------|--------------|--------------|--------------|--------------|--------------|-------------|--------|--------------|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|--|
| ID                                                                                                                                    | Task Name                                                                                                                                                                                                          | Duration    | Start        | Finish       | Early Start  | Early Finish | Late Start   | Late Finish  | Total Slack | TRA    | Predecessors | 2023 |    |    |    | 2024 |    |    |    | 2025 |    |    |    | 2026 |    |    |    | 2027 |    |    |    |  |
|                                                                                                                                       |                                                                                                                                                                                                                    |             | Q1           | Q2           | Q3           | Q4           | Q1           | Q2           | Q3          | Q4     | Q1           | Q2   | Q3 | Q4 | Q1 | Q2   | Q3 | Q4 | Q1 | Q2   | Q3 | Q4 | Q1 | Q2   | Q3 | Q4 | Q1 | Q2   | Q3 | Q4 | Q1 |  |
| 1                                                                                                                                     | Starting date                                                                                                                                                                                                      | 1 day       | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29 | 0 days |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 2                                                                                                                                     | Access date                                                                                                                                                                                                        | 270 days    | Mon 23/5/29  | Fri 24/2/23  | Mon 23/5/29  | Fri 24/2/23  | Sun 26/7/5   | Wed 27/3/31  | 1132 days   |        |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 3                                                                                                                                     | Portion A                                                                                                                                                                                                          | 270 days    | Tue 23/5/30  | Fri 24/2/23  | Tue 23/5/30  | Fri 24/2/23  | Sun 26/7/5   | Wed 27/3/31  | 1132 days   | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 4                                                                                                                                     | Portion B                                                                                                                                                                                                          | 210 days    | Tue 23/5/30  | Mon 23/12/25 | Tue 23/5/30  | Mon 23/12/25 | Thu 26/9/3   | Wed 27/3/31  | 1192 days   | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 5                                                                                                                                     | Portion C1 & C2                                                                                                                                                                                                    | 270 days    | Tue 23/5/30  | Fri 24/2/23  | Tue 23/5/30  | Fri 24/2/23  | Sun 26/7/5   | Wed 27/3/31  | 1132 days   | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 6                                                                                                                                     | Portion C3                                                                                                                                                                                                         | 0 days      | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Wed 27/3/31  | Wed 27/3/31  | 1402 days   | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 7                                                                                                                                     | Portion D                                                                                                                                                                                                          | 210 days    | Tue 23/5/30  | Mon 23/12/25 | Tue 23/5/30  | Mon 23/12/25 | Thu 26/9/3   | Wed 27/3/31  | 1192 days   | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 8                                                                                                                                     | Portion E1                                                                                                                                                                                                         | 0 days      | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Wed 27/3/31  | Wed 27/3/31  | 1402 days   | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 9                                                                                                                                     | Portion E2                                                                                                                                                                                                         | 270 days    | Tue 23/5/30  | Fri 24/2/23  | Tue 23/5/30  | Fri 24/2/23  | Sun 26/7/5   | Wed 27/3/31  | 1132 days   | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 10                                                                                                                                    | Completion Date (Extended as accepted)                                                                                                                                                                             | 1201.5 days | Tue 23/5/30  | Sat 26/9/12  | Tue 23/5/30  | Sat 26/9/12  | Tue 23/5/30  | Sat 26/9/12  | 0 days      |        |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 11                                                                                                                                    | Section I - Drainage Improvement Works at Sung Shan New Village                                                                                                                                                    | 1110.5 days | Tue 23/5/30  | Sat 26/6/13  | Tue 23/5/30  | Sat 26/6/13  | Tue 23/5/30  | Sat 26/6/13  | 0 days      | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 12                                                                                                                                    | Original                                                                                                                                                                                                           | 1095 days   | Tue 23/5/30  | Thu 26/5/28  | Tue 23/5/30  | Thu 26/5/28  | Tue 23/5/30  | Thu 26/5/28  | 0 days      | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 13                                                                                                                                    | EOT - Indement weather Cl. 60.1(1.3)(iv)(v) [CE-088]                                                                                                                                                               | 15.5 days   | Fri 26/5/29  | Sat 26/6/13  | Fri 26/5/29  | Sat 26/6/13  | Fri 26/5/29  | Sat 26/6/13  | 0 days      | 12     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 14                                                                                                                                    | Section II - Drainage Improvement Works at Tai Wo                                                                                                                                                                  | 820 days    | Tue 23/5/30  | Tue 25/8/26  | Tue 23/5/30  | Tue 25/8/26  | Tue 23/5/30  | Tue 25/8/26  | 0 days      | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 15                                                                                                                                    | Section III - Drainage Improvement Works at Lin Fa Tei (except flood wall construction and drainage improvement works along Kam Sheung Road)                                                                       | 1201.5 days | Tue 23/5/30  | Sat 26/9/12  | Tue 23/5/30  | Sat 26/9/12  | Tue 23/5/30  | Sat 26/9/12  | 0 days      |        |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 16                                                                                                                                    | Original                                                                                                                                                                                                           | 1155 days   | Tue 23/5/30  | Mon 26/7/27  | Tue 23/5/30  | Mon 26/7/27  | Tue 23/5/30  | Mon 26/7/27  | 0 days      | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 17                                                                                                                                    | EOT - Indement weather Cl. 60.1(1.3)(iv)(v) [CE-033,069,086]                                                                                                                                                       | 46.5 days   | Tue 26/7/28  | Sat 26/9/12  | Tue 26/7/28  | Sat 26/9/12  | Tue 26/7/28  | Sat 26/9/12  | 0 days      | 16     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 18                                                                                                                                    | Section IV - Drainage Improvement Works at Ha Che (except pipe laying works by trenchless method and pipe rehabilitation works across Fan Kam Road)                                                                | 1148 days   | Tue 23/5/30  | Mon 26/7/20  | Tue 23/5/30  | Mon 26/7/20  | Tue 23/5/30  | Mon 26/7/20  | 0 days      |        |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 19                                                                                                                                    | Original                                                                                                                                                                                                           | 1095 days   | Tue 23/5/30  | Thu 26/5/28  | Tue 23/5/30  | Thu 26/5/28  | Tue 23/5/30  | Thu 26/5/28  | 0 days      | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 20                                                                                                                                    | EOT - Indement weather Cl. 60.1(1.3)(iv)(v) [CE-033,069,086]                                                                                                                                                       | 53 days     | Fri 26/5/29  | Mon 26/7/20  | Fri 26/5/29  | Mon 26/7/20  | Fri 26/5/29  | Mon 26/7/20  | 0 days      | 19     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 21                                                                                                                                    | Section V - Drainage Improvement Works at Shan Ha Tsuen                                                                                                                                                            | 1013 days   | Tue 23/5/30  | Sat 26/3/7   | Tue 23/5/30  | Sat 26/3/7   | Tue 23/5/30  | Sat 26/3/7   | 0 days      |        |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 22                                                                                                                                    | Original                                                                                                                                                                                                           | 973 days    | Tue 23/5/30  | Mon 26/1/26  | Tue 23/5/30  | Mon 26/1/26  | Tue 23/5/30  | Mon 26/1/26  | 0 days      | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 23                                                                                                                                    | EOT - Indement weather Cl. 60.1(1.3)(iv)(v) [CE-033,069,086]                                                                                                                                                       | 40 days     | Tue 26/1/27  | Sat 26/3/7   | Tue 26/1/27  | Sat 26/3/7   | Tue 26/1/27  | Sat 26/3/7   | 0 days      | 22     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 24                                                                                                                                    | Section VI - Flood Wall Construction and Drainage Improvement Works along Kam Sheung Road at Lin Fa Tei                                                                                                            | 820 days    | Tue 23/5/30  | Tue 25/8/26  | Tue 23/5/30  | Tue 25/8/26  | Tue 23/5/30  | Tue 25/8/26  | 0 days      | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 25                                                                                                                                    | Section VII - Pipe Laying Works by Trenchless Method and Pipe Rehabilitation Works across Fan Kam Road and Upstream Channel and Downstream Box Culvert Construction Works (Chainage 626.224m - 678.859m) at Ha Che | 820 days    | Tue 23/5/30  | Tue 25/8/26  | Tue 23/5/30  | Tue 25/8/26  | Tue 23/5/30  | Tue 25/8/26  | 0 days      | 1      |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 46                                                                                                                                    | Planned Completion Day of whole of the works                                                                                                                                                                       | 582 days    | Wed 25/8/27  | Wed 27/3/31  | Wed 25/8/27  | Wed 27/3/31  | Wed 25/8/27  | Wed 27/3/31  | 0 days      |        |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 47                                                                                                                                    | Section I - Drainage Improvement Works at Sung Shan New Village                                                                                                                                                    | 291.5 days  | Sat 26/6/13  | Wed 27/3/31  | Sat 26/6/13  | Wed 27/3/31  | Sat 26/6/13  | Wed 27/3/31  | 0 days      |        |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 48                                                                                                                                    | EOT - Indement weather (anticipated)                                                                                                                                                                               | 42 days     | Sat 26/6/13  | Sat 26/7/25  | Sat 26/6/13  | Sat 26/7/25  | Sat 26/6/13  | Sat 26/7/25  | 0 days      | 11     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 49                                                                                                                                    | EOT - Uncharted/Retained Trees obstructing the works                                                                                                                                                               | 150 days    | Sat 26/7/25  | Tue 26/12/22 | Sat 26/7/25  | Tue 26/12/22 | Sat 26/7/25  | Tue 26/12/22 | 0 days      | 48     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 50                                                                                                                                    | EOT - Obstruction to Sheet Piling at CHA50 - CHA280                                                                                                                                                                | 99.5 days   | Tue 26/12/22 | Wed 27/3/31  | Tue 26/12/22 | Wed 27/3/31  | Tue 26/12/22 | Wed 27/3/31  | 0 days      | 49     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |
| 51                                                                                                                                    | Section II - Drainage Improvement Works at Tai Wo                                                                                                                                                                  | 582 days    | Wed 25/8/27  | Wed 27/3/31  | Wed 25/8/27  | Wed 27/3/31  | Wed 25/8/27  | Wed 27/3/31  | 0 days      |        |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |  |

| WING TAT CIVIL ENGINEERING CO LTD |                                                            |           |             |              |             |              |             |              |             |     |                    | CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2 PROJECT PROGRAMME |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|-----------------------------------|------------------------------------------------------------|-----------|-------------|--------------|-------------|--------------|-------------|--------------|-------------|-----|--------------------|-----------------------------------------------------------------------------------------------|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
| ID                                | Task Name                                                  | Duration  | Start       | Finish       | Early Start | Early Finish | Late Start  | Late Finish  | Total Slack | TRA | Predecessors       | <div> <div>2023</div> <div>2024</div> <div>2025</div> <div>2026</div> <div>2027</div> </div>  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 115                               | Move-in [A]                                                | 7 days    | Thu 24/1/18 | Wed 24/1/24  | Thu 24/1/18 | Wed 24/1/24  | Thu 27/3/25 | Wed 27/3/31  | 1162 days   | 0   | 114                |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 116                               |                                                            |           |             |              |             |              |             |              |             |     |                    |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 117                               | Section I                                                  | 1402 days | Tue 23/5/30 | Wed 27/3/31  | Tue 23/5/30 | Wed 27/3/31  | Tue 23/5/30 | Wed 27/3/31  | 0 days      |     |                    |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 2                                 | access date of Portion A                                   | 270 days  | Tue 23/5/30 | Fri 24/2/23  | Tue 23/5/30 | Fri 24/2/23  | Tue 23/5/30 | Fri 24/2/23  | 0 days      | 0   | \\WingTatNas02\\DC |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 3                                 | Period of section I (Sung Shan New Village)                | 1095 days | Tue 23/5/30 | Tue 23/5/30  | Tue 23/5/30 | Tue 23/5/30  | Thu 26/5/28 | Tue 23/5/30  | 0 days      | 0   | \\WingTatNas02\\DC |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 4                                 | Extended Completion Day                                    | 7.5 days  | Fri 26/5/29 | Fri 26/6/5   | Fri 26/5/29 | Fri 26/6/5   | Wed 27/3/24 | Wed 27/3/31  | 299.5 days  | 0   | 3                  |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 5                                 | Planned Completion Day                                     | 307 days  | Fri 26/5/29 | Wed 27/3/31  | Fri 26/5/29 | Wed 27/3/31  | Fri 26/5/29 | Wed 27/3/31  | 0 days      | 0   | 3                  |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 6                                 | Early access (partial) [A]                                 | 200 days  | Tue 23/5/30 | Fri 23/12/15 | Tue 23/5/30 | Tue 23/8/8   | Fri 24/2/23 | Fri 24/2/23  | 70 days     | 0   | \\WingTatNas02\\DC |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 7                                 | Site Establishment                                         | 878 days  | Tue 23/9/12 | Thu 26/2/5   | Tue 23/9/12 | Thu 26/2/5   | Tue 23/9/12 | Wed 27/3/31  | 0 days      | 0   | \\WingTatNas02\\DC |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 8                                 | Prepare and Accept Temp. Works Design and Method Statement | 864 days  | Tue 23/9/26 | Thu 26/2/5   | Tue 23/9/26 | Thu 26/2/5   | Tue 24/6/18 | Thu 26/10/29 | 266 days    | 0   | \\WingTatNas02\\DC |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| 9                                 | Public Liaison and Negotiation with Village Rep.           | 164 days  | Tue 23/9/12 | Thu 24/2/22  | Tue 23/9/12 | Thu 24/2/22  | Tue 23/9/12 | Thu 24/2/22  | 0 days      | 0   | \\WingTatNas02\\DC |                                                                                               |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

| WING TAT CIVIL ENGINEERING CO LTD                                           |                                                    |          |              |              |              |              |              |              |             |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
|-----------------------------------------------------------------------------|----------------------------------------------------|----------|--------------|--------------|--------------|--------------|--------------|--------------|-------------|-----|---------------|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|----|
| CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2 |                                                    |          |              |              |              |              |              |              |             |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| PROJECT PROGRAMME                                                           |                                                    |          |              |              |              |              |              |              |             |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| ID                                                                          | Task Name                                          | Duration | Start        | Finish       | Early Start  | Early Finish | Late Start   | Late Finish  | Total Slack | TRA | Predecessors  | 2023 |    |    |    | 2024 |    |    |    | 2025 |    |    |    | 2026 |    |    |    | 2027 |    |    |    |    |
|                                                                             |                                                    |          |              |              |              |              |              |              |             |     |               | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1 |
| 83                                                                          | Excavation and Lateral Support                     | 35 days  | Mon 26/5/4   | Sun 26/6/7   | Mon 26/5/4   | Sun 26/6/7   | Mon 26/5/4   | Sun 26/6/7   | 0 days      |     | 82FS-20 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 84                                                                          | Ground and Edge Beams                              | 58 days  | Tue 26/5/19  | Wed 26/7/15  | Tue 26/5/19  | Wed 26/7/15  | Wed 26/5/27  | Wed 27/3/31  | 8 days      |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 85                                                                          | Rebar Fixing                                       | 35 days  | Tue 26/5/19  | Mon 26/6/22  | Tue 26/5/19  | Mon 26/6/22  | Tue 27/2/2   | Mon 27/3/8   | 259 days    |     | 83FS-20 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 86                                                                          | Formwork Erection and Cast-in items                | 35 days  | Thu 26/6/11  | Wed 26/7/15  | Wed 26/6/11  | Wed 26/7/15  | Thu 27/2/25  | Wed 27/3/31  | 259 days    |     | 85FS-12 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 87                                                                          | Concreting                                         | 4 days   | Wed 26/5/27  | Sat 26/5/30  | Wed 26/5/27  | Sat 26/5/30  | Wed 26/5/27  | Sat 26/5/30  | 0 days      |     | 83FS-12 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 88                                                                          | Walls                                              | 58 days  | Sun 26/5/31  | Mon 26/7/27  | Sun 26/5/31  | Mon 26/7/27  | Sun 26/5/31  | Mon 26/7/27  | 0 days      |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 89                                                                          | Rebar Fixing                                       | 35 days  | Sun 26/5/31  | Sat 26/7/4   | Sun 26/5/31  | Sat 26/7/4   | Sun 26/5/31  | Sat 26/7/4   | 0 days      |     | 87            |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 90                                                                          | Formwork Erection and Cast-in items                | 35 days  | Tue 26/6/23  | Mon 26/7/27  | Tue 26/6/23  | Mon 26/7/27  | Tue 26/6/23  | Mon 26/7/27  | 0 days      |     | 89FS-12 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 91                                                                          | Concreting                                         | 4 days   | Thu 26/7/16  | Sun 26/7/19  | Thu 26/7/16  | Sun 26/7/19  | Thu 26/7/16  | Sun 26/7/19  | 0 days      |     | 90FS-12 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 92                                                                          | Backfilling and Compaction                         | 30 days  | Mon 26/7/20  | Tue 26/8/18  | Mon 26/7/20  | Tue 26/8/18  | Mon 26/7/20  | Tue 26/8/18  | 0 days      |     | 91            |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 93                                                                          | Removal of Sheetpiles                              | 20 days  | Sun 26/8/9   | Fri 26/8/28  | Sun 26/8/9   | Fri 26/8/28  | Sun 26/8/9   | Fri 26/8/28  | 0 days      |     | 92FS-10 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 94                                                                          | Demolish & relocate wall, hoarding YLL796/B/13,13B | 30 days  | Wed 26/8/19  | Thu 26/9/17  | Wed 26/8/19  | Thu 26/9/17  | Wed 26/8/19  | Thu 26/9/17  | 0 days      | 0   | 93FS-10 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 95                                                                          | Demolish & relocate OSC YLL 796/B/14A,14B          | 30 days  | Wed 26/8/19  | Thu 26/9/17  | Wed 26/8/19  | Thu 26/9/17  | Wed 26/8/19  | Thu 26/9/17  | 0 days      | 0   | 93FS-10 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 96                                                                          | Demolish & relocate fence & wall YLL796/B/14       | 30 days  | Wed 26/8/19  | Thu 26/9/17  | Wed 26/8/19  | Thu 26/9/17  | Wed 26/8/19  | Thu 26/9/17  | 0 days      | 0   | 93FS-10 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 97                                                                          | SSNV05 CH.A200.00~ CH.A300.00                      | 195 days | Fri 26/9/18  | Wed 27/3/31  | Fri 26/9/18  | Wed 27/3/31  | Fri 26/9/18  | Wed 27/3/31  | 0 days      |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 98                                                                          | Sheetpiling & Temp. Drainage Diversion             | 48 days  | Fri 26/9/18  | Wed 26/11/4  | Fri 26/9/18  | Wed 26/11/4  | Fri 26/9/18  | Wed 26/11/4  | 0 days      | 2   | 94,95,96      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 99                                                                          | Excavation and Lateral Support                     | 48 days  | Fri 26/10/16 | Wed 26/12/2  | Fri 26/10/16 | Wed 26/12/2  | Fri 26/10/16 | Wed 26/12/2  | 0 days      | 2   | 98FS-20 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 100                                                                         | Ground and Edge Beams                              | 58 days  | Thu 26/11/12 | Fri 27/1/8   | Thu 26/11/12 | Fri 27/1/8   | Thu 26/11/12 | Fri 27/1/8   | 0 days      |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 101                                                                         | Rebar Fixing                                       | 35 days  | Thu 26/11/12 | Wed 26/12/16 | Thu 26/11/12 | Wed 26/12/16 | Thu 26/11/12 | Wed 26/12/16 | 0 days      | 1   | 99FS-21 days  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 102                                                                         | Formwork Erection and Cast-in items                | 35 days  | Sat 26/12/5  | Fri 27/1/8   | Sat 26/12/5  | Fri 27/1/8   | Sat 26/12/5  | Fri 27/1/8   | 0 days      | 1   | 101FS-12 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 103                                                                         | Concreting                                         | 4 days   | Mon 26/12/28 | Thu 26/12/31 | Mon 26/12/28 | Thu 26/12/31 | Mon 26/12/28 | Thu 26/12/31 | 0 days      | 0   | 102FS-12 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 104                                                                         | Walls                                              | 58 days  | Fri 27/1/1   | Sat 27/2/27  | Fri 27/1/1   | Sat 27/2/27  | Fri 27/1/1   | Sat 27/2/27  | 0 days      |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 105                                                                         | Rebar Fixing                                       | 35 days  | Fri 27/1/1   | Thu 27/2/4   | Fri 27/1/1   | Thu 27/2/4   | Fri 27/1/1   | Thu 27/2/4   | 0 days      | 1   | 103           |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 106                                                                         | Formwork Erection and Cast-in items                | 35 days  | Sun 27/1/24  | Sat 27/2/27  | Sun 27/1/24  | Sat 27/2/27  | Sun 27/1/24  | Sat 27/2/27  | 0 days      | 1   | 105FS-12 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 107                                                                         | Concreting                                         | 4 days   | Tue 27/2/16  | Tue 27/2/19  | Tue 27/2/16  | Fri 27/2/19  | Tue 27/2/16  | Fri 27/2/19  | 0 days      | 0   | 106FS-12 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 108                                                                         | Backfilling and Compaction                         | 30 days  | Sat 27/2/20  | Sun 27/3/21  | Sat 27/2/20  | Sun 27/3/21  | Sat 27/2/20  | Sun 27/3/21  | 0 days      | 0   | 107           |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 109                                                                         | Removal of Sheetpiles                              | 20 days  | Fri 27/3/12  | Wed 27/3/31  | Fri 27/3/12  | Wed 27/3/31  | Fri 27/3/12  | Wed 27/3/31  | 0 days      | 0   | 108FS-10 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 110                                                                         | Animal Escape Ramp                                 | 14 days  | Thu 26/11/5  | Wed 26/11/18 | Thu 26/11/5  | Wed 26/11/18 | Thu 26/11/5  | Wed 26/11/18 | 0 days      | 0   | 98            |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 111                                                                         | Demolish & relocate metal frame YLL796/B/6         | 20 days  | Mon 26/11/9  | Sat 26/11/28 | Mon 26/11/9  | Sat 26/11/28 | Mon 26/11/9  | Sat 26/11/28 | 0 days      | 0   | 110FS-10 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 112                                                                         | Demolish & relocate metal frame YLL796/B/7-8       | 20 days  | Mon 26/11/9  | Sat 26/11/28 | Mon 26/11/9  | Sat 26/11/28 | Mon 26/11/9  | Sat 26/11/28 | 0 days      | 0   | 110FS-10 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 113                                                                         | SSNV04 CH.A300.00~ CH.A333.00                      | 123 days | Sun 26/11/29 | Wed 27/3/31  | Sun 26/11/29 | Wed 27/3/31  | Sun 26/11/29 | Wed 27/3/31  | 0 days      |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 114                                                                         | Sheetpiling & Temp. Drainage Diversion [A]         | 28 days  | Sun 26/11/29 | Sat 26/12/26 | Sun 26/11/29 | Sat 26/12/26 | Sun 26/11/29 | Sat 26/12/26 | 0 days      | 2   | 111,112       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 115                                                                         | Excavation and Lateral Support [A]                 | 28 days  | Thu 26/2     |              |              |              |              |              |             |     |               |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |

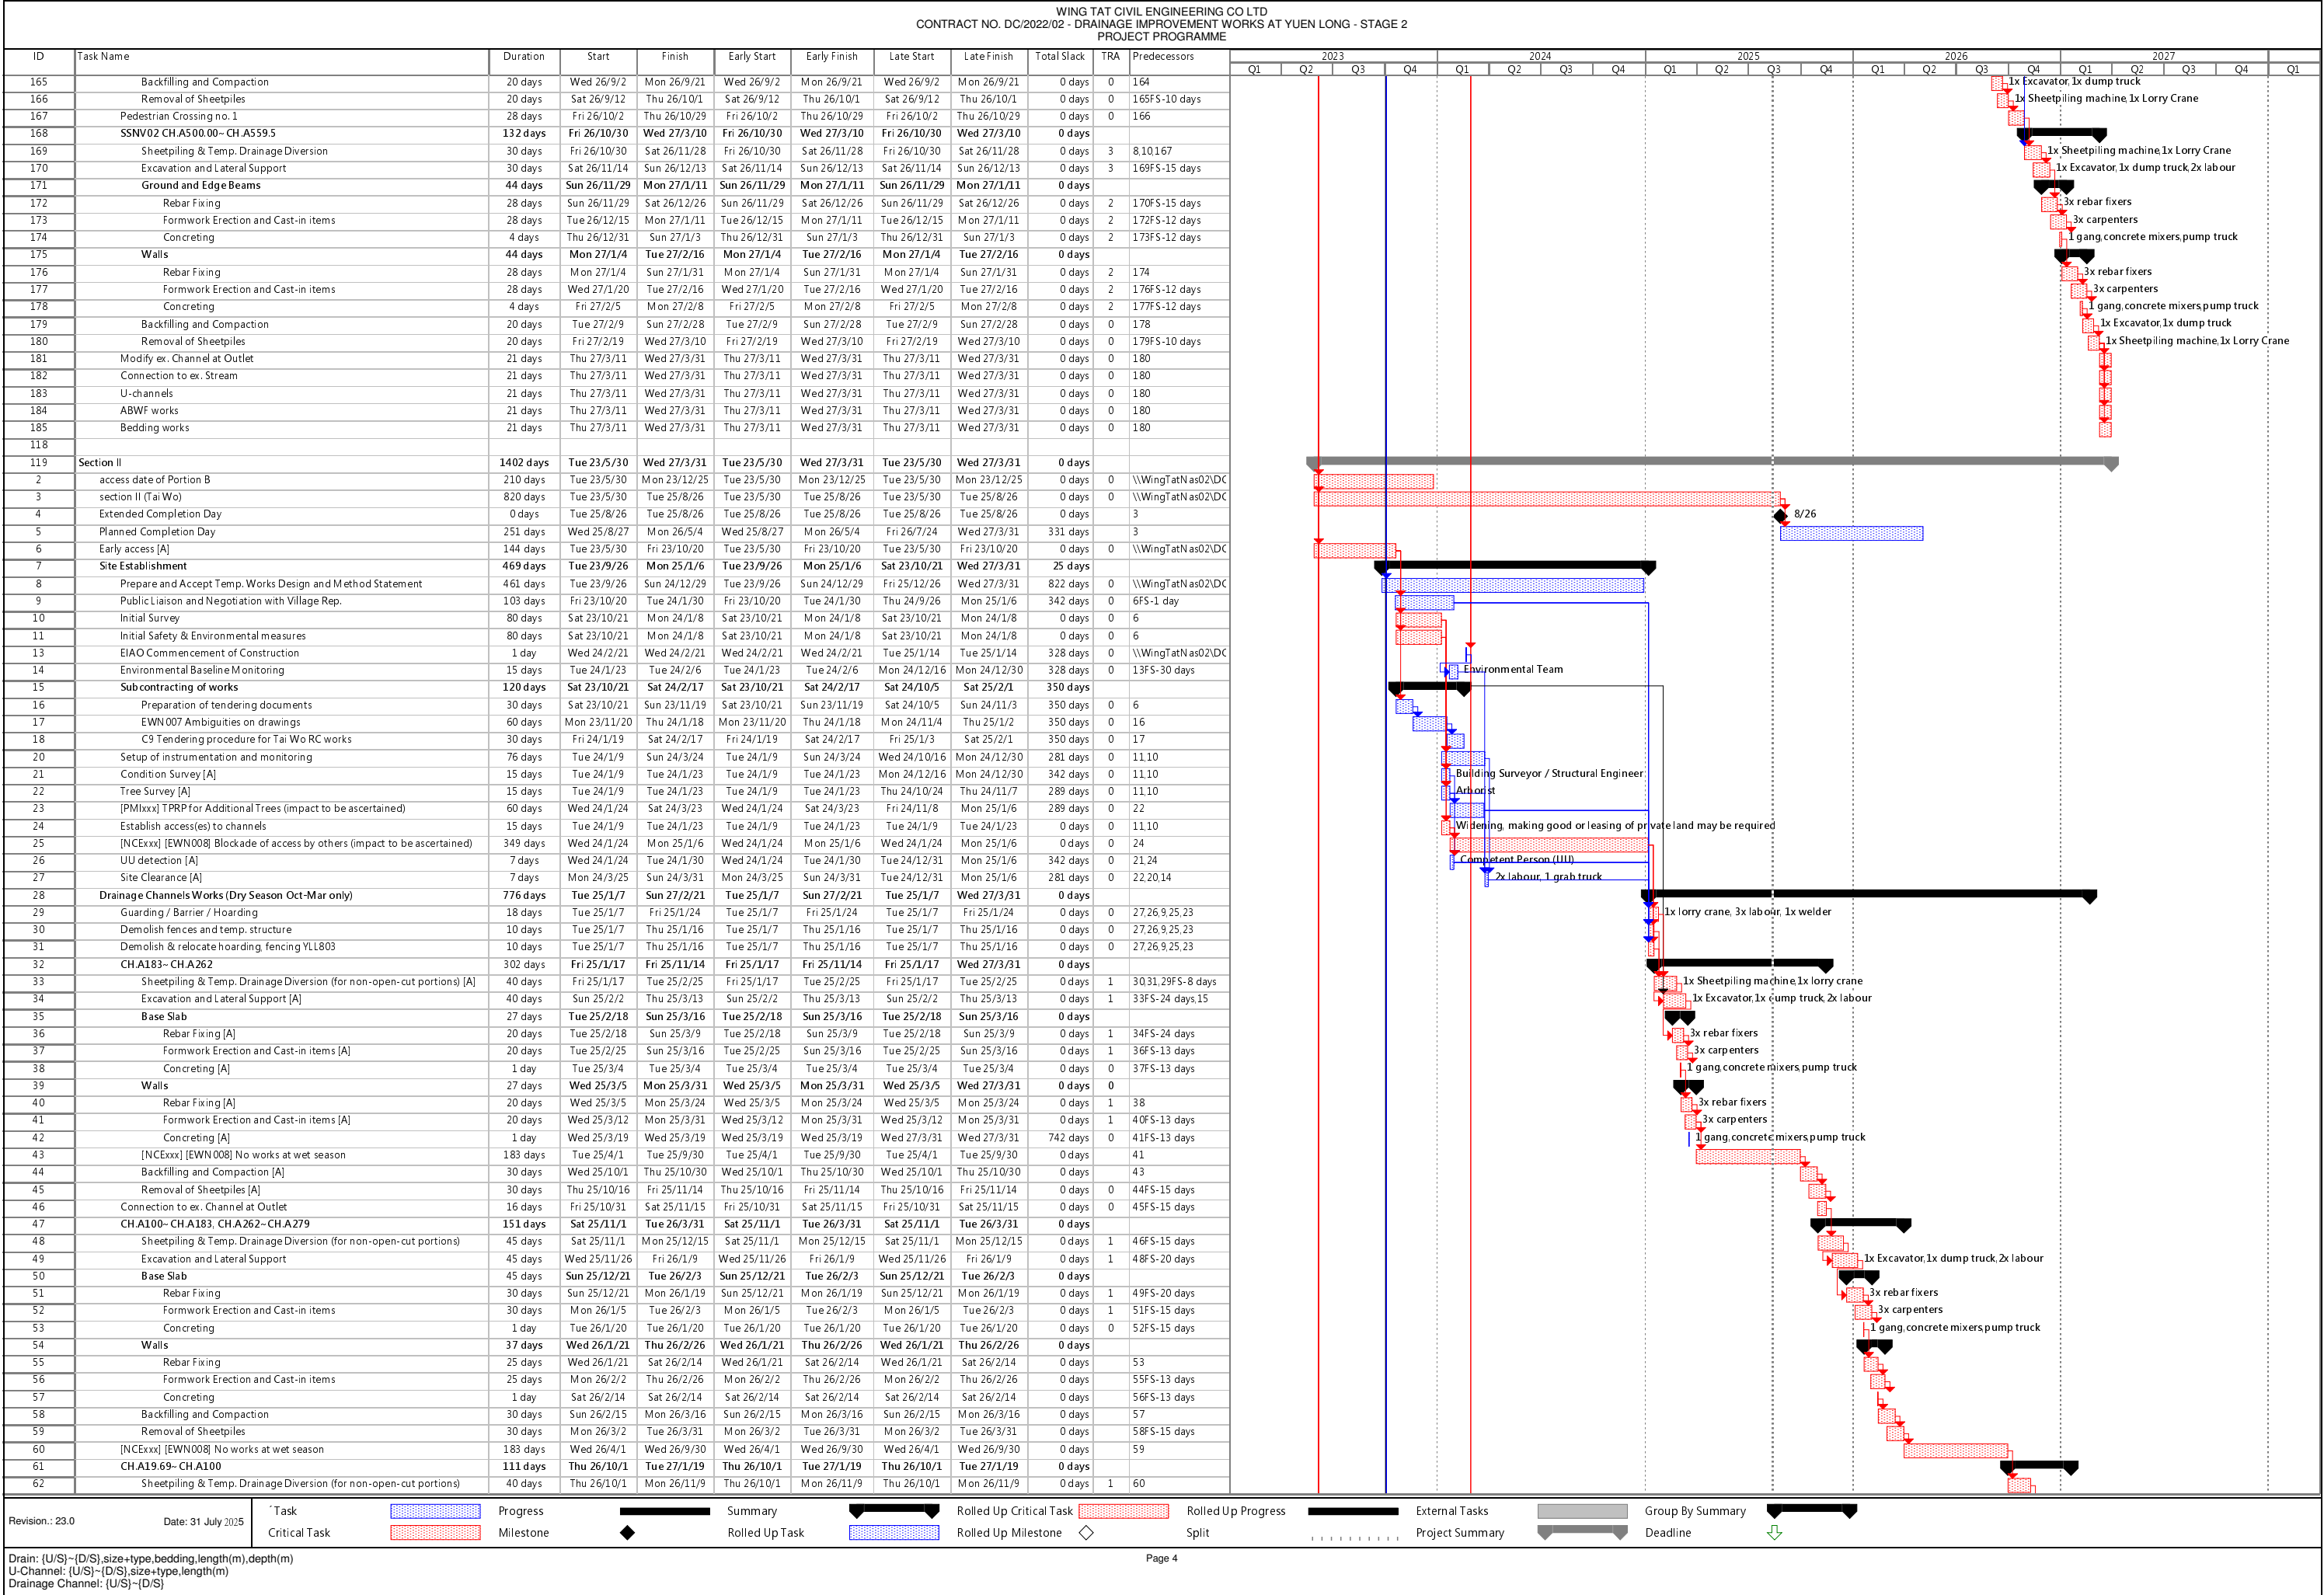

| WING TAT CIVIL ENGINEERING CO LTD                                           |                                                            |           |              |              |              |              |              |              |             |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
|-----------------------------------------------------------------------------|------------------------------------------------------------|-----------|--------------|--------------|--------------|--------------|--------------|--------------|-------------|-----|-------------------|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|--|--|--|--|
| CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2 |                                                            |           |              |              |              |              |              |              |             |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| PROJECT PROGRAMME                                                           |                                                            |           |              |              |              |              |              |              |             |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| ID                                                                          | Task Name                                                  | Duration  | Start        | Finish       | Early Start  | Early Finish | Late Start   | Late Finish  | Total Slack | TRA | Predecessors      | 2023 |    |    |    | 2024 |    |    |    | 2025 |    |    |    | 2026 |    |    |    | 2027 |  |  |  |  |
|                                                                             |                                                            |           |              |              |              |              |              |              |             |     |                   | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   |  |  |  |  |
| 63                                                                          | Excavation and Lateral Support                             | 40 days   | Wed 26/10/21 | Sun 26/11/29 | Wed 26/10/21 | Sun 26/11/29 | Wed 26/10/21 | Sun 26/11/29 | 0 days      | 1   | 62FS-20 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 64                                                                          | Base Slab                                                  | 27 days   | Fri 26/11/6  | Wed 26/12/2  | Fri 26/11/6  | Wed 26/12/2  | Fri 26/11/6  | Wed 26/12/2  | 0 days      |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 65                                                                          | Rebar Fixing                                               | 20 days   | Fri 26/11/6  | Wed 26/11/25 | Fri 26/11/6  | Wed 26/11/25 | Fri 26/11/6  | Wed 26/11/25 | 0 days      | 1   | 63FS-24 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 66                                                                          | Formwork Erection and Cast-in items                        | 20 days   | Fri 26/11/13 | Wed 26/12/2  | Fri 26/11/13 | Wed 26/12/2  | Fri 26/11/13 | Wed 26/12/2  | 0 days      | 1   | 65FS-13 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 67                                                                          | Concreting                                                 | 1 day     | Fri 26/11/20 | Fri 26/11/20 | Fri 26/11/20 | Fri 26/11/20 | Fri 26/11/20 | Fri 26/11/20 | 0 days      | 0   | 66F-S-13 days     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 68                                                                          | Walls                                                      | 27 days   | Sat 26/11/21 | Thu 26/12/17 | Sat 26/11/21 | Thu 26/12/17 | Sat 26/11/21 | Thu 26/12/17 | 0 days      |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 69                                                                          | Rebar Fixing                                               | 20 days   | Sat 26/11/21 | Thu 26/12/10 | Sat 26/11/21 | Thu 26/12/10 | Sat 26/11/21 | Thu 26/12/10 | 0 days      | 1   | 67                |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 70                                                                          | Formwork Erection and Cast-in items                        | 20 days   | Sat 26/11/28 | Thu 26/12/17 | Sat 26/11/28 | Thu 26/12/17 | Sat 26/11/28 | Thu 26/12/17 | 0 days      | 1   | 69FS-13 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 71                                                                          | Concreting                                                 | 1 day     | Sat 26/12/5  | Sat 26/12/5  | Sat 26/12/5  | Sat 26/12/5  | Sat 26/12/5  | Sat 26/12/5  | 0 days      | 0   | 70F-S-13 days     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 72                                                                          | Backfilling and Compaction                                 | 30 days   | Sun 26/12/6  | Mon 27/1/4   | Sun 26/12/6  | Mon 27/1/4   | Sun 26/12/6  | Mon 27/1/4   | 0 days      | 0   | 71                |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 73                                                                          | Removal of Sheetpiles                                      | 30 days   | Mon 26/12/21 | Tue 27/1/19  | Mon 26/12/21 | Tue 27/1/19  | Mon 26/12/21 | Tue 27/1/19  | 0 days      | 0   | 72FS-15 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 74                                                                          | 900pipewith flap valve                                     | 14 days   | Tue 27/1/5   | Mon 27/1/18  | Tue 27/1/5   | Mon 27/1/18  | Tue 27/1/5   | Mon 27/1/18  | 0 days      | 0   | 73FS-15 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 75                                                                          | Box Culvert & Pedestrian Crossing                          | 28 days   | Thu 27/1/14  | Wed 27/2/10  | Thu 27/1/14  | Wed 27/2/10  | Thu 27/1/14  | Wed 27/2/10  | 0 days      | 0   | 74FS-5 days       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 76                                                                          | ABWF works                                                 | 21 days   | Mon 27/2/1   | Sun 27/2/21  | Mon 27/2/1   | Sun 27/2/21  | Thu 27/3/11  | Wed 27/3/31  | 38 days     | 0   | 75FS-10 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 77                                                                          | Bedding works                                              | 21 days   | Mon 27/2/1   | Sun 27/2/21  | Mon 27/2/1   | Sun 27/2/21  | Thu 27/3/11  | Wed 27/3/31  | 38 days     | 0   | 75FS-10 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 78                                                                          | U-Channel Works                                            | 30 days   | Mon 27/2/1   | Tue 27/3/2   | Mon 27/2/1   | Tue 27/3/2   | Mon 27/2/1   | Tue 27/3/2   | 0 days      |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 79                                                                          | CH.A0.00-CH.A16.40,900CU L=16.40                           | 30 days   | Mon 27/2/1   | Tue 27/3/2   | Mon 27/2/1   | Tue 27/3/2   | Mon 27/2/1   | Tue 27/3/2   | 0 days      |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 80                                                                          | Excavation and Lateral Support                             | 30 days   | Mon 27/2/1   | Tue 27/3/2   | Mon 27/2/1   | Tue 27/3/2   | Mon 27/2/1   | Tue 27/3/2   | 0 days      | 1   | 75FS-10 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 81                                                                          | Channel Formwork Erection                                  | 14 days   | Tue 27/2/16  | Mon 27/3/1   | Tue 27/2/16  | Mon 27/3/1   | Tue 27/2/16  | Mon 27/3/1   | 0 days      | 1   | 80FS-15 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 82                                                                          | Concreting                                                 | 1 day     | Mon 27/2/15  | Mon 27/2/15  | Mon 27/2/15  | Mon 27/2/15  | Mon 27/2/15  | Mon 27/2/15  | 0 days      | 0   | 81FS-15 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 83                                                                          | Drain Laying Works                                         | 44 days   | Tue 27/2/16  | Wed 27/3/31  | Tue 27/2/16  | Wed 27/3/31  | Tue 27/2/16  | Wed 27/3/31  | 0 days      |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 84                                                                          | CH.A16.40-CH.A19.69,900PC B,L=3.30,D=1.5                   | 44 days   | Tue 27/2/16  | Wed 27/3/31  | Tue 27/2/16  | Wed 27/3/31  | Tue 27/2/16  | Wed 27/3/31  | 0 days      |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 85                                                                          | Excavation and Lateral Support                             | 30 days   | Tue 27/2/16  | Wed 27/3/17  | Tue 27/2/16  | Wed 27/3/17  | Tue 27/2/16  | Wed 27/3/17  | 0 days      | 0   | 82                |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 86                                                                          | Drain Laying                                               | 20 days   | Wed 27/3/3   | Mon 27/3/22  | Wed 27/3/3   | Mon 27/3/22  | Wed 27/3/3   | Mon 27/3/22  | 0 days      | 0   | 85FS-15 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 87                                                                          | Bedding and Backfilling                                    | 14 days   | Sat 27/3/13  | Fri 27/3/26  | Sat 27/3/13  | Fri 27/3/26  | Sat 27/3/13  | Fri 27/3/26  | 0 days      | 0   | 86FS-10 days      |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 88                                                                          | Reinstatement                                              | 10 days   | Mon 27/3/22  | Wed 27/3/31  | Mon 27/3/22  | Wed 27/3/31  | Mon 27/3/22  | Wed 27/3/31  | 0 days      | 0   | 87FS-5 days       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 120                                                                         |                                                            |           |              |              |              |              |              |              |             |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 121                                                                         | Section III                                                | 1402 days | Tue 23/5/30  | Wed 27/3/31  | Tue 23/5/30  | Wed 27/3/31  | Tue 23/5/30  | Wed 27/3/31  | 0 days      |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 2                                                                           | access date of Portion C1 & C2                             | 270 days  | Tue 23/5/30  | Fri 24/2/23  | Tue 23/5/30  | Fri 24/2/23  | Tue 23/5/30  | Fri 24/2/23  | 0 days      | 0   | \\WingTatNas02\DC |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 3                                                                           | section III (Lin Fa Tei)                                   | 1155 days | Tue 23/5/30  | Mon 26/7/27  | Tue 23/5/30  | Mon 26/7/27  | Tue 23/5/30  | Mon 26/7/27  | 0 days      | 0   | \\WingTatNas02\DC |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 4                                                                           | Extended Completion Day                                    | 35 days   | Tue 26/7/28  | Mon 26/8/31  | Tue 26/7/28  | Mon 26/8/31  | Tue 26/7/28  | Mon 26/8/31  | 0 days      | 3   |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 5                                                                           | Planned Completion Day                                     | 247 days  | Tue 26/7/28  | Wed 27/3/31  | Tue 26/7/28  | Wed 27/3/31  | Tue 26/7/28  | Wed 27/3/31  | 0 days      | 0   | 3                 |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 6                                                                           | Early access (partial) [A]                                 | 200 days  | Tue 23/5/30  | Fri 23/12/15 | Tue 23/5/30  | Fri 23/12/15 | Tue 23/5/30  | Fri 24/2/23  | 70 days     | 0   | \\WingTatNas02\DC |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 7                                                                           | Site Establishment                                         | 989 days  | Tue 23/9/12  | Wed 26/5/27  | Tue 23/9/12  | Wed 26/5/27  | Tue 23/9/12  | Wed 27/3/31  | 0 days      |     |                   |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |  |  |  |  |
| 8                                                                           | Prepare and Accept Temp. Works Design and Method Statement | 975 days  | Tue 23/9/26  | Wed 26/5/27  | Tue 23/9/26  | Wed 26/5/27  | Thu 24/4/25  | Fri 26/12/25 | 212 days    | 0   | \\WingTatNas02\DC |      |    |    |    |      |    | </ |    |      |    |    |    |      |    |    |    |      |  |  |  |  |

WING TAT CIVIL ENGINEERING CO LTD

CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2

PROJECT PROGRAMME

| ID  | Task Name                                               | Duration | Start        | Finish       | Early Start  | Early Finish | Late Start   | Late Finish  | Total Slack | TRA | Predecessors        | 2023 |    |    |    | 2024 |    |    |    | 2025 |    |    |    | 2026 |    |    |    | 2027 |    |    |    |
|-----|---------------------------------------------------------|----------|--------------|--------------|--------------|--------------|--------------|--------------|-------------|-----|---------------------|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|
|     |                                                         |          |              |              |              |              |              |              |             |     |                     | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 |
| 59  | Removal of Sheetpiles                                   | 25 days  | Tue 24/12/17 | Fri 25/1/10  | Tue 24/12/17 | Fri 25/1/10  | Wed 27/2/24  | Sat 27/3/20  | 799 days    | 0   | 58FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 60  | Pedestrian & Vehicular Crossing no. 2 [A]               | 28 days  | Wed 24/12/25 | Tue 25/1/21  | Wed 24/12/25 | Tue 25/1/21  | Tue 27/3/14  | Wed 27/3/31  | 799 days    | 4   | 59FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 61  | LFT05 CH.A163.00~CH.A173.50                             | 72 days  | Wed 24/12/25 | Thu 25/3/6   | Wed 24/12/25 | Thu 25/3/6   | Wed 24/12/25 | Tue 27/3/30  | 0 days      |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 62  | Temp. Drainage Diversion / Sheetpiling [A]              | 27 days  | Wed 24/12/25 | Mon 25/1/20  | Wed 24/12/25 | Mon 25/1/20  | Wed 24/12/25 | Mon 25/1/20  | 0 days      | 0   | 53FS+33 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 63  | Excavation and Lateral Support [A]                      | 27 days  | Mon 25/1/6   | Sat 25/2/1   | Mon 25/1/6   | Sat 25/2/1   | Mon 25/1/6   | Sat 25/2/1   | 0 days      | 0   | 62FS-15 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 64  | Ground and Edge Beams                                   | 33 days  | Thu 25/1/16  | Mon 25/2/17  | Thu 25/1/16  | Mon 25/2/17  | Thu 25/1/16  | Mon 25/2/17  | 0 days      |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 65  | Rebar Fixing [A]                                        | 25 days  | Thu 25/1/16  | Sun 25/2/9   | Thu 25/1/16  | Sun 25/2/9   | Thu 25/1/16  | Sun 25/2/9   | 0 days      | 0   | 63FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 66  | Formwork Erection and Cast-in items [A]                 | 25 days  | Fri 25/1/24  | Mon 25/2/17  | Fri 25/1/24  | Mon 25/2/17  | Fri 25/1/24  | Mon 25/2/17  | 0 days      | 0   | 65FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 67  | Concreting [A]                                          | 1 day    | Sat 25/2/1   | Sat 25/2/1   | Sat 25/2/1   | Sat 25/2/1   | Sat 25/2/1   | Sat 25/2/1   | 0 days      | 0   | 66FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 68  | Walls                                                   | 33 days  | Sun 25/2/2   | Thu 25/3/6   | Sun 25/2/2   | Thu 25/3/6   | Fri 27/2/26  | Tue 27/3/30  | 754 days    |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 69  | Rebar Fixing                                            | 25 days  | Sun 25/2/2   | Wed 25/2/26  | Sun 25/2/2   | Wed 25/2/26  | Fri 27/2/26  | Mon 27/3/22  | 754 days    | 0   | 67                  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 70  | Formwork Erection and Cast-in items                     | 25 days  | Mon 25/2/10  | Thu 25/3/6   | Mon 25/2/10  | Thu 25/3/6   | Sat 27/3/6   | Tue 27/3/30  | 754 days    | 0   | 69FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 71  | Concreting                                              | 1 day    | Tue 25/2/18  | Tue 25/2/18  | Tue 25/2/18  | Tue 25/2/18  | Sun 27/3/14  | Sun 27/3/14  | 754 days    | 0   | 70FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 72  | Backfilling and Compaction                              | 10 days  | Wed 25/2/19  | Fri 25/2/28  | Wed 25/2/19  | Fri 25/2/28  | Mon 27/3/15  | Wed 27/3/24  | 754 days    | 0   | 71                  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 73  | Removal of Sheetpiles                                   | 10 days  | Sat 25/2/22  | Mon 25/3/3   | Sat 25/2/22  | Mon 25/3/3   | Thu 27/3/18  | Sat 27/3/27  | 754 days    | 0   | 72FS-7 days         |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 74  | Animal Escape Ramps                                     | 21 days  | Sat 25/2/15  | Fri 25/3/7   | Sat 25/2/15  | Fri 25/3/7   | Thu 27/3/11  | Wed 27/3/31  | 754 days    | 0   | 73FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 75  | Demolish & relocate retaining wall YLL 796/A/5-6 [A]    | 30 days  | Sat 25/2/15  | Sun 25/3/16  | Sat 25/2/15  | Sun 25/3/16  | Sat 25/2/15  | Sun 25/3/16  | 0 days      | 0   | 67FS+13 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 76  | Demolish & relocate AFCD Weir & pedestrian crossing [A] | 30 days  | Sat 25/2/15  | Sun 25/3/16  | Sat 25/2/15  | Sun 25/3/16  | Sat 25/2/15  | Sun 25/3/16  | 0 days      | 0   | 67FS+13 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 77  | LFT07 CH.A300.75~CH.A360.0                              | 89 days  | Tue 25/2/25  | Tue 25/5/24  | Tue 25/2/25  | Sat 25/5/24  | Tue 25/2/25  | Wed 27/3/31  | 0 days      |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 78  | Temp. Drainage Diversion / Sheetpiling [A]              | 25 days  | Tue 25/2/25  | Fri 25/3/21  | Tue 25/2/25  | Fri 25/3/21  | Tue 25/2/25  | Fri 25/3/21  | 0 days      |     | 75FS-20 days, 76FS- |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 79  | Excavation and Lateral Support [A]                      | 25 days  | Fri 25/3/7   | Mon 25/3/31  | Fri 25/3/7   | Mon 25/3/31  | Fri 25/3/7   | Mon 25/3/31  | 0 days      |     | 78FS-15 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 80  | Ground and Edge Beams                                   | 28 days  | Mon 25/3/17  | Sun 25/4/13  | Mon 25/3/17  | Sun 25/4/13  | Mon 25/3/17  | Sun 25/4/13  | 0 days      |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 81  | Rebar Fixing [A]                                        | 20 days  | Mon 25/3/17  | Sat 25/4/5   | Mon 25/3/17  | Sat 25/4/5   | Mon 25/3/17  | Sat 25/4/5   | 0 days      |     | 79FS-15 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 82  | Formwork Erection and Cast-in items [A]                 | 20 days  | Tue 25/3/25  | Sun 25/4/13  | Tue 25/3/25  | Sun 25/4/13  | Tue 25/3/25  | Sun 25/4/13  | 0 days      |     | 81FS-12 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 83  | Concreting [A]                                          | 1 day    | Wed 25/4/2   | Wed 25/4/2   | Wed 25/4/2   | Wed 25/4/2   | Wed 25/4/2   | Wed 25/4/2   | 0 days      |     | 82FS-12 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 84  | Walls                                                   | 28 days  | Thu 25/4/3   | Wed 25/4/30  | Thu 25/4/3   | Wed 25/4/30  | Mon 27/2/8   | Sun 27/3/7   | 676 days    |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 85  | Rebar Fixing [A]                                        | 20 days  | Thu 25/4/3   | Tue 25/4/22  | Thu 25/4/3   | Tue 25/4/22  | Mon 27/2/8   | Sat 27/2/27  | 676 days    |     | 83                  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 86  | Formwork Erection and Cast-in items [A]                 | 20 days  | Fri 25/4/11  | Wed 25/4/30  | Fri 25/4/11  | Wed 25/4/30  | Tue 27/2/16  | Sun 27/3/7   | 676 days    |     | 85FS-12 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 87  | Concreting [A]                                          | 1 day    | Sat 25/4/19  | Sat 25/4/19  | Sat 25/4/19  | Sat 25/4/19  | Wed 27/2/24  | Wed 27/2/24  | 676 days    |     | 86FS-12 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 88  | Backfilling and Compaction [A]                          | 25 days  | Sun 25/4/20  | Wed 25/5/14  | Sun 25/4/20  | Wed 25/5/14  | Thu 27/2/25  | Sun 27/3/21  | 676 days    |     | 87                  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 89  | Removal of Sheetpiles [A]                               | 25 days  | Wed 25/4/30  | Sat 25/5/24  | Wed 25/4/30  | Sat 25/5/24  | Sun 27/3/7   | Wed 27/3/31  | 676 days    |     | 88FS-15 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 90  | LFT02 CH.A100.00~CH.A163.00                             | 85 days  | Thu 25/4/10  | Thu 25/7/3   | Thu 25/4/10  | Thu 25/7/3   | Thu 25/4/10  | Sat 27/3/27  | 0 days      |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 91  | Temp. Drainage Diversion / Sheetpiling [A]              | 25 days  | Thu 25/4/10  | Sun 25/5/4   | Thu 25/4/10  | Sun 25/5/4   | Thu 25/4/10  | Sun 25/5/4   | 0 days      | 0   | 83FS+7 days         |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 92  | Excavation and Lateral Support [A]                      | 25 days  | Sun 25/4/20  | Sun 25/5/14  | Sun 25/4/20  | Sun 25/5/14  | Wed 25/5/14  | Wed 25/5/14  | 0 days      | 0   | 91FS-15 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 93  | Ground and Edge Beams                                   | 33 days  | Mon 25/4/28  | Fri 25/5/30  | Mon 25/4/28  | Fri 25/5/30  | Mon 25/4/28  | Fri 25/5/30  | 0 days      |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 94  | Rebar Fixing [A]                                        | 25 days  | Mon 25/4/28  | Thu 25/5/22  | Mon 25/4/28  | Thu 25/5/22  | Mon 25/4/28  | Thu 25/5/22  | 0 days      | 0   | 92FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 95  | Formwork Erection and Cast-in items [A]                 | 25 days  | Tue 25/5/6   | Fri 25/5/30  | Tue 25/5/6   | Fri 25/5/30  | Tue 25/5/6   | Fri 25/5/30  | 0 days      | 0   | 94FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 96  | Concreting [A]                                          | 1 day    | Wed 25/5/14  | Wed 25/5/14  | Wed 25/5/14  | Wed 25/5/14  | Wed 25/5/14  | Wed 25/5/14  | 0 days      | 0   | 95FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 97  | Walls                                                   | 33 days  | Thu 25/5/15  | Mon 25/6/16  | Thu 25/5/15  | Mon 25/6/16  | Sat 27/2/6   | Wed 27/3/10  | 632 days    |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 98  | Rebar Fixing                                            | 25 days  | Thu 25/5/15  | Sun 25/6/8   | Thu 25/5/15  | Sun 25/6/8   | Sat 27/2/6   | Tue 27/3/2   | 632 days    | 0   | 96                  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 99  | Formwork Erection and Cast-in items                     | 25 days  | Fri 25/5/23  | Mon 25/6/16  | Fri 25/5/23  | Mon 25/6/16  | Sun 27/2/14  | Wed 27/3/10  | 632 days    | 0   | 98FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 100 | Concreting                                              | 1 day    | Sat 25/5/31  | Sat 25/5/31  | Sat 25/5/31  | Sat 25/5/31  | Mon 27/2/22  | Mon 27/2/22  | 632 days    | 0   | 99FS-17 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 101 | Backfilling and Compaction                              | 25 days  | Sun 25/6/1   | Wed 25/6/25  | Sun 25/6/1   | Wed 25/6/25  | Tue 27/2/23  | Fri 27/3/19  | 632 days    | 0   | 100                 |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 102 | Removal of Sheetpiles                                   | 25 days  | Mon 25/6/9   | Thu 25/7/3   | Mon 25/6/9   | Thu 25/7/3   | Wed 27/3/3   | Sat 27/3/27  | 632 days    | 0   | 101FS-17 days       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 103 | Pedestrian Crossing no. 2                               | 21 days  | Tue 25/6/17  | Mon 25/7/7   | Tue 25/6/17  | Mon 25/7/7   | Thu 27/3/11  | Wed 27/3/31  | 632 days    | 3   | 102FS-17 days       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 104 | Demolish & relocate retaining wall YLL 796/A/14-15      | 30 days  | Tue 25/6/17  | Wed 25/7/16  | Tue 25/6/17  | Wed 25/7/16  | Tue 25/6/17  | Wed 25/7/16  | 0 days      | 0   | 96FS+33 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 105 | LFT08 CH.A360.0~CH.A391.0                               | 117 days | Sun 25/6/22  | Thu 25/10/16 | Sun 25/6/22  | Thu 25/10/16 | Sun 25/6/22  | Thu 25/10/16 | 0 days      |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 106 | Temp. Drainage Diversion / Sheetpiling                  | 35 days  | Sun 25/6/22  | Sat 25/7/26  | Sun 25/6/22  | Sat 25/7/26  | Sun 25/6/22  | Sat 25/7/26  | 0 days      | 1   | 104FS-25 days       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 107 | Excavation and Lateral Support                          | 35 days  | Thu 25/7/17  | Wed 25/8/20  | Thu 25/7/17  | Wed 25/8/20  | Thu 25/7/17  | Wed 25/8/20  | 0 days      | 1   | 106FS-10 days       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 108 | Ground and Edge Beams                                   | 35 days  | Mon 25/8/11  | Sun 25/9/14  | Mon 25/8/11  | Sun 25/9/14  | Mon 25/8/11  | Sun 25/9/14  | 0 days      |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 109 | Rebar Fixing                                            | 25 days  | Mon 25/8/11  | Thu 25/8/11  | Mon 25/8/11  | Thu 25/8/11  | Mon 25/8/11  | Thu 25/8/11  | 0 days      | 1   | 107FS-10 days       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 110 | Formwork Erection and Cast-in items                     | 25 days  | Thu 25/8/21  | Sun 25/9/14  | Thu 25/8/21  | Sun 25/9/14  | Thu 25/8/21  | Sun 25/9/14  | 0 days      | 1   | 109FS-15 days       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 111 | Concreting                                              | 1 day    | Sun 25/8/31  | Sun 25/8/31  | Sun 25/8/31  | Sun 25/8/31  | Sun 25/8/31  | Sun 25/8/31  | 0 days      | 0   | 110FS-15 days       |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 112 | Walls                                                   | 35 days  | Mon 25/9/1   | Sun 25/10/5  | Mon 25/9/1   | Sun 25/10/5  | Mon 25/9/1   | Sun 25/10/5  | 0 days      |     |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |
| 113 | Rebar Fixing                                            | 25 days  | Mon 25/9/1   | Thu 25/9/25  | Mon 25/9/1   | Thu 25/9/25  | Mon 25/9/1   | Thu 25/9/25  | 0 days      | 1   | 111                 |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    | </ |      |    |    |    |



[illegible]


WING TAT CIVIL ENGINEERING CO LTD

CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2


PROJECT PROGRAMME


| ID  | Task Name                                                                                                                     | Duration  | Start        | Finish       | Early Start  | Early Finish | Late Start   | Late Finish  | Total Slack | TRA | Predecessors      | 2023 |  |  |  | 2024 |  |  |  | 2025 |  |  |  | 2026 |  |  |  | 2027 |  |  |  | Q1 |
|-----|-------------------------------------------------------------------------------------------------------------------------------|-----------|--------------|--------------|--------------|--------------|--------------|--------------|-------------|-----|-------------------|------|--|--|--|------|--|--|--|------|--|--|--|------|--|--|--|------|--|--|--|----|
| 223 | Formwork Erection and Cast-in items                                                                                           | 25 days   | Mon 25/9/22  | Thu 25/10/16 | Mon 25/9/22  | Thu 25/10/16 | Fri 26/8/21  | Mon 26/9/14  | 333 days    | 1   | 222FS-17 days     |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 224 | Concreting                                                                                                                    | 1 day     | Tue 25/9/30  | Tue 25/9/30  | Tue 25/9/30  | Tue 25/9/30  | Sat 26/8/29  | Sat 26/8/29  | 333 days    | 0   | 223FS-17 days     |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 225 | Backfilling and Compaction                                                                                                    | 25 days   | Wed 25/10/1  | Sat 25/10/25 | Wed 25/10/1  | Sat 25/10/25 | Sun 26/8/30  | Wed 26/9/23  | 333 days    | 0   | 224               |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 226 | Removal of Sheetpiles                                                                                                         | 25 days   | Thu 25/10/9  | Sun 25/11/2  | Thu 25/10/9  | Sun 25/11/2  | Mon 26/9/7   | Thu 26/10/1  | 333 days    | 0   | 225FS-17 days     |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 227 | Pedestrian Crossing no. 3                                                                                                     | 21 days   | Fri 25/10/17 | Thu 25/11/6  | Fri 25/10/17 | Thu 25/11/6  | Tue 26/9/15  | Mon 26/10/5  | 333 days    | 3   | 226FS-17 days     |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 122 |                                                                                                                               |           |              |              |              |              |              |              |             |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 123 | Section VI                                                                                                                    | 1327 days | Mon 23/5/15  | Thu 26/12/31 | Mon 23/5/15  | Thu 26/12/31 | Tue 23/5/30  | Thu 26/12/31 | 0 days      |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 2   | access date of Portion C3                                                                                                     | 0 days    | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Mon 23/5/29  | Mon 24/2/5   | Mon 24/2/5   | 252 days    | 0   | \\WingTatNas02\DC |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 3   | section VI (Lin Fa Tei - Kam Sheung Road)                                                                                     | 820 days  | Tue 23/5/30  | Tue 25/8/26  | Tue 23/5/30  | Tue 25/8/26  | Tue 23/5/30  | Tue 25/8/26  | 0 days      | 0   | \\WingTatNas02\DC |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 4   | Planned Completion Day                                                                                                        | 492 days  | Wed 25/8/27  | Thu 26/12/31 | Wed 25/8/27  | Thu 26/12/31 | Wed 25/8/27  | Thu 26/12/31 | 0 days      | 0   | 3                 |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 5   | Site Establishment                                                                                                            | 868 days  | Mon 23/5/15  | Sun 25/9/28  | Mon 23/5/15  | Sun 25/9/28  | Mon 24/3/4   | Thu 26/12/31 | 294 days    |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 6   | Prepare and Accept Temp. Works Design and Method Statement [A]                                                                | 734 days  | Tue 23/9/26  | Sun 25/9/28  | Tue 23/9/26  | Sun 25/9/28  | Fri 24/11/1  | Wed 26/11/4  | 402 days    | 0   | \\WingTatNas02\DC |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 7   | Public Liaison and Negotiation with Village Rep. [A]                                                                          | 194 days  | Tue 23/9/12  | Sat 24/3/23  | Tue 23/9/12  | Sat 24/3/23  | Tue 24/7/30  | Sat 25/2/8   | 322 days    | 0   | \\WingTatNas02\DC |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 8   | Initial Survey [A]                                                                                                            | 868 days  | Mon 23/5/15  | Sun 25/9/28  | Mon 23/5/15  | Sun 25/9/28  | Thu 24/6/20  | Wed 26/11/4  | 402 days    | 0   |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 10  | Initial Safety & Environmental measures                                                                                       | 60 days   | Thu 24/1/4   | Mon 24/3/4   | Thu 24/1/4   | Mon 24/3/4   | Mon 26/11/2  | Thu 26/12/31 | 1033 days   | 0   | 15SF              |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 12  | Setup of instrumentation and monitoring                                                                                       | 25 days   | Thu 24/2/8   | Mon 24/3/4   | Thu 24/2/8   | Mon 24/3/4   | Mon 26/12/7  | Thu 26/12/31 | 1033 days   | 0   | 15SF              |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 13  | Tree Survey                                                                                                                   | 25 days   | Thu 24/2/8   | Mon 24/3/4   | Thu 24/2/8   | Mon 24/3/4   | Mon 26/12/7  | Thu 26/12/31 | 1033 days   | 0   | 15SF              |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 14  | UU detection                                                                                                                  | 25 days   | Thu 24/2/8   | Mon 24/3/4   | Thu 24/2/8   | Mon 24/3/4   | Mon 26/12/7  | Thu 26/12/31 | 1033 days   | 0   | 15SF              |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 15  | [NCExxx] [PMI-03] Difficulty/infeasibility for construction of 1650mm dia. pipe at Kam Sheung Road (impact to be ascertained) | 522 days  | Mon 24/3/4   | Thu 25/8/7   | Mon 24/3/4   | Thu 25/8/7   | Mon 24/3/4   | Thu 25/8/7   | 0 days      | 0   |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 16  | Temporary Traffic Arrangement                                                                                                 | 550 days  | Mon 23/5/29  | Thu 24/11/28 | Mon 23/5/29  | Thu 24/11/28 | Mon 24/2/5   | Thu 25/8/7   | 252 days    |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 17  | Application of XP [A]                                                                                                         | 400 days  | Mon 23/5/29  | Mon 24/7/1   | Mon 23/5/29  | Mon 24/7/1   | Mon 24/2/5   | Mon 25/3/10  | 252 days    | 0   | 2FS-1 day         |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 18  | Submission of TTA and Arrange TMLG [A]                                                                                        | 370 days  | Mon 23/5/29  | Sat 24/6/1   | Mon 23/5/29  | Sat 24/6/1   | Mon 24/2/5   | Sat 25/2/8   | 252 days    | 0   | 2FS-1 day         |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 19  | Approval of TTA [A]                                                                                                           | 30 days   | Sun 24/6/2   | Mon 24/7/1   | Sun 24/6/2   | Mon 24/7/1   | Sun 25/2/9   | Mon 25/3/10  | 252 days    | 0   | 17FF,18.7         |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 20  | [NCExxx] [PMI-03] Submission of revised TTA and Arrange TMLG                                                                  | 120 days  | Tue 24/7/2   | Tue 24/10/29 | Tue 24/7/2   | Tue 24/10/29 | Tue 25/3/11  | Tue 25/7/8   | 252 days    | 0   | 19                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 21  | [NCExxx] [PMI-03] Approval of revised TTA                                                                                     | 30 days   | Wed 24/10/30 | Thu 24/11/28 | Wed 24/10/30 | Thu 24/11/28 | Wed 25/7/9   | Thu 25/8/7   | 252 days    | 0   | 20                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 22  | Drain Laying Works                                                                                                            | 913 days  | Tue 24/7/2   | Thu 26/12/31 | Tue 24/7/2   | Thu 26/12/31 | Mon 25/6/9   | Thu 26/12/31 | 0 days      |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 23  | Inspection Pit                                                                                                                | 60 days   | Tue 24/7/2   | Fri 24/8/30  | Tue 24/7/2   | Fri 24/8/30  | Mon 25/6/9   | Thu 25/8/7   | 342 days    | 0   | 19                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 24  | [NCExxx] [PMI-03] Procurement, sampling and testing of drain pipes                                                            | 60 days   | Mon 25/6/9   | Thu 25/8/7   | Mon 25/6/9   | Thu 25/8/7   | Mon 25/6/9   | Thu 25/8/7   | 0 days      | 0   | 15FS-60 days      |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 25  | LFT.D3a~LFT.D4,1650PC,B,L=22.88,D=3.418                                                                                       | 47 days   | Fri 25/8/8   | Tue 25/9/23  | Fri 25/8/8   | Tue 25/9/23  | Fri 25/8/8   | Tue 25/9/23  | 0 days      |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 26  | TTA Implementation                                                                                                            | 2 days    | Fri 25/8/8   | Sat 25/8/9   | Fri 25/8/8   | Sat 25/8/9   | Fri 25/8/8   | Sat 25/8/9   | 0 days      | 0   | 15.21,23,24       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 27  | Breaking Ground                                                                                                               | 8 days    | Fri 25/8/8   | Fri 25/8/15  | Fri 25/8/8   | Fri 25/8/15  | Fri 25/8/8   | Fri 25/8/15  | 0 days      | 0   | 26FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 28  | Excavation and Lateral Support                                                                                                | 10 days   | Tue 25/8/14  | Sat 25/8/23  | Tue 25/8/14  | Sat 25/8/23  | Thu 25/8/14  | Sat 25/8/23  | 0 days      | 2   | 27FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 29  | Drain Laying                                                                                                                  | 10 days   | Fri 25/8/22  | Sun 25/8/31  | Fri 25/8/22  | Sun 25/8/31  | Fri 25/8/22  | Sun 25/8/31  | 0 days      | 2   | 28FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 30  | Bedding and Backfilling                                                                                                       | 8 days    | Sat 25/8/30  | Sat 25/9/6   | Sat 25/8/30  | Sat 25/9/6   | Sat 25/8/30  | Sat 25/9/6   | 0 days      | 0   | 29FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 31  | Manhole Construction                                                                                                          | 10 days   | Fri 25/9/5   | Sun 25/9/14  | Fri 25/9/5   | Sun 25/9/14  | Fri 25/9/5   | Sun 25/9/14  | 0 days      | 2   | 30FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 32  | Reinstatement                                                                                                                 | 8 days    | Mon 25/9/15  | Mon 25/9/22  | Mon 25/9/15  | Mon 25/9/22  | Mon 25/9/15  | Mon 25/9/22  | 0 days      | 0   | 31                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 33  | TTA Removal                                                                                                                   | 1 day     | Tue 25/9/23  | Tue 25/9/23  | Tue 25/9/23  | Tue 25/9/23  | Tue 25/9/23  | Tue 25/9/23  | 0 days      | 0   | 32                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 34  | LFT.D4~LFT.D5,1650PC,B,L=50.95,D=3.417                                                                                        | 91 days   | Wed 25/9/24  | Tue 25/12/23 | Wed 25/9/24  | Tue 25/12/23 | Wed 25/9/24  | Tue 25/12/23 | 0 days      |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 35  | Stage 1                                                                                                                       | 52 days   | Wed 25/9/24  | Fri 25/11/14 | Wed 25/9/24  | Fri 25/11/14 | Wed 25/9/24  | Fri 25/11/14 | 0 days      |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 36  | TTA Implementation                                                                                                            | 2 days    | Wed 25/9/24  | Thu 25/9/25  | Wed 25/9/24  | Thu 25/9/25  | Wed 25/9/24  | Thu 25/9/25  | 0 days      | 0   | 33                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 37  | Breaking Ground                                                                                                               | 10 days   | Wed 25/9/24  | Fri 25/10/3  | Wed 25/9/24  | Fri 25/10/3  | Wed 25/9/24  | Fri 25/10/3  | 0 days      | 2   | 36FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 38  | Excavation and Lateral Support                                                                                                | 12 days   | Thu 25/10/2  | Mon 25/10/13 | Thu 25/10/2  | Mon 25/10/13 | Thu 25/10/2  | Mon 25/10/13 | 0 days      | 2   | 37FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 39  | Drain Laying                                                                                                                  | 10 days   | Sun 25/10/12 | Tue 25/10/21 | Sun 25/10/12 | Tue 25/10/21 | Sun 25/10/12 | Tue 25/10/21 | 0 days      | 2   | 38FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 40  | Bedding and Backfilling                                                                                                       | 8 days    | Mon 25/10/20 | Mon 25/10/27 | Mon 25/10/20 | Mon 25/10/27 | Mon 25/10/20 | Mon 25/10/27 | 0 days      | 0   | 39FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 41  | Manhole Construction                                                                                                          | 10 days   | Sun 25/10/26 | Tue 25/11/4  | Sun 25/10/26 | Tue 25/11/4  | Sun 25/10/26 | Tue 25/11/4  | 0 days      | 2   | 40FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 42  | Reinstatement                                                                                                                 | 8 days    | Wed 25/11/5  | Wed 25/11/12 | Wed 25/11/5  | Wed 25/11/12 | Wed 25/11/5  | Wed 25/11/12 | 0 days      | 0   | 41                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 43  | TTA Removal                                                                                                                   | 2 days    | Thu 25/11/13 | Fri 25/11/14 | Thu 25/11/13 | Fri 25/11/14 | Thu 25/11/13 | Fri 25/11/14 | 0 days      | 0   | 42                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 44  | Stage 2                                                                                                                       | 39 days   | Sat 25/11/15 | Tue 25/12/23 | Sat 25/11/15 | Tue 25/12/23 | Sat 25/11/15 | Tue 25/12/23 | 0 days      |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 45  | TTA Implementation                                                                                                            | 2 days    | Sat 25/11/15 | Sun 25/11/16 | Sat 25/11/15 | Sun 25/11/16 | Sat 25/11/15 | Sun 25/11/16 | 0 days      | 0   | 43                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 46  | Breaking Ground                                                                                                               | 8 days    | Sat 25/11/15 | Sat 25/11/22 | Sat 25/11/15 | Sat 25/11/22 | Sat 25/11/15 | Sat 25/11/22 | 0 days      | 2   | 45FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 47  | Excavation and Lateral Support                                                                                                | 10 days   | Fri 25/11/21 | Sun 25/11/30 | Fri 25/11/21 | Sun 25/11/30 | Fri 25/11/21 | Sun 25/11/30 | 0 days      | 2   | 46FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 48  | Drain Laying                                                                                                                  | 8 days    | Sat 25/11/29 | Sat 25/12/6  | Sat 25/11/29 | Sat 25/12/6  | Sat 25/11/29 | Sat 25/12/6  | 0 days      | 2   | 47FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 49  | Bedding and Backfilling                                                                                                       | 6 days    | Fri 25/12/5  | Wed 25/12/10 | Fri 25/12/5  | Wed 25/12/10 | Fri 25/12/5  | Wed 25/12/10 | 0 days      | 0   | 48FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 50  | Manhole Construction                                                                                                          | 8 days    | Tue 25/12/9  | Tue 25/12/16 | Tue 25/12/9  | Tue 25/12/16 | Tue 25/12/9  | Tue 25/12/16 | 0 days      | 2   | 49FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 51  | Reinstatement                                                                                                                 | 6 days    | Wed 25/12/17 | Mon 25/12/22 | Mon 25/12/17 | Mon 25/12/22 | Mon 25/12/17 | Mon 25/12/22 | 0 days      | 0   | 50                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 52  | TTA Removal                                                                                                                   | 1 day     | Tue 25/12/23 | Tue 25/12/23 | Tue 25/12/23 | Tue 25/12/23 | Tue 25/12/23 | Tue 25/12/23 | 0 days      | 0   | 51                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 53  | LFT.D5~NKT Channel,1650PC,B,L=14.5,D=3.54                                                                                     | 52 days   | Wed 25/12/24 | Fri 26/2/13  | Wed 25/12/24 | Fri 26/2/13  | Wed 25/12/24 | Fri 26/2/13  | 0 days      |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 54  | TTA Implementation (trial run)                                                                                                | 4 days    | Wed 25/12/24 | Sat 25/12/27 | Wed 25/12/24 | Sat 25/12/27 | Wed 25/12/24 | Sat 25/12/27 | 0 days      | 0   | 52                |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 55  | Breaking Ground                                                                                                               | 10 days   | Fri 25/12/26 | Sun 26/1/4   | Fri 25/12/26 | Sun 26/1/4   | Fri 25/12/26 | Sun 26/1/4   | 0 days      | 0   | 54FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 56  | Excavation and Lateral Support                                                                                                | 13 days   | Sat 26/1/3   | Thu 26/1/15  | Sat 26/1/3   | Thu 26/1/15  | Sat 26/1/3   | Thu 26/1/15  | 0 days      | 1   | 55FS-2 days       |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |
| 57  | Drain Laying                                                                                                                  | 10 days   | Wed 26/1/14  | Fri 26/1/23  | Wed 26/1/14  | Fri 26/1/23  | Wed 26/1/    |              |             |     |                   |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |      |  |  |  |    |



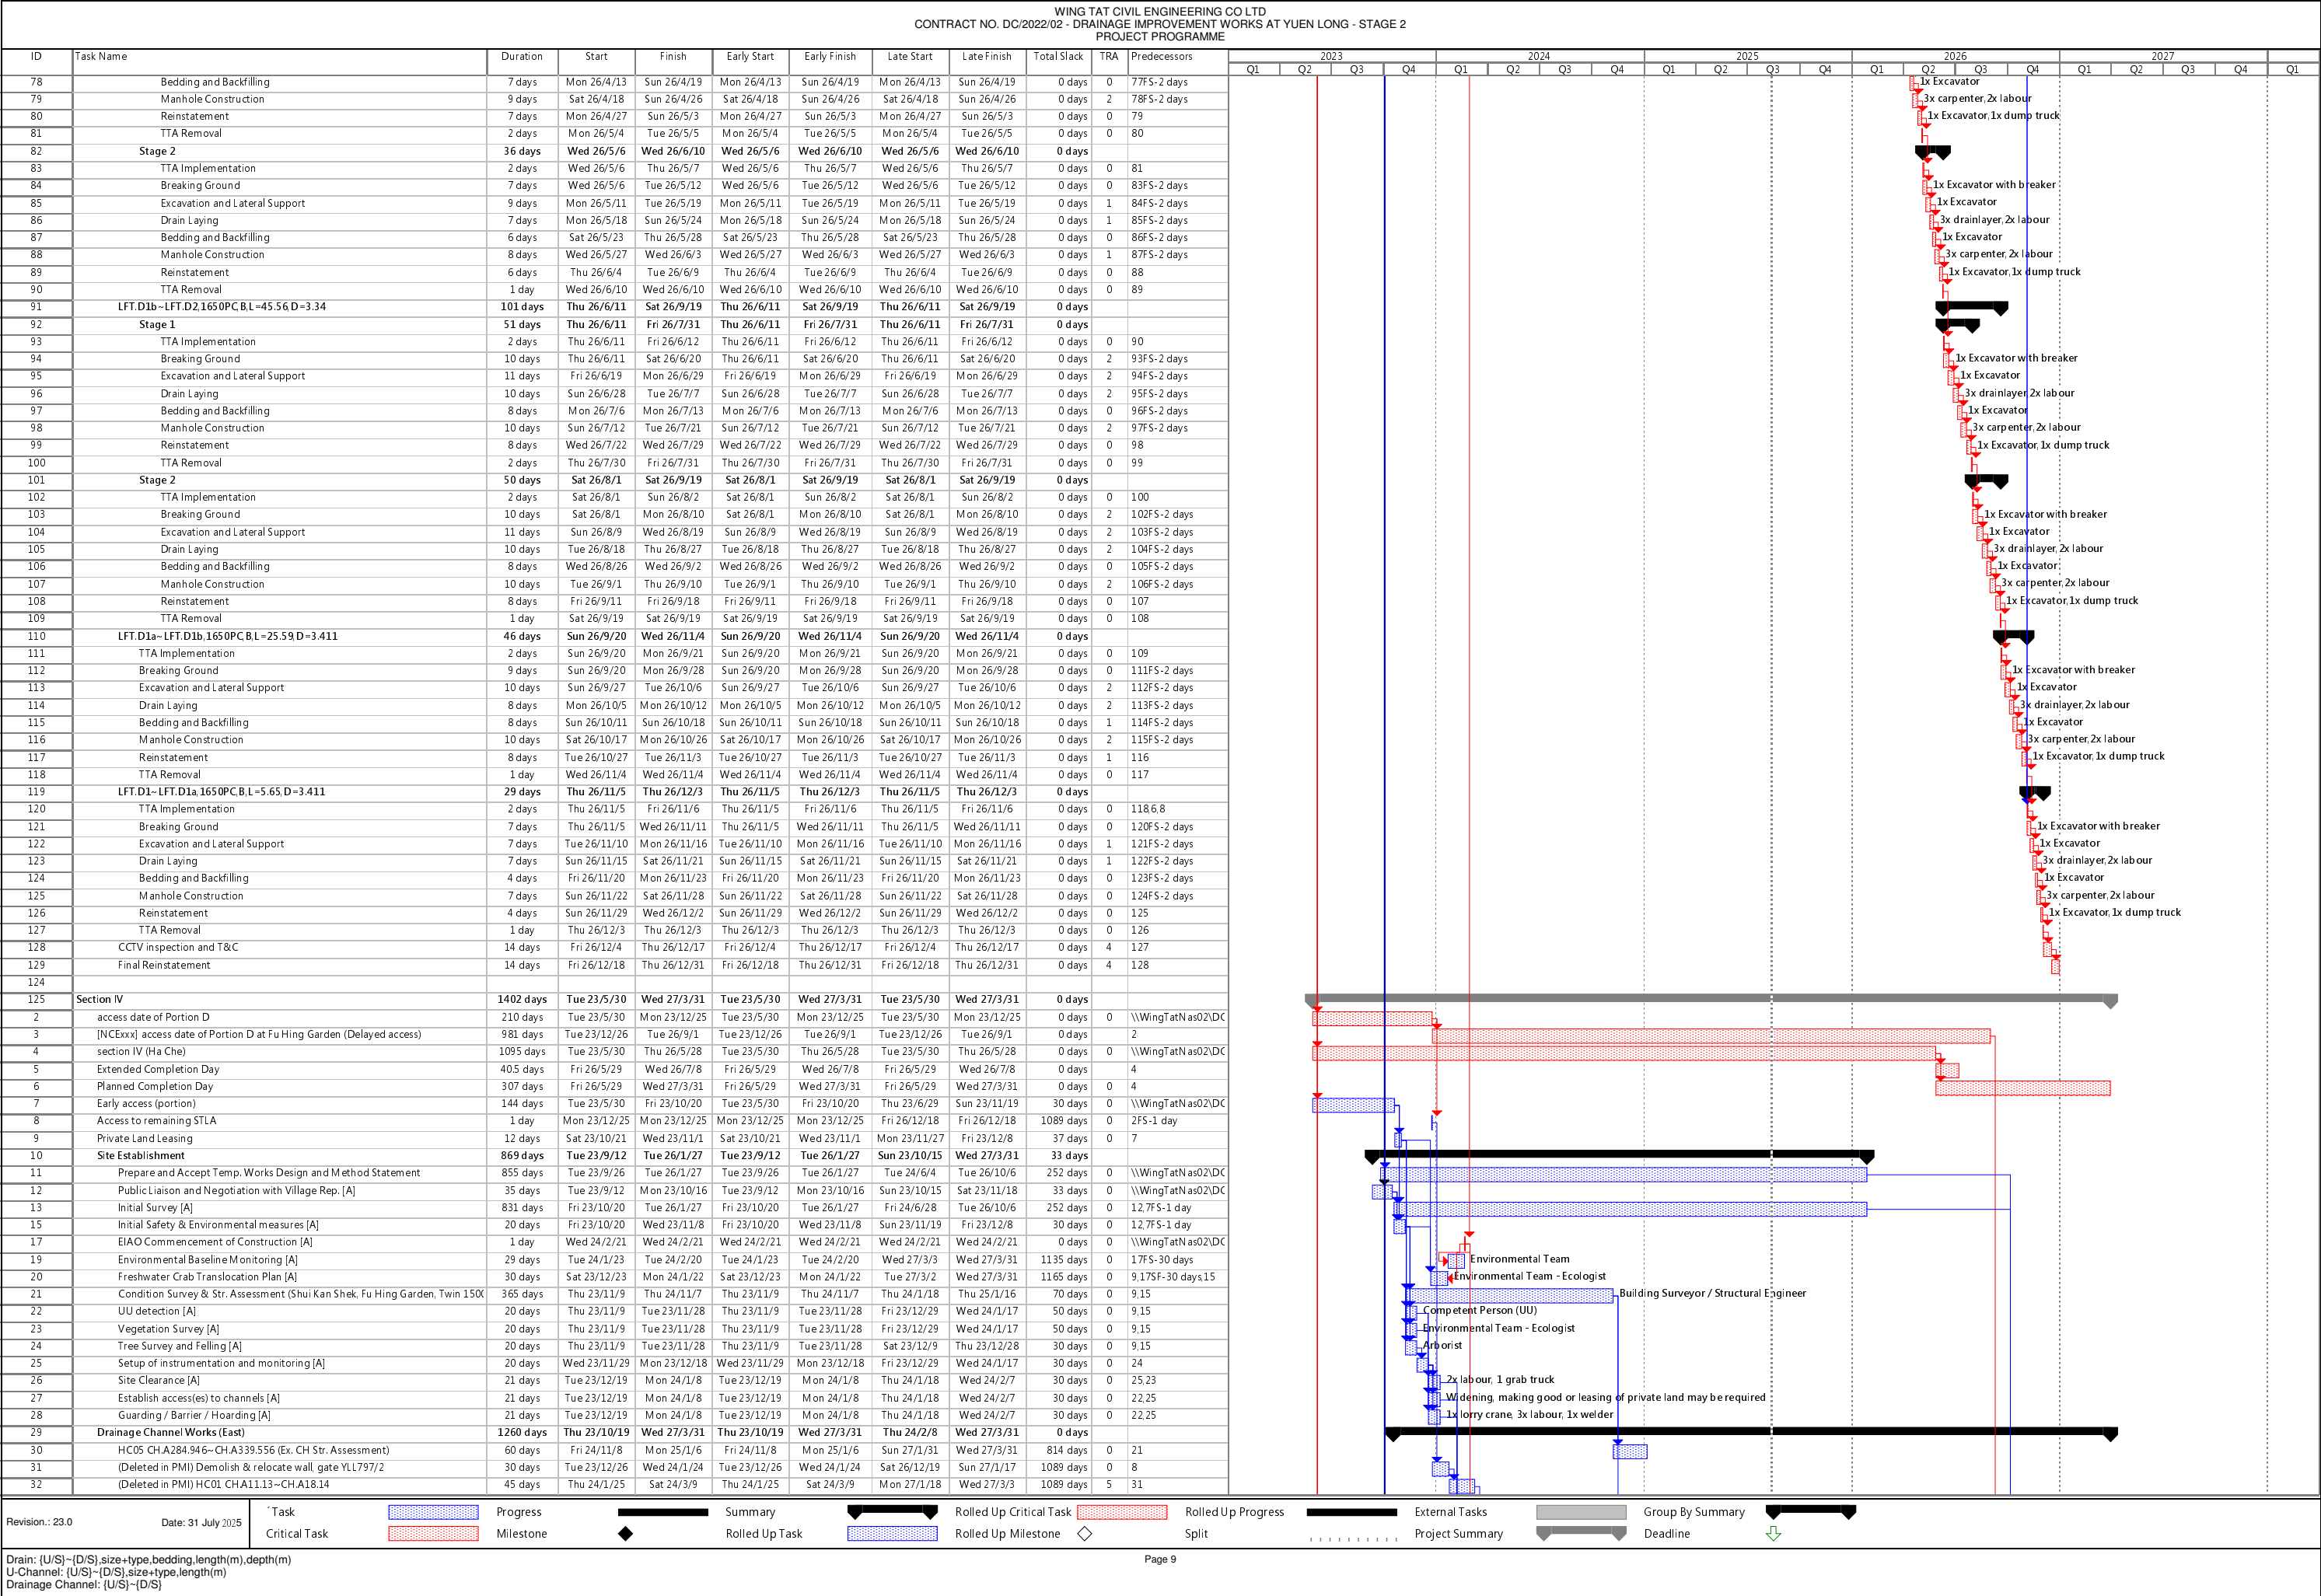

| WING TAT CIVIL ENGINEERING CO LTD                                           |                                                                            |          |              |              |              |              |              |              |             |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
|-----------------------------------------------------------------------------|----------------------------------------------------------------------------|----------|--------------|--------------|--------------|--------------|--------------|--------------|-------------|--------------|---------------------|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|----|
| CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2 |                                                                            |          |              |              |              |              |              |              |             |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| PROJECT PROGRAMME                                                           |                                                                            |          |              |              |              |              |              |              |             |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| ID                                                                          | Task Name                                                                  | Duration | Start        | Finish       | Early Start  | Early Finish | Late Start   | Late Finish  | Total Slack | TRA          | Predecessors        | 2023 |    |    |    | 2024 |    |    |    | 2025 |    |    |    | 2026 |    |    |    | 2027 |    |    |    |    |
|                                                                             |                                                                            |          |              |              |              |              |              |              |             |              |                     | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1 |
| 33                                                                          | (Deleted in PMI) Pedestrian & Vehicular Crossing no. 1 (Box Culvert no. 1) | 28 days  | Sun 24/3/10  | Sat 24/4/6   | Sun 24/3/10  | Sat 24/4/6   | Thu 27/3/4   | Wed 27/3/31  | 1089 days   | 0            | 32                  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 34                                                                          | [PMI072] HC01 Additional Drainage Channel CH.A11.23~CH.A29.00              | 166 days | Mon 24/12/9  | Fri 25/5/23  | Mon 24/12/9  | Fri 25/5/23  | Tue 26/9/29  | Sat 27/3/13  | 659 days    |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 35                                                                          | Liaison with local landlord and HAD for BCL [A]                            | 30 days  | Mon 24/12/9  | Tue 25/1/7   | Mon 24/12/9  | Tue 25/1/7   | Tue 26/9/29  | Wed 26/10/28 | 659 days    |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 36                                                                          | Site Clearance and Hoarding [A]                                            | 14 days  | Wed 25/1/8   | Tue 25/1/21  | Wed 25/1/8   | Tue 25/1/21  | Thu 26/10/29 | Wed 26/11/11 | 659 days    | 35           |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 37                                                                          | Sheetpiling & Temp. Drainage Diversion [A]                                 | 35 days  | Wed 25/1/22  | Tue 25/2/25  | Wed 25/1/22  | Tue 25/2/25  | Thu 26/11/12 | Wed 26/12/16 | 659 days    | 36           |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 38                                                                          | Excavation and Lateral Support [A]                                         | 35 days  | Sun 25/2/16  | Sat 25/3/22  | Sun 25/2/16  | Sat 25/3/22  | Mon 26/12/7  | Sun 27/1/10  | 659 days    | 37FS-10 days |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 39                                                                          | Ground Beams                                                               | 21 days  | Thu 25/3/13  | Wed 25/4/2   | Thu 25/3/13  | Wed 25/4/2   | Fri 27/1/1   | Thu 27/1/21  | 659 days    |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 40                                                                          | Rebar Fixing [A]                                                           | 15 days  | Thu 25/3/13  | Thu 25/3/27  | Thu 25/3/13  | Thu 25/3/27  | Fri 27/1/1   | Fri 27/1/15  | 659 days    | 38FS-10 days |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 41                                                                          | Formwork Erection and Cast-in items [A]                                    | 15 days  | Tue 25/3/18  | Tue 25/4/1   | Tue 25/3/18  | Tue 25/4/1   | Wed 27/1/6   | Wed 27/1/20  | 659 days    | 40FS-10 days |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 42                                                                          | Concreting [A]                                                             | 1 day    | Wed 25/4/2   | Wed 25/4/2   | Wed 25/4/2   | Wed 25/4/2   | Thu 27/1/21  | Thu 27/1/21  | 659 days    | 41           |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 43                                                                          | Walls                                                                      | 21 days  | Thu 25/4/3   | Wed 25/4/23  | Thu 25/4/3   | Wed 25/4/23  | Fri 27/1/22  | Thu 27/2/11  | 659 days    |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 44                                                                          | Rebar Fixing [A]                                                           | 15 days  | Thu 25/4/3   | Thu 25/4/17  | Thu 25/4/3   | Thu 25/4/17  | Fri 27/1/22  | Fri 27/2/5   | 659 days    | 42           |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 45                                                                          | Formwork Erection and Cast-in items [A]                                    | 15 days  | Tue 25/4/8   | Tue 25/4/22  | Tue 25/4/8   | Tue 25/4/22  | Wed 27/1/27  | Wed 27/2/10  | 659 days    | 44FS-10 days |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 46                                                                          | Concreting [A]                                                             | 1 day    | Wed 25/4/23  | Wed 25/4/23  | Wed 25/4/23  | Wed 25/4/23  | Thu 27/2/11  | Thu 27/2/11  | 659 days    | 45           |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 47                                                                          | Backfilling and Compaction [A]                                             | 20 days  | Thu 25/4/24  | Tue 25/5/13  | Thu 25/4/24  | Tue 25/5/13  | Fri 27/2/12  | Wed 27/3/3   | 659 days    | 46           |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 48                                                                          | Removal of Sheetpiles [A]                                                  | 20 days  | Sun 25/5/4   | Fri 25/5/23  | Sun 25/5/4   | Fri 25/5/23  | Mon 27/2/22  | Sat 27/3/13  | 659 days    | 47FS-10 days |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 49                                                                          | Pedestrian & Vehicular Crossing no. 1 (Box Culvert no.1) [A]               | 28 days  | Wed 25/5/14  | Tue 25/6/10  | Wed 25/5/14  | Tue 25/6/10  | Thu 27/3/4   | Wed 27/3/31  | 659 days    | 48FS-10 days |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 50                                                                          | Pedestrian & Vehicular Crossing no. 2 (Box Culvert no. 2) [A]              | 28 days  | Thu 24/2/8   | Wed 24/3/6   | Thu 24/2/8   | Wed 24/3/6   | Thu 24/2/8   | Wed 24/3/6   | 0 days      | 0            | 28,27,17FS-14 days. |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 51                                                                          | HC02 CH.A18.14~ CH.A120.261 (BC1~2)                                        | 359 days | Thu 23/10/19 | Fri 24/10/11 | Thu 23/10/19 | Fri 24/10/11 | Thu 24/3/7   | Wed 27/3/31  | 140 days    |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 52                                                                          | EWN/007 NCE/001 Ambiguity on Drawings                                      | 30 days  | Thu 23/10/19 | Fri 23/11/17 | Thu 23/10/19 | Fri 23/11/17 | Wed 27/2/10  | Thu 27/3/11  | 1210 days   | 0            |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 53                                                                          | C9 tender for Precast units [A]                                            | 20 days  | Sat 23/11/18 | Thu 23/12/7  | Sat 23/11/18 | Thu 23/12/7  | Fri 27/3/12  | Wed 27/3/31  | 1210 days   | 0            | 52                  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 54                                                                          | Sheetpiling & Temp. Drainage Diversion [A]                                 | 44 days  | Thu 24/3/7   | Thu 24/4/19  | Thu 24/3/7   | Fri 24/4/19  | Thu 24/3/7   | Fri 24/4/19  | 0 days      | 1            | 50                  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 55                                                                          | Excavation and Lateral Support [A]                                         | 44 days  | Tue 24/4/2   | Wed 24/5/15  | Tue 24/4/2   | Wed 24/5/15  | Tue 24/4/2   | Wed 24/5/15  | 0 days      | 1            | 54FS-18 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 56                                                                          | Walls                                                                      | 68 days  | Sun 24/4/28  | Thu 24/7/4   | Sun 24/4/28  | Thu 24/7/4   | Sun 24/4/28  | Thu 24/7/4   | 0 days      |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 57                                                                          | Install precast portion (double beam) [A]                                  | 68 days  | Sun 24/4/28  | Thu 24/7/4   | Sun 24/4/28  | Thu 24/7/4   | Sun 24/4/28  | Thu 24/7/4   | 0 days      | 0            | 55FS-18 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 58                                                                          | Ground Beams                                                               | 40 days  | Mon 24/6/10  | Fri 24/7/19  | Mon 24/6/10  | Fri 24/7/19  | Mon 24/6/10  | Fri 24/7/19  | 0 days      |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 59                                                                          | Rebar Fixing [A]                                                           | 30 days  | Mon 24/6/10  | Tue 24/7/9   | Mon 24/6/10  | Tue 24/7/9   | Mon 24/6/10  | Tue 24/7/9   | 0 days      | 1            | 57FS-25 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 60                                                                          | Formwork Erection and Cast-in items [A]                                    | 30 days  | Thu 24/6/20  | Fri 24/7/19  | Thu 24/6/20  | Fri 24/7/19  | Thu 24/6/20  | Fri 24/7/19  | 0 days      | 1            | 59FS-20 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 61                                                                          | Concreting [A]                                                             | 14 days  | Sun 24/6/30  | Sat 24/7/13  | Sun 24/6/30  | Sat 24/7/13  | Sun 24/6/30  | Sat 24/7/13  | 0 days      | 0            | 60FS-20 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 62                                                                          | Top Wall                                                                   | 50 days  | Sun 24/7/14  | Sun 24/9/1   | Sun 24/7/14  | Sun 24/9/1   | Sun 24/7/14  | Sun 24/9/1   | 0 days      |              |                     |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 63                                                                          | Rebar Fixing [A]                                                           | 35 days  | Sun 24/7/14  | Sat 24/8/17  | Sun 24/7/14  | Sat 24/8/17  | Sun 24/7/14  | Sat 24/8/17  | 0 days      | 1            | 61                  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 64                                                                          | Formwork Erection and Cast-in items [A]                                    | 35 days  | Mon 24/7/29  | Sun 24/9/1   | Mon 24/7/29  | Sun 24/9/1   | Mon 24/7/29  | Sun 24/9/1   | 0 days      | 1            | 63FS-20 days        |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |

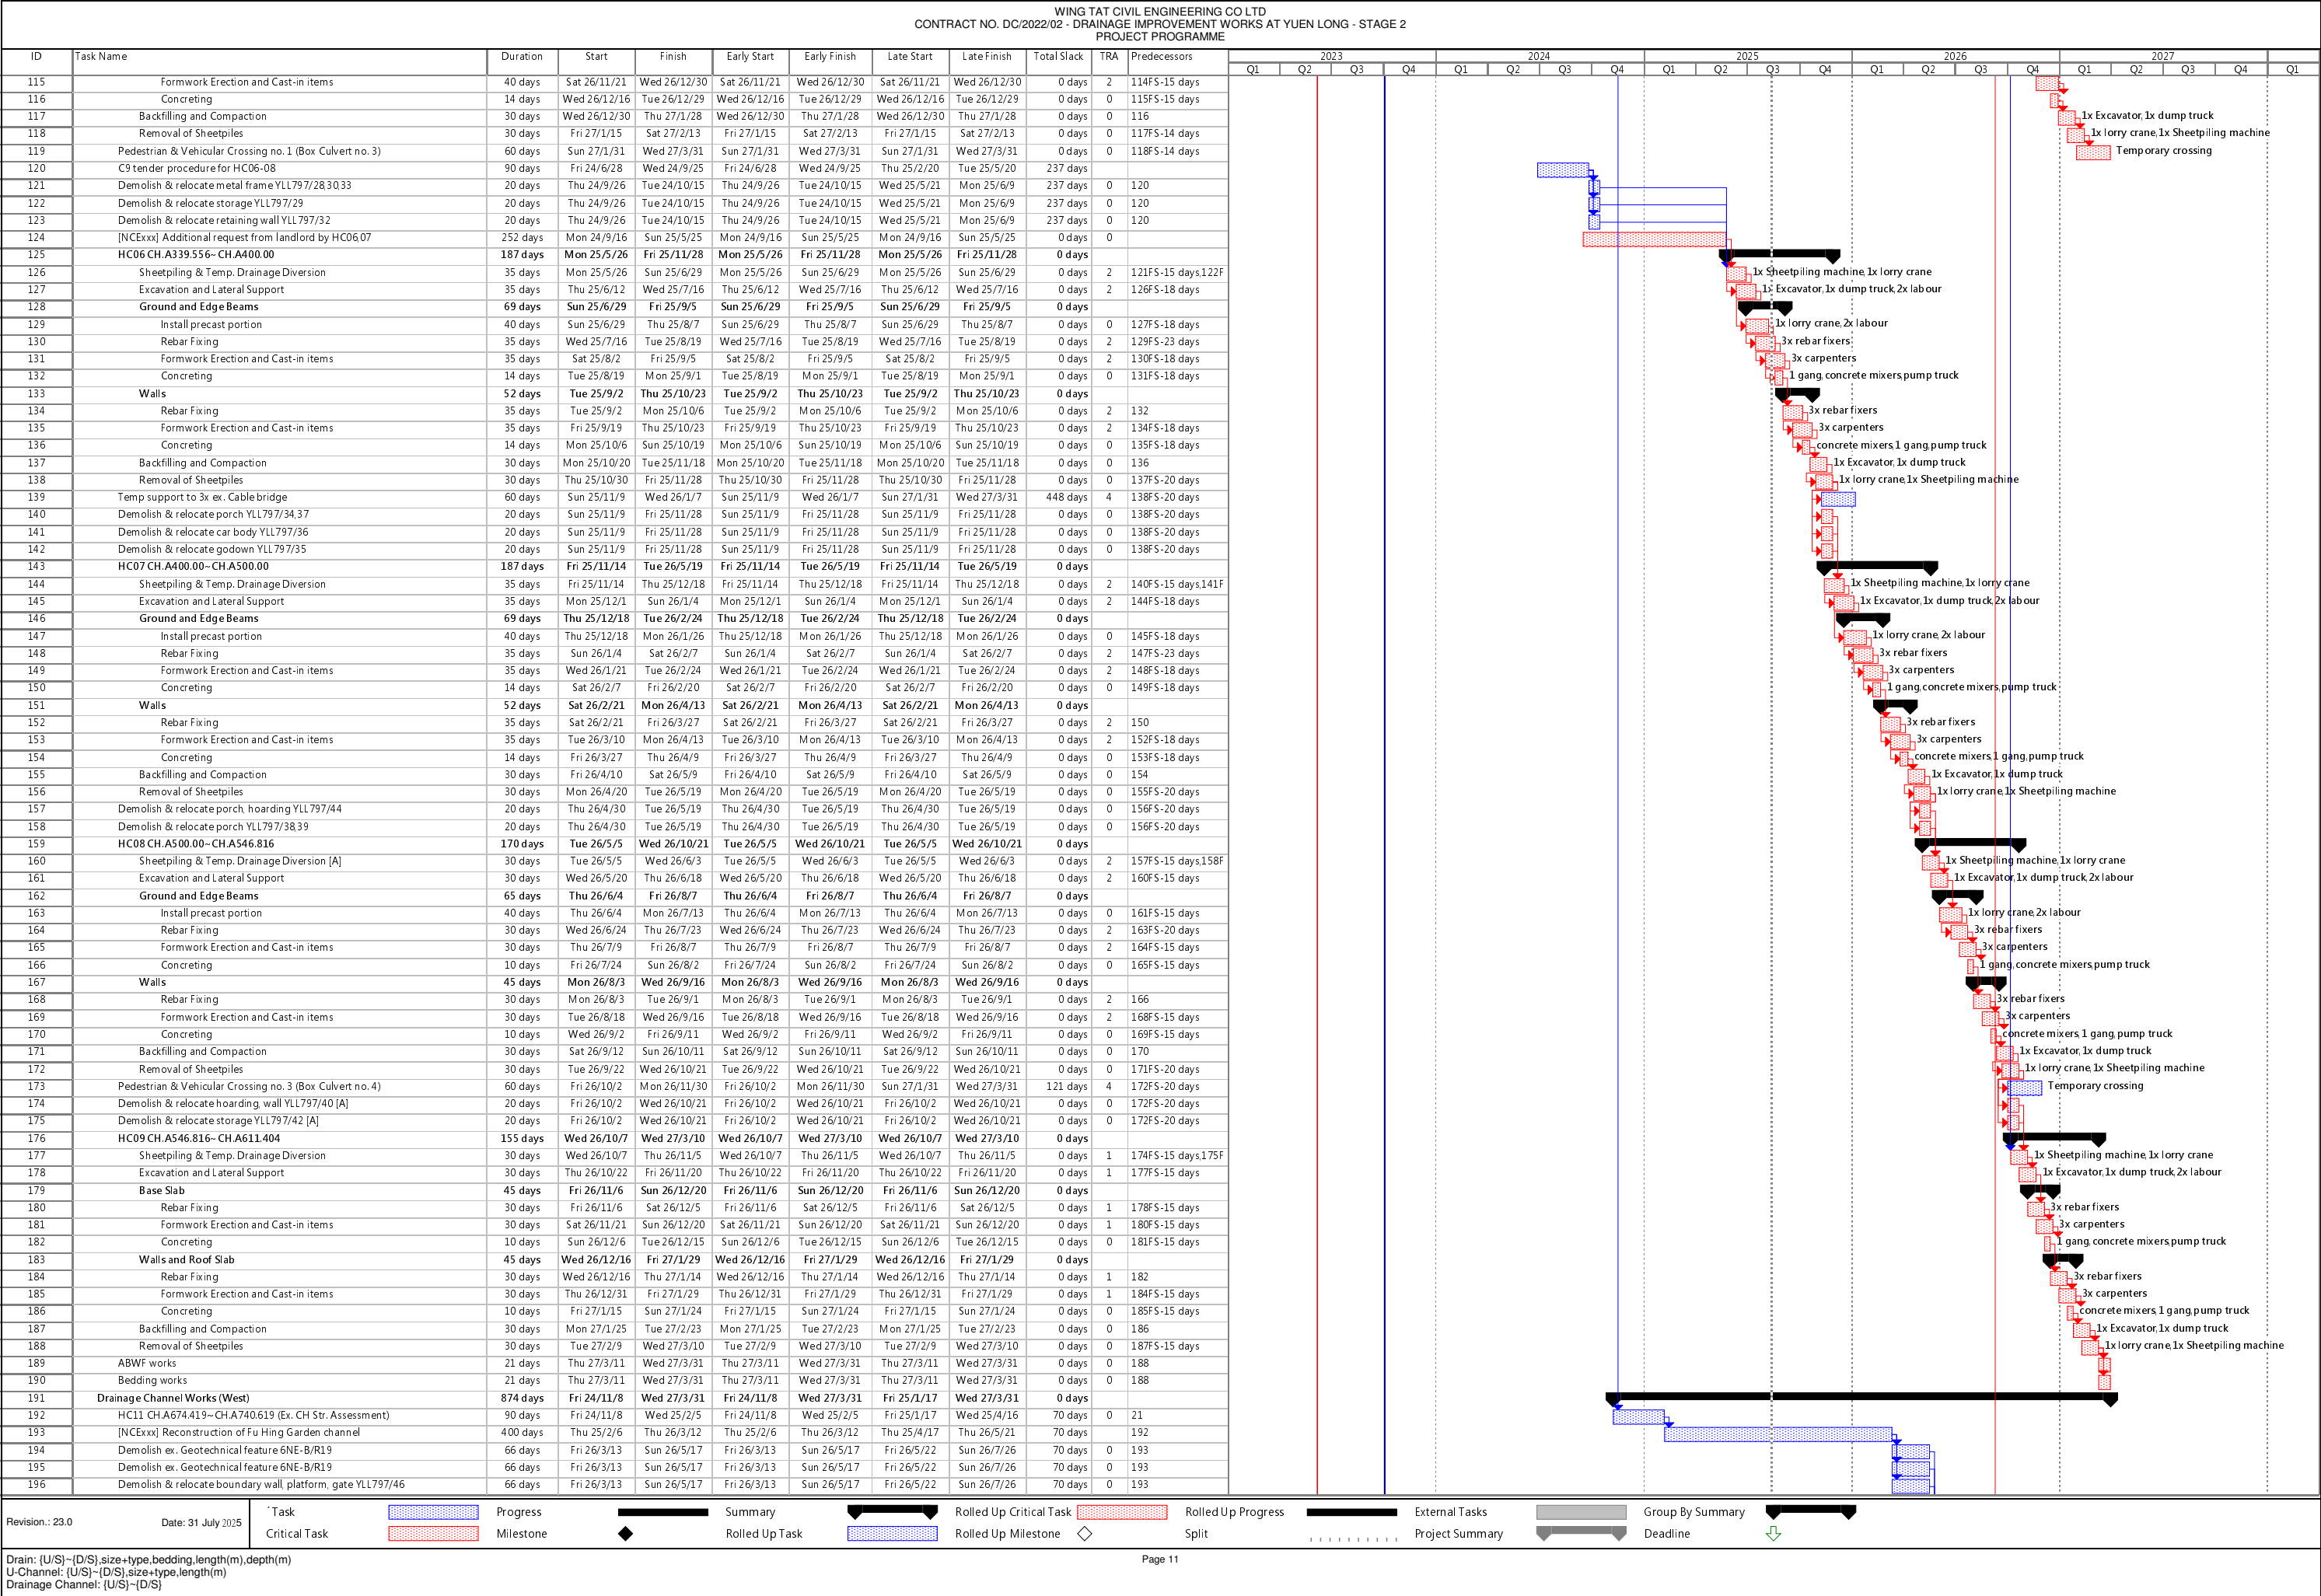

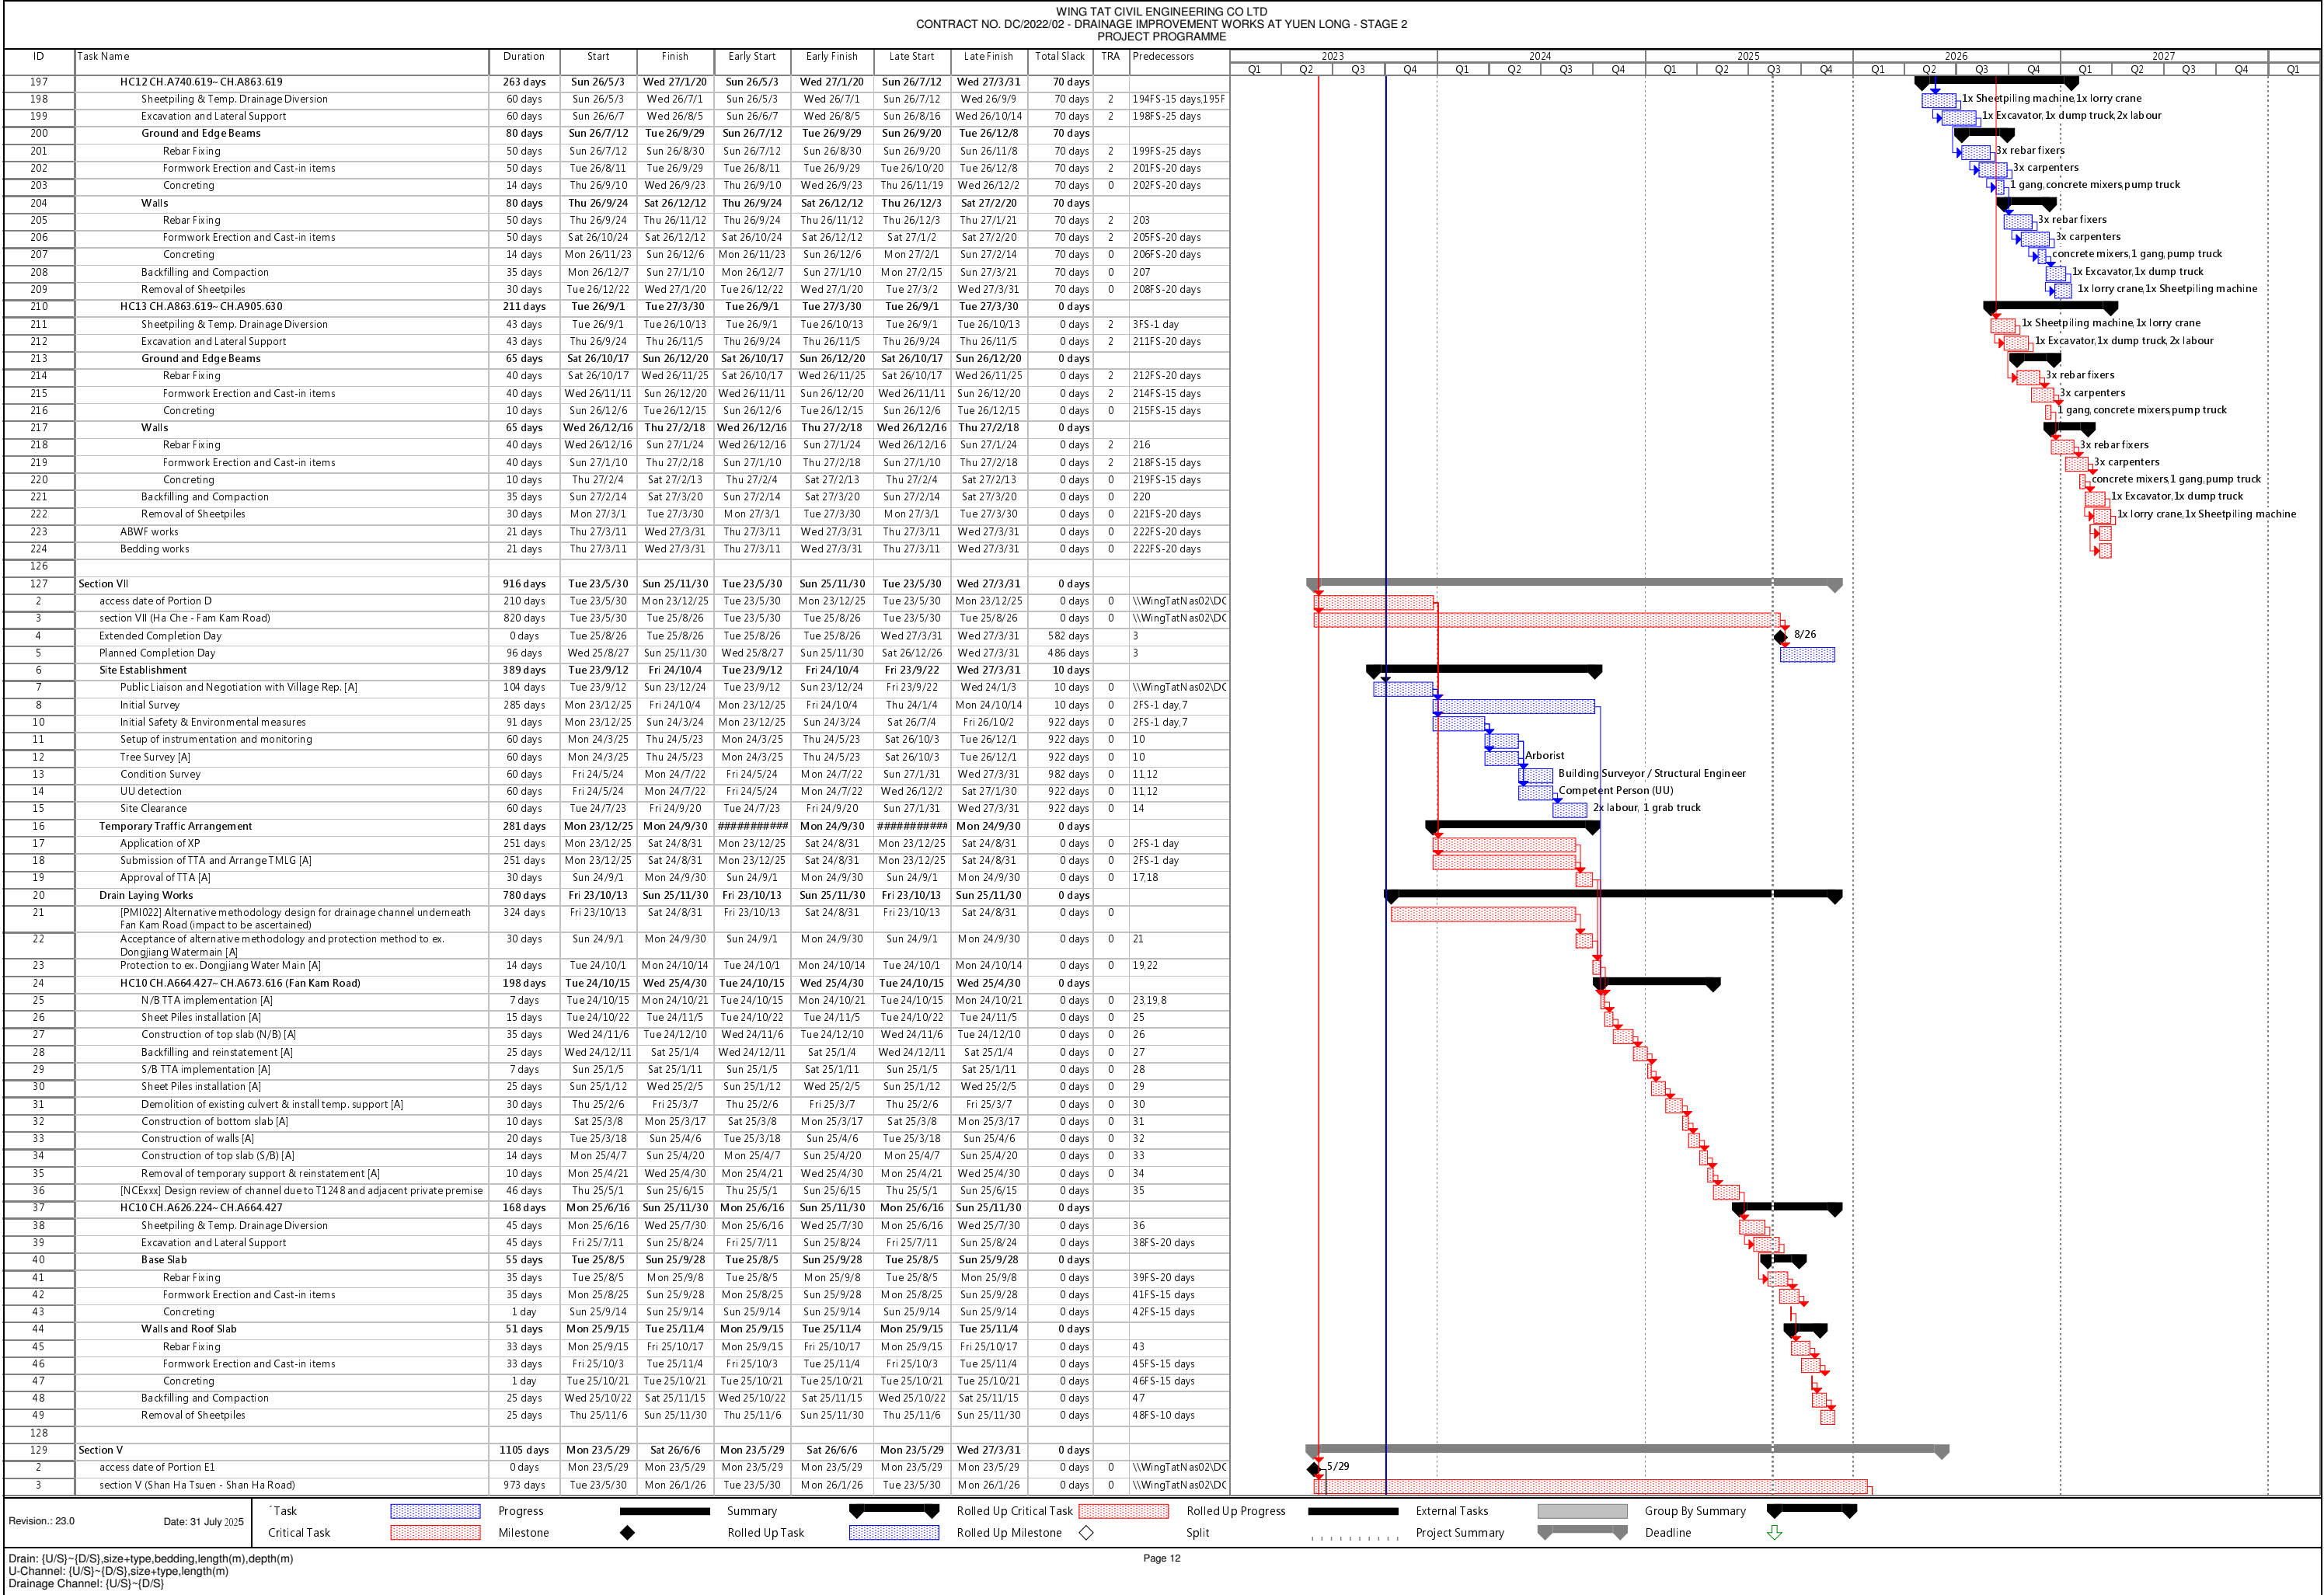

WING TAT CIVIL ENGINEERING CO LTD

CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2

PROJECT PROGRAMME

| ID | Task Name                                                      | Duration | Start        | Finish       | Early Start  | Early Finish | Late Start   | Late Finish  | Total Slack | TBA | Predecessors         |
|----|----------------------------------------------------------------|----------|--------------|--------------|--------------|--------------|--------------|--------------|-------------|-----|----------------------|
| 4  | Extended Completion Day                                        | 9 days   | Tue 26/1/27  | Wed 26/2/4   | Tue 26/1/27  | Wed 26/2/4   | Tue 26/1/27  | Wed 26/2/4   | 0 days      |     | 3                    |
| 5  | Planned Completion Day                                         | 70 days  | Tue 26/1/27  | Mon 26/4/6   | Tue 26/1/27  | Mon 26/4/6   | Tue 26/1/27  | Mon 26/4/6   | 0 days      |     | 3                    |
| 6  | Site Establishment                                             | 871 days | Mon 23/5/29  | Wed 25/10/15 | Mon 23/5/29  | Wed 25/10/15 | Sun 23/9/24  | Mon 26/4/6   | 118 days    |     |                      |
| 7  | Prepare and Accept Temp. Works Design and Method Statement [A] | 751 days | Tue 23/9/26  | Wed 25/10/15 | Tue 23/9/26  | Wed 25/10/15 | Sun 24/3/17  | Mon 26/4/6   | 173 days    | 0   | \\WingTatNas02\DC    |
| 8  | Public Liaison and Negotiation with Village Rep. [A]           | 104 days | Tue 23/9/12  | Sun 23/12/24 | Tue 23/9/12  | Sun 23/12/24 | Sun 23/9/24  | Fri 24/1/5   | 12 days     | 0   | \\WingTatNas02\DC    |
| 9  | Initial Survey [A]                                             | 871 days | Mon 23/5/29  | Wed 25/10/15 | Mon 23/5/29  | Wed 25/10/15 | Sat 23/11/18 | Mon 26/4/6   | 173 days    | 0   | 2FS-1 day            |
| 10 | [EWN01] Objection and additional request of Village Rep.       | 85 days  | Mon 23/12/25 | Mon 24/3/18  | Mon 23/12/25 | Mon 24/3/18  | Sat 24/1/6   | Sat 24/3/30  | 12 days     | 0   | 8                    |
| 11 | [EWN01] Objection and additional request of Village Rep.       | 30 days  | Tue 24/3/19  | Wed 24/4/17  | Tue 24/3/19  | Wed 24/4/17  | Sun 24/3/31  | Mon 24/4/29  | 12 days     | 0   | 10                   |
| 13 | Initial Safety & Environmental measures [A]                    | 30 days  | Sun 24/3/31  | Mon 24/4/29  | Sun 24/3/31  | Mon 24/4/29  | Sun 24/3/31  | Mon 24/4/29  | 0 days      | 0   | 18FF                 |
| 15 | Setup of instrumentation and monitoring [A]                    | 45 days  | Sat 24/3/16  | Mon 24/4/29  | Sat 24/3/16  | Mon 24/4/29  | Sat 24/3/16  | Mon 24/4/29  | 0 days      | 0   | 18FF                 |
| 16 | Tree Survey [A]                                                | 45 days  | Sat 24/3/16  | Mon 24/4/29  | Sat 24/3/16  | Mon 24/4/29  | Sat 24/3/16  | Mon 24/4/29  | 0 days      | 0   | 18FF                 |
| 17 | UU detection [A]                                               | 30 days  | Sun 24/3/31  | Mon 24/4/29  | Sun 24/3/31  | Mon 24/4/29  | Sun 24/3/31  | Mon 24/4/29  | 0 days      | 0   | 18FF                 |
| 18 | Site Clearance [A]                                             | 30 days  | Sun 24/3/31  | Mon 24/4/29  | Sun 24/3/31  | Mon 24/4/29  | Sun 24/3/31  | Mon 24/4/29  | 0 days      | 0   | 22FF                 |
| 19 | Temporary Traffic Arrangement                                  | 337 days | Mon 23/5/29  | Mon 24/4/29  | Mon 23/5/29  | Mon 24/4/29  | Mon 23/5/29  | Mon 24/4/29  | 0 days      |     |                      |
| 20 | Application of XP [A]                                          | 307 days | Mon 23/5/29  | Sat 24/3/30  | Mon 23/5/29  | Sat 24/3/30  | Mon 23/5/29  | Sat 24/3/30  | 0 days      | 0   | 2FS-1 day            |
| 21 | Submission of TTA and Arrange TMLG [A]                         | 307 days | Mon 23/5/29  | Sat 24/3/30  | Mon 23/5/29  | Sat 24/3/30  | Mon 23/5/29  | Sat 24/3/30  | 0 days      | 0   | 2FS-1 day            |
| 22 | Approval of TTA [A]                                            | 30 days  | Sun 24/3/31  | Mon 24/4/29  | Sun 24/3/31  | Mon 24/4/29  | Sun 24/3/31  | Mon 24/4/29  | 0 days      | 0   | 20,21,10             |
| 23 | Drain Laying Works                                             | 707 days | Tue 24/4/30  | Mon 26/4/6   | Tue 24/4/30  | Mon 26/4/6   | Tue 24/4/30  | Mon 26/4/6   | 0 days      |     |                      |
| 24 | SHT.A3A-SHT.A04.1500PC,B,L=49.29,D=3.65                        | 161 days | Tue 24/4/30  | Mon 24/10/7  | Tue 24/4/30  | Mon 24/10/7  | Tue 24/4/30  | Mon 24/10/7  | 0 days      |     |                      |
| 25 | Stage 1                                                        | 83 days  | Tue 24/4/30  | Sun 24/7/21  | Tue 24/4/30  | Sun 24/7/21  | Tue 24/4/30  | Sun 24/7/21  | 0 days      |     |                      |
| 26 | TTA Implementation (trial run) [A]                             | 7 days   | Tue 24/4/30  | Mon 24/5/6   | Tue 24/4/30  | Mon 24/5/6   | Tue 24/4/30  | Mon 24/5/6   | 0 days      | 0   | 18,22,13,15,16,17,11 |
| 27 | Breaking Ground [A]                                            | 14 days  | Sun 24/5/5   | Sat 24/5/18  | Sun 24/5/5   | Sat 24/5/18  | Sun 24/5/5   | Sat 24/5/18  | 0 days      | 1   | 26FS-2 days          |
| 28 | Excavation and Lateral Support [A]                             | 20 days  | Fri 24/5/17  | Wed 24/6/5   | Fri 24/5/17  | Wed 24/6/5   | Fri 24/5/17  | Wed 24/6/5   | 0 days      | 2   | 27FS-2 days          |
| 29 | Drain Laying [A]                                               | 20 days  | Tue 24/6/4   | Sun 24/6/23  | Tue 24/6/4   | Sun 24/6/23  | Tue 24/6/4   | Sun 24/6/23  | 0 days      | 2   | 28FS-2 days          |
| 30 | Bedding and Backfilling [A]                                    | 18 days  | Sat 24/6/22  | Tue 24/7/9   | Tue 24/6/22  | Tue 24/7/9   | Sat 24/6/22  | Tue 24/7/9   | 0 days      | 0   | 29FS-2 days          |
| 31 | Reinstatement [A]                                              | 12 days  | Mon 24/7/8   | Fri 24/7/19  | Mon 24/7/8   | Fri 24/7/19  | Mon 24/7/8   | Fri 24/7/19  | 0 days      | 0   | 30FS-2 days          |
| 32 | TTA Removal [A]                                                | 2 days   | Sat 24/7/20  | Sun 24/7/21  | Sat 24/7/20  | Sun 24/7/21  | Sat 24/7/20  | Sun 24/7/21  | 0 days      | 0   | 31                   |
| 33 | Stage 2                                                        | 78 days  | Mon 24/7/22  | Mon 24/10/7  | Mon 24/7/22  | Mon 24/10/7  | Mon 24/7/22  | Mon 24/10/7  | 0 days      |     |                      |
| 34 | TTA Implementation [A]                                         | 4 days   | Mon 24/7/22  | Thu 24/7/25  | Mon 24/7/22  | Thu 24/7/25  | Mon 24/7/22  | Thu 24/7/25  | 0 days      | 0   | 32                   |
| 35 | Breaking Ground [A]                                            | 14 days  | Wed 24/7/24  | Tue 24/8/6   | Wed 24/7/24  | Tue 24/8/6   | Wed 24/7/24  | Tue 24/8/6   | 0 days      | 1   | 34FS-2 days          |
| 36 | Excavation and Lateral Support [A]                             | 20 days  | Mon 24/8/5   | Sat 24/8/24  | Mon 24/8/5   | Sat 24/8/24  | Mon 24/8/5   | Sat 24/8/24  | 0 days      | 2   | 35FS-2 days          |
| 37 | Drain Laying [A]                                               | 20 days  | Fri 24/8/23  | Wed 24/9/11  | Fri 24/8/23  | Wed 24/9/11  | Fri 24/8/23  | Wed 24/9/11  | 0 days      | 2   | 36FS-2 days          |
| 38 | Bedding and Backfilling [A]                                    | 16 days  | Tue 24/9/10  | Wed 24/9/25  | Tue 24/9/10  | Wed 24/9/25  | Tue 24/9/10  | Wed 24/9/25  | 0 days      | 0   | 37FS-2 days          |
| 39 | Reinstatement [A]                                              | 12 days  | Tue 24/9/24  | Sat 24/10/5  | Tue 24/9/24  | Sat 24/10/5  | Tue 24/9/24  | Sat 24/10/5  | 0 days      | 0   | 38FS-2 days          |
| 40 | TTA Removal [A]                                                | 2 days   | Sun 24/10/6  | Mon 24/10/7  | Sun 24/10/6  | Mon 24/10/7  | Sun 24/10/6  | Mon 24/10/7  | 0 days      | 0   | 39                   |
| 41 | SHT.A05-SHT.A06A.1500PC,B,L=13.12,D=3.15                       | 77 days  | Tue 24/10/8  | Mon 24/12/23 | Tue 24/10/8  | Mon 24/12/23 | Tue 24/10/8  | #####        | 0 days      |     |                      |
| 42 | TTA Implementation [A]                                         | 4 days   | Tue 24/10/8  | Fri 24/10/11 | Tue 24/10/8  | Fri 24/10/11 | Tue 24/10/8  | Fri 24/10/11 | 0 days      | 0   | 40                   |
| 43 | Breaking Ground [A]                                            | 14 days  | Thu 24/10/10 | Wed 24/10/23 | Thu 24/10/10 | Wed 24/10/23 | Thu 24/10/10 | Wed 24/10/23 | 0 days      | 0   | 42FS-2 days          |
| 44 | Excavation and Lateral Support [A]                             | 15 days  | Tue 24/10/22 | Tue 24/11/5  | Tue 24/10/22 | Tue 24/11/5  | Tue 24/10/22 | Tue 24/11/5  | 0 days      | 0   | 43FS-2 days          |
| 45 | Drain Laying [A]                                               | 14 days  | Mon 24/11/4  | Sun 24/11/17 | Mon 24/11/4  | Sun 24/11/17 | Mon 24/11/4  | Sun 24/11/17 | 0 days      | 0   | 44FS-2 days          |
| 46 | Bedding and Backfilling [A]                                    | 15 days  | Sat 24/11/16 | Sat 24/11/30 | Sat 24/11/16 | Sat 24/11/30 | Sat 24/11/16 | Sat 24/11/30 | 0 days      | 0   | 45FS-2 days          |
| 47 | Manhole Construction SHT.A06A [A]                              | 14 days  | Fri 24/11/29 | Thu 24/12/12 | Fri 24/11/29 | Thu 24/12/12 | Fri 24/11/29 | Thu 24/12/12 | 0 days      | 0   | 46FS-2 days          |
| 48 | Reinstatement [A]                                              | 10 days  | Fri 24/12/13 | Sun 24/12/22 | Fri 24/12/13 | Sun 24/12/22 | Fri 24/12/13 | Sun 24/12/22 | 0 days      | 0   | 47                   |
| 49 | TTA Removal [A]                                                | 1 day    | Mon 24/12/23 | Mon 24/12/23 | Mon 24/12/23 | Mon 24/12/23 | Mon 24/12/23 | Mon 24/12/23 | 0 days      | 0   | 48                   |
| 50 | Connection of ex. 900pipe to SHT.A06A                          | 30 days  | Tue 24/12/24 | Wed 25/1/22  | Tue 24/12/24 | Wed 25/1/22  | Tue 24/12/24 | Wed 25/1/22  | 0 days      | 0   | 49                   |
| 51 | SHT.A04-SHT.A05.1500PC,B,L=81.31,D=3.44                        | 260 days | Thu 25/1/23  | Thu 25/10/9  | Thu 25/1/23  | Thu 25/10/9  | Thu 25/1/23  | Thu 25/10/9  | 0 days      |     |                      |
| 52 | Stage 1                                                        | 84 days  | Thu 25/1/23  | Wed 25/4/16  | Thu 25/1/23  | Wed 25/4/16  | Thu 25/1/23  | Wed 25/4/16  | 0 days      |     |                      |
| 53 | TTA Implementation [A]                                         | 4 days   | Thu 25/1/23  | Sun 25/1/26  | Thu 25/1/23  | Sun 25/1/26  | Thu 25/1/23  | Sun 25/1/26  | 0 days      | 0   | 50                   |
| 54 | Breaking Ground [A]                                            | 15 days  | Sat 25/1/25  | Sat 25/2/8   | Sat 25/1/25  | Sat 25/2/8   | Sat 25/1/25  | Sat 25/2/8   | 0 days      | 1   | 53FS-2 days          |
| 55 | Excavation and Lateral Support [A]                             | 20 days  | Fri 25/2/7   | Wed 25/2/26  | Fri 25/2/7   | Wed 25/2/26  | Fri 25/2/7   | Wed 25/2/26  | 0 days      | 2   | 54FS-2 days          |
| 56 | Drain Laying [A]                                               | 15 days  | Tue 25/2/25  | Tue 25/3/11  | Tue 25/2/25  | Tue 25/3/11  | Tue 25/2/25  | Tue 25/3/11  | 0 days      | 2   | 55FS-2 days          |
| 57 | Bedding and Backfilling [A]                                    | 15 days  | Mon 25/3/10  | Mon 25/3/24  | Mon 25/3/10  | Mon 25/3/24  | Mon 25/3/10  | Mon 25/3/24  | 0 days      | 0   | 56FS-2 days          |
| 58 | Manhole Construction SHT.A05 [A]                               | 14 days  | Sun 25/3/23  | Sat 25/4/5   | Sun 25/3/23  | Sat 25/4/5   | Sun 25/3/23  | Sat 25/4/5   | 0 days      | 1   | 57FS-2 days          |
| 59 | Reinstatement [A]                                              | 10 days  | Sun 25/4/6   | Tue 25/4/15  | Sun 25/4/6   | Tue 25/4/15  | Sun 25/4/6   | Tue 25/4/15  | 0 days      | 0   | 58                   |
| 60 | TTA Removal [A]                                                | 1 day    | Wed 25/4/16  | Wed 25/4/16  | Wed 25/4/16  | Wed 25/4/16  | Wed 25/4/16  | Wed 25/4/16  | 0 days      | 0   | 59                   |
| 61 | Connection of ex. 900pipe to SHT.A05 [A]                       | 30 days  | Thu 25/4/17  | Fri 25/5/16  | Thu 25/4/17  | Fri 25/5/16  | Thu 25/4/17  | Fri 25/5/16  | 0 days      | 0   | 60                   |
| 62 | Stage 2                                                        | 73 days  | Sat 25/5/17  | Mon 25/7/28  | Sat 25/5/17  | Mon 25/7/28  | Sat 25/5/17  | Mon 25/7/28  | 0 days      |     |                      |
| 63 | TTA Implementation [A]                                         | 4 days   | Sat 25/5/17  | Tue 25/5/20  | Sat 25/5/17  | Tue 25/5/20  | Sat 25/5/17  | Tue 25/5/20  | 0 days      | 0   | 61                   |
| 64 | Breaking Ground [A]                                            | 15 days  | Mon 25/5/19  | Mon 25/6/2   | Mon 25/5/19  | Mon 25/6/2   | Mon 25/5/19  | Mon 25/6/2   | 0 days      | 1   | 63FS-2 days          |
| 65 | Excavation and Lateral Support [A]                             | 20 days  | Sun 25/6/1   | Sun 25/6/20  | Sun 25/6/1   | Sun 25/6/20  | Sun 25/6/1   | Sun 25/6/20  | 0 days      | 2   | 64FS-2 days          |
| 66 | Drain Laying [A]                                               | 15 days  | Thu 25/6/19  | Thu 25/7/3   | Thu 25/6/19  | Thu 25/7/3   | Thu 25/6/19  | Thu 25/7/3   | 0 days      | 2   | 65FS-2 days          |
| 67 | Bedding and Backfilling                                        | 15 days  | Wed 25/7/2   | Wed 25/7/16  | Wed 25/7/2   | Wed 25/7/16  | Wed 25/7/2   | Wed 25/7/16  | 0 days      | 0   | 66FS-2 days          |
| 68 | Reinstatement                                                  | 10 days  | Thu 25/7/17  | Sat 25/7/26  | Thu 25/7/17  | Sat 25/7/26  | Thu 25/7/17  | Sat 25/7/26  | 0 days      | 0   | 67                   |
| 69 | TTA Removal                                                    | 2 days   | Sun 25/7/27  | Mon 25/7/28  | Sun 25/7/27  | Mon 25/7/28  | Sun 25/7/27  | Mon 25/7/28  | 0 days      | 0   | 68                   |
| 70 | Stage 3                                                        | 73 days  | Tue 25/7/29  | Thu 25/10/9  | Tue 25/7/29  | Thu 25/10/9  | Tue 25/7/29  | Thu 25/10/9  | 0 days      |     |                      |
| 71 | TTA Implementation                                             | 4 days   | Tue 25/7/29  | Fri 25/8/1   | Tue 25/7/29  | Fri 25/8/1   | Tue 25/7/29  | Fri 25/8/1   | 0 days      | 0   | 69                   |
| 72 | Breaking Ground                                                | 15 days  | Thu 25/7/31  | Thu 25/8/14  | Thu 25/7/31  | Thu 25/8/14  | Thu 25/7/31  | Thu 25/8/14  | 0 days      | 1   | 71FS-2 days          |
| 73 | Excavation and Lateral Support                                 | 15 days  | Wed 25/8/13  | Wed 25/8/27  | Wed 25/8/13  | Wed 25/8/27  | Wed 25/8/13  | Wed 25/8/27  | 0 days      | 2   | 72FS-2 days          |
| 74 | Drain Laying                                                   | 12 days  | Tue 25/8/26  | Sat 25/9/6   | Tue 25/8/26  | Sat 25/9/6   | Tue 25/8/26  | Sat 25/9/6   | 0 days      | 2   | 73FS-2 days          |
| 75 | Bedding and Backfilling                                        | 15 days  | Fri 25/9/5   | Fri 25/9/19  | Fri 25/9/5   | Fri 25/9/19  | Fri 25/9/5   | Fri 25/9/19  | 0 days      | 0   | 74FS-2 days          |
| 76 | Manhole Construction SHT.A04                                   | 10 days  | Thu 25/9/18  | Sat 25/9/27  | Thu 25/9/18  | Sat 25/9/27  | Thu 25/9/18  | Sat 25/9/27  | 0 days      | 1   | 75FS-2 days          |
| 77 | Reinstatement                                                  | 10 days  | Sun 25/9/28  | Tue 25/10/7  | Sun 25/9/28  | Tue 25/10/7  | Sun 25/9/28  | Tue 25/10/7  | 0 days      | 0   | 76                   |
| 78 | TTA Removal                                                    | 2 days   | Wed 25/10/8  | Thu 25/10/9  | Wed 25/10/8  | Thu 25/10/9  | Wed 25/10/8  | Thu 25/10/9  | 0 days      | 0   | 77                   |
| 79 | SHT.A03-SHT.A3A.1500PC,B,L=8.59,D=3.65                         | 82 days  | Tue 25/10/10 | Tue 25/12/30 | Fri 25/10/10 | Tue 25/12/30 | Fri 25/10/10 | Tue 25/12/30 | 0 days      |     |                      |
| 80 | TTA Implementation                                             | 4 days   | Fri 25/10/10 | Mon 25/10/13 | Fri 25/10/10 | Mon 25/10/13 | Fri 25/10/10 | Mon 25/10/13 | 0 days      | 0   | 78                   |
| 81 | Breaking Ground                                                | 14 days  | Sun 25/10/12 | Sat 25/10/25 | Sun 25/10/12 | Sat 25/10/25 | Sun 25/10/12 | Sat 25/10/25 | 0 days      | 1   | 80FS-2 days          |
| 82 | Excavation and Lateral Support                                 | 18 days  | Fri 25/10/24 | Mon 25/11/10 | Fri 25/10/24 | Mon 25/11/10 | Fri 25/10/24 | Mon 25/11/10 | 0 days      | 2   | 81FS-2 days          |
| 83 | Drain Laying                                                   | 14 days  | Sun 25/11/9  | Sat 25/11/22 | Sun 25/11/9  | Sat 25/11/22 | Sun 25/11/9  | Sat 25/11/22 | 0 days      | 2   | 82FS-2 days          |
| 84 | Bedding and Backfilling                                        | 10 days  | Fri 25/11/30 | Sun 25/11/30 | Fri 25/11/30 | Sun 25/11/30 | Fri 25/11/30 | Sun 25/11/30 | 0 days      | 0   | 83FS-2 days          |
| 85 | Manhole Construction                                           | 20 days  | Sat 25/11/29 | Thu 25/12/18 | Sat 25/11/29 | Thu 25/12/18 | Sat 25/11/29 | Thu 25/12/18 | 0 days      | 1   | 84FS-2 days          |
| 86 | Reinstatement                                                  | 10 days  | Fri 25/12/19 | Sun 25/12/28 | Fri 25/12/19 | Sun 25/12/28 | Fri 25/12/19 | Sun 25/12/28 | 0 days      | 0   | 85                   |
| 87 | TTA Removal                                                    | 2 days   | Mon 25/12/29 | Tue 25/12/30 | Mon 25/12/29 | Tue 25/12/30 | Mon 25/12/29 | Tue 25/12/30 | 0 days      | 0   | 86                   |

Revision.: 23.0

Date: 31 July 2025

Task

Critical Task

Progress

Milestone

Summary

Rolled Up Task

Rolled Up Critical Task

Rolled Up Milestone

Rolled Up Progress

Split

External Tasks

Project Summary

Group By Summary

Deadline

Drain: {U/S}~{D/S},size+type,bedding,length(m),depth(m)

U-Channel: {U/S}~{D/S},size+type,length(m)

Drainage Channel: {U/S}~{D/S}

Page 13







WING TAT CIVIL ENGINEERING CO LTD

CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2

PROJECT PROGRAMME

| ID  | Task Name                                 | Duration | Start        | Finish       | Early Start  | Early Finish | Late Start   | Late Finish  | Total Slack | TRA | Predecessors | 2023 |    |    |    | 2024 |    |    |    | 2025 |    |    |    | 2026 |    |    |    | 2027 |    |    |    | Q1 |
|-----|-------------------------------------------|----------|--------------|--------------|--------------|--------------|--------------|--------------|-------------|-----|--------------|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|----|
| 252 | Stage 1                                   | 24 days  | Tue 25/7/29  | Thu 25/8/21  | Tue 25/7/29  | Thu 25/8/21  | Tue 25/7/29  | Thu 25/8/21  | 0 days      |     |              | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1 |
| 253 | Excavation and Lateral Support            | 8 days   | Tue 25/7/29  | Tue 25/7/29  | Tue 25/7/29  | Tue 25/7/29  | Tue 25/7/29  | Tue 25/7/29  | 0 days      | 0   | 250          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 254 | Formwork Erection                         | 10 days  | Mon 25/8/4   | Wed 25/8/13  | Mon 25/8/4   | Wed 25/8/13  | Mon 25/8/4   | Wed 25/8/13  | 0 days      | 0   | 253FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 255 | Catchpit construcion                      | 10 days  | Tue 25/8/12  | Thu 25/8/21  | Tue 25/8/12  | Thu 25/8/21  | Tue 25/8/12  | Thu 25/8/21  | 0 days      | 0   | 254FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 256 | Concreting                                | 1 day    | Wed 25/8/20  | Wed 25/8/20  | Wed 25/8/20  | Wed 25/8/20  | Wed 25/8/20  | Wed 25/8/20  | 0 days      | 0   | 255FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 257 | Stage 2                                   | 24 days  | Thu 25/8/21  | Sat 25/9/13  | Thu 25/8/21  | Sat 25/9/13  | Thu 25/8/21  | Sat 25/9/13  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 258 | Excavation and Lateral Support            | 8 days   | Thu 25/8/21  | Thu 25/8/28  | Thu 25/8/21  | Thu 25/8/28  | Thu 25/8/21  | Thu 25/8/28  | 0 days      | 0   | 256          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 259 | Formwork Erection                         | 10 days  | Wed 25/8/27  | Fri 25/9/5   | Wed 25/8/27  | Fri 25/9/5   | Wed 25/8/27  | Fri 25/9/5   | 0 days      | 0   | 258FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 260 | Catchpit construcion                      | 10 days  | Thu 25/9/4   | Sat 25/9/13  | Thu 25/9/4   | Sat 25/9/13  | Thu 25/9/4   | Sat 25/9/13  | 0 days      | 0   | 259FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 261 | Concreting                                | 1 day    | Fri 25/9/12  | Fri 25/9/12  | Fri 25/9/12  | Fri 25/9/12  | Fri 25/9/12  | Fri 25/9/12  | 0 days      | 0   | 260FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 262 | Stage 3                                   | 24 days  | Sat 25/9/13  | Mon 25/10/6  | Sat 25/9/13  | Mon 25/10/6  | Sat 25/9/13  | Mon 25/10/6  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 263 | Excavation and Lateral Support            | 8 days   | Sat 25/9/13  | Sat 25/9/20  | Sat 25/9/13  | Sat 25/9/20  | Sat 25/9/13  | Sat 25/9/20  | 0 days      | 0   | 261          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 264 | Formwork Erection                         | 10 days  | Fri 25/9/19  | Sun 25/9/28  | Fri 25/9/19  | Sun 25/9/28  | Fri 25/9/19  | Sun 25/9/28  | 0 days      | 0   | 263FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 265 | Catchpit construcion                      | 10 days  | Sat 25/9/27  | Mon 25/10/6  | Sat 25/9/27  | Mon 25/10/6  | Sat 25/9/27  | Mon 25/10/6  | 0 days      | 0   | 264FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 266 | Concreting                                | 1 day    | Sun 25/10/5  | Sun 25/10/5  | Sun 25/10/5  | Sun 25/10/5  | Sun 25/10/5  | Sun 25/10/5  | 0 days      | 0   | 265FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 267 | SHT.CP3.3--SHT.CP3.300->450CU(G).L=54.5   | 76 days  | Mon 25/10/6  | Sat 25/12/20 | Mon 25/10/6  | Sat 25/12/20 | Mon 25/10/6  | Sat 25/12/20 | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 268 | Stage 1                                   | 24 days  | Mon 25/10/6  | Wed 25/10/29 | Mon 25/10/6  | Wed 25/10/29 | Mon 25/10/6  | Wed 25/10/29 | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 269 | Excavation and Lateral Support            | 8 days   | Mon 25/10/6  | Mon 25/10/13 | Mon 25/10/6  | Mon 25/10/13 | Mon 25/10/6  | Mon 25/10/13 | 0 days      | 0   | 266          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 270 | Formwork Erection                         | 10 days  | Sun 25/10/12 | Tue 25/10/21 | Tue 25/10/12 | Tue 25/10/21 | Tue 25/10/12 | Tue 25/10/21 | 0 days      | 0   | 269FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 271 | Catchpit construcion                      | 10 days  | Mon 25/10/20 | Wed 25/10/29 | Mon 25/10/20 | Wed 25/10/29 | Mon 25/10/20 | Wed 25/10/29 | 0 days      | 0   | 270FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 272 | Concreting                                | 1 day    | Tue 25/10/28 | Tue 25/10/28 | Tue 25/10/28 | Tue 25/10/28 | Tue 25/10/28 | Tue 25/10/28 | 0 days      | 0   | 271FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 273 | Stage 2                                   | 27 days  | Wed 25/10/29 | Mon 25/11/24 | Wed 25/10/29 | Mon 25/11/24 | Wed 25/10/29 | Mon 25/11/24 | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 274 | Excavation and Lateral Support            | 8 days   | Wed 25/10/29 | Wed 25/11/5  | Wed 25/10/29 | Wed 25/11/5  | Wed 25/10/29 | Wed 25/11/5  | 0 days      | 0   | 272          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 275 | Formwork Erection                         | 12 days  | Tue 25/11/4  | Sat 25/11/15 | Tue 25/11/4  | Sat 25/11/15 | Tue 25/11/4  | Sat 25/11/15 | 0 days      | 0   | 274FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 276 | Catchpit construcion                      | 11 days  | Fri 25/11/14 | Mon 25/11/24 | Fri 25/11/14 | Mon 25/11/24 | Fri 25/11/14 | Mon 25/11/24 | 0 days      | 0   | 275FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 277 | Concreting                                | 1 day    | Sun 25/11/23 | Sun 25/11/23 | Sun 25/11/23 | Sun 25/11/23 | Sun 25/11/23 | Sun 25/11/23 | 0 days      | 0   | 276FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 278 | Stage 3                                   | 27 days  | Mon 25/11/24 | Sat 25/12/20 | #####        | Sat 25/12/20 | #####        | Sat 25/12/20 | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 279 | Excavation and Lateral Support            | 8 days   | Mon 25/11/24 | Mon 25/12/1  | Mon 25/11/24 | Mon 25/12/1  | Mon 25/11/24 | Mon 25/12/1  | 0 days      | 0   | 277          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 280 | Formwork Erection                         | 12 days  | Sun 25/11/30 | Thu 25/12/11 | Sun 25/11/30 | Thu 25/12/11 | Sun 25/11/30 | Thu 25/12/11 | 0 days      | 0   | 279FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 281 | Catchpit construcion                      | 11 days  | Wed 25/12/10 | Sat 25/12/20 | Wed 25/12/10 | Sat 25/12/20 | Wed 25/12/10 | Sat 25/12/20 | 0 days      | 0   | 280FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 282 | Concreting                                | 1 day    | Fri 25/12/19 | Fri 25/12/19 | Fri 25/12/19 | Fri 25/12/19 | Fri 25/12/19 | Fri 25/12/19 | 0 days      | 0   | 281FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 283 | SHT.CP3.5--SHT.CP3.3,300->450CU(G).L=43.3 | 57 days  | Sat 25/12/20 | Sat 26/2/14  | Sat 25/12/20 | Sat 26/2/14  | Sat 25/12/20 | Sat 26/2/14  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 284 | Stage 1                                   | 29 days  | Sat 25/12/20 | Sat 26/1/17  | Sat 25/12/20 | Sat 26/1/17  | Sat 25/12/20 | Sat 26/1/17  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 285 | Excavation and Lateral Support [A]        | 10 days  | Sat 25/12/20 | Mon 25/12/29 | Mon 25/12/20 | Mon 25/12/29 | Mon 25/12/20 | Mon 25/12/29 | 0 days      | 0   | 282          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 286 | Formwork Erection [A]                     | 12 days  | Sun 25/12/28 | Thu 26/1/8   | Sun 25/12/28 | Thu 26/1/8   | Sun 25/12/28 | Thu 26/1/8   | 0 days      | 0   | 285FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 287 | Catchpit construcion [A]                  | 11 days  | Wed 26/1/7   | Sat 26/1/17  | Wed 26/1/7   | Sat 26/1/17  | Wed 26/1/7   | Sat 26/1/17  | 0 days      | 0   | 286FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 288 | Concreting [A]                            | 1 day    | Fri 26/1/16  | Fri 26/1/16  | Fri 26/1/16  | Fri 26/1/16  | Fri 26/1/16  | Fri 26/1/16  | 0 days      | 0   | 287FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 289 | Stage 2                                   | 29 days  | Sat 26/1/17  | Sat 26/2/14  | Sat 26/1/17  | Sat 26/2/14  | Sat 26/1/17  | Sat 26/2/14  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 290 | Excavation and Lateral Support [A]        | 10 days  | Sat 26/1/17  | Mon 26/1/26  | Mon 26/1/17  | Mon 26/1/26  | Mon 26/1/17  | Mon 26/1/26  | 0 days      | 0   | 288          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 291 | Formwork Erection [A]                     | 12 days  | Sun 26/1/25  | Thu 26/2/5   | Sun 26/1/25  | Thu 26/2/5   | Sun 26/1/25  | Thu 26/2/5   | 0 days      | 0   | 290FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 292 | Catchpit construcion [A]                  | 11 days  | Wed 26/2/4   | Sat 26/2/14  | Wed 26/2/4   | Sat 26/2/14  | Wed 26/2/4   | Sat 26/2/14  | 0 days      | 0   | 291FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 293 | Concreting [A]                            | 1 day    | Fri 26/2/13  | Fri 26/2/13  | Fri 26/2/13  | Fri 26/2/13  | Fri 26/2/13  | Fri 26/2/13  | 0 days      | 0   | 292FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 294 | End-SHT.CP3.5,300->450CU(G).L=107.7       | 113 days | Sat 26/2/14  | Sat 26/6/6   | Sat 26/2/14  | Sat 26/6/6   | Sat 26/2/14  | Wed 27/3/31  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 295 | Stage 1                                   | 29 days  | Sat 26/2/14  | Sat 26/3/14  | Sat 26/2/14  | Sat 26/3/14  | Sat 26/2/14  | Sat 26/3/14  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 296 | Excavation and Lateral Support [A]        | 10 days  | Sat 26/2/14  | Mon 26/2/23  | Sat 26/2/14  | Mon 26/2/23  | Sat 26/2/14  | Mon 26/2/23  | 0 days      | 0   | 293          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 297 | Formwork Erection [A]                     | 12 days  | Sun 26/2/22  | Thu 26/3/5   | Sun 26/2/22  | Thu 26/3/5   | Sun 26/2/22  | Thu 26/3/5   | 0 days      | 0   | 296FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 298 | Catchpit construcion [A]                  | 11 days  | Wed 26/3/4   | Sat 26/3/14  | Wed 26/3/4   | Sat 26/3/14  | Wed 26/3/4   | Sat 26/3/14  | 0 days      | 0   | 297FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 299 | Concreting [A]                            | 1 day    | Fri 26/3/13  | Fri 26/3/13  | Fri 26/3/13  | Fri 26/3/13  | Fri 26/3/13  | Fri 26/3/13  | 0 days      | 0   | 298FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 300 | Stage 2                                   | 29 days  | Sat 26/3/14  | Sat 26/4/11  | Sat 26/3/14  | Sat 26/4/11  | Sat 26/3/14  | Sat 26/4/11  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 301 | Excavation and Lateral Support [A]        | 10 days  | Sat 26/3/14  | Mon 26/3/23  | Sat 26/3/14  | Mon 26/3/23  | Sat 26/3/14  | Mon 26/3/23  | 0 days      | 0   | 299          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 302 | Formwork Erection [A]                     | 12 days  | Sun 26/3/22  | Thu 26/4/2   | Sun 26/3/22  | Thu 26/4/2   | Sun 26/3/22  | Thu 26/4/2   | 0 days      | 0   | 301FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 303 | Catchpit construcion [A]                  | 11 days  | Wed 26/4/1   | Sat 26/4/11  | Wed 26/4/1   | Sat 26/4/11  | Wed 26/4/1   | Sat 26/4/11  | 0 days      | 0   | 302FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 304 | Concreting [A]                            | 1 day    | Fri 26/4/10  | Fri 26/4/10  | Fri 26/4/10  | Fri 26/4/10  | Fri 26/4/10  | Fri 26/4/10  | 0 days      | 0   | 303FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 305 | Stage 3                                   | 29 days  | Sat 26/4/11  | Sat 26/5/9   | Sat 26/4/11  | Sat 26/5/9   | Sat 26/4/11  | Sat 26/5/9   | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 306 | Excavation and Lateral Support [A]        | 10 days  | Sat 26/4/11  | Mon 26/4/20  | Sat 26/4/11  | Mon 26/4/20  | Sat 26/4/11  | Mon 26/4/20  | 0 days      | 0   | 304          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 307 | Formwork Erection [A]                     | 12 days  | Sun 26/4/19  | Thu 26/4/30  | Sun 26/4/19  | Thu 26/4/30  | Sun 26/4/19  | Thu 26/4/30  | 0 days      | 0   | 306FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |

| WING TAT CIVIL ENGINEERING CO LTD                                           |                                        |          |             |             |             |              |             |              |             |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
|-----------------------------------------------------------------------------|----------------------------------------|----------|-------------|-------------|-------------|--------------|-------------|--------------|-------------|-----|--------------|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|----|
| CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2 |                                        |          |             |             |             |              |             |              |             |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| PROJECT PROGRAMME                                                           |                                        |          |             |             |             |              |             |              |             |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| ID                                                                          | Task Name                              | Duration | Start       | Finish      | Early Start | Early Finish | Late Start  | Late Finish  | Total Slack | TRA | Predecessors | 2023 |    |    |    | 2024 |    |    |    | 2025 |    |    |    | 2026 |    |    |    | 2027 |    |    |    |    |
|                                                                             |                                        |          |             |             |             |              |             |              |             |     |              | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1 |
| 334                                                                         | Catchpit construcion                   | 7 days   | Tue 25/2/18 | Mon 25/2/24 | Tue 25/2/18 | Mon 25/2/24  | Tue 25/2/18 | Mon 25/2/24  | 0 days      | 0   | 333FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 335                                                                         | Concreting                             | 1 day    | Sun 25/2/23 | Sun 25/2/23 | Sun 25/2/23 | Sun 25/2/23  | Sun 25/2/23 | Sun 25/2/23  | 0 days      | 0   | 334FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 336                                                                         | SHT.CP10B~SHT.CP10A, 750CU(HD-G),L=6.4 | 17 days  | Mon 25/2/24 | Wed 25/3/12 | Mon 25/2/24 | Wed 25/3/12  | Mon 25/2/24 | Wed 25/3/12  | 0 days      | 0   |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 337                                                                         | Excavation and Lateral Support         | 6 days   | Mon 25/2/24 | Sat 25/3/1  | Mon 25/2/24 | Sat 25/3/1   | Mon 25/2/24 | Sat 25/3/1   | 0 days      | 0   | 335          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 338                                                                         | Formwork Erection                      | 8 days   | Fri 25/2/28 | Fri 25/3/7  | Fri 25/2/28 | Fri 25/3/7   | Fri 25/2/28 | Fri 25/3/7   | 0 days      | 0   | 337FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 339                                                                         | Catchpit construcion                   | 7 days   | Thu 25/3/6  | Wed 25/3/12 | Thu 25/3/6  | Wed 25/3/12  | Thu 25/3/6  | Wed 25/3/12  | 0 days      | 0   | 338FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 340                                                                         | Concreting                             | 1 day    | Tue 25/3/11 | Tue 25/3/11 | Tue 25/3/11 | Tue 25/3/11  | Tue 25/3/11 | Tue 25/3/11  | 0 days      | 0   | 339FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 341                                                                         | SHT.CP10A~SHT.CP10,750CU(HD-G),L=26.7  | 39 days  | Wed 25/3/12 | Sat 25/4/19 | Wed 25/3/12 | Sat 25/4/19  | Wed 25/3/12 | Sat 25/4/19  | 0 days      | 0   |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 342                                                                         | Excavation and Lateral Support         | 14 days  | Wed 25/3/12 | Tue 25/3/25 | Wed 25/3/12 | Tue 25/3/25  | Wed 25/3/12 | Tue 25/3/25  | 0 days      | 0   | 340          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 343                                                                         | Formwork Erection                      | 15 days  | Mon 25/3/24 | Mon 25/4/7  | Mon 25/3/24 | Mon 25/4/7   | Mon 25/3/24 | Mon 25/4/7   | 0 days      | 0   | 342FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 344                                                                         | Catchpit construcion                   | 14 days  | Sun 25/4/6  | Sat 25/4/19 | Sun 25/4/6  | Sat 25/4/19  | Sun 25/4/6  | Sat 25/4/19  | 0 days      | 0   | 343FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 345                                                                         | Concreting                             | 1 day    | Fri 25/4/18 | Fri 25/4/18 | Fri 25/4/18 | Fri 25/4/18  | Fri 25/4/18 | Fri 25/4/18  | 0 days      | 0   | 344FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 346                                                                         | SHT.CP10~SHT.CP9,750CU(HD-G),L=4.3     | 17 days  | Sat 25/4/19 | Mon 25/5/5  | Sat 25/4/19 | Mon 25/5/5   | Sat 25/4/19 | Mon 25/5/5   | 0 days      | 0   |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 347                                                                         | Excavation and Lateral Support         | 6 days   | Sat 25/4/19 | Thu 25/4/24 | Sat 25/4/19 | Thu 25/4/24  | Sat 25/4/19 | Thu 25/4/24  | 0 days      | 0   | 345          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 348                                                                         | Formwork Erection                      | 8 days   | Wed 25/4/23 | Wed 25/4/30 | Wed 25/4/23 | Wed 25/4/30  | Wed 25/4/23 | Wed 25/4/30  | 0 days      | 0   | 347FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 349                                                                         | Catchpit construcion                   | 7 days   | Tue 25/4/29 | Mon 25/5/5  | Tue 25/4/29 | Mon 25/5/5   | Tue 25/4/29 | Mon 25/5/5   | 0 days      | 0   | 348FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 350                                                                         | Concreting                             | 1 day    | Sun 25/5/4  | Sun 25/5/4  | Sun 25/5/4  | Sun 25/5/4   | Sun 25/5/4  | Sun 25/5/4   | 0 days      | 0   | 349FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 351                                                                         | SHT.CP9~SHT.CP8,600CU(HD-G),L=33.7     | 45 days  | Mon 25/5/5  | Wed 25/6/18 | Mon 25/5/5  | Wed 25/6/18  | Mon 25/5/5  | Wed 25/6/18  | 0 days      | 0   |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 352                                                                         | Stage 1                                | 24 days  | Mon 25/5/5  | Wed 25/5/28 | Mon 25/5/5  | Wed 25/5/28  | Mon 25/5/5  | Wed 25/5/28  | 0 days      | 0   |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 353                                                                         | Excavation and Lateral Support         | 8 days   | Mon 25/5/5  | Mon 25/5/12 | Mon 25/5/5  | Mon 25/5/12  | Mon 25/5/5  | Mon 25/5/12  | 0 days      | 0   | 350          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 354                                                                         | Formwork Erection                      | 10 days  | Sun 25/5/11 | Tue 25/5/20 | Sun 25/5/11 | Tue 25/5/20  | Sun 25/5/11 | Tue 25/5/20  | 0 days      | 0   | 353FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 355                                                                         | Catchpit construcion                   | 10 days  | Mon 25/5/19 | Wed 25/5/28 | Mon 25/5/19 | Wed 25/5/28  | Mon 25/5/19 | Wed 25/5/28  | 0 days      | 0   | 354FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 356                                                                         | Concreting                             | 1 day    | Tue 25/5/27 | Tue 25/5/27 | Tue 25/5/27 | Tue 25/5/27  | Tue 25/5/27 | Tue 25/5/27  | 0 days      | 0   | 355FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 357                                                                         | Stage 2                                | 22 days  | Wed 25/5/28 | Wed 25/6/18 | Wed 25/5/28 | Wed 25/6/18  | Wed 25/5/28 | Wed 25/6/18  | 0 days      | 0   |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 358                                                                         | Excavation and Lateral Support         | 8 days   | Wed 25/5/28 | Wed 25/6/4  | Wed 25/5/28 | Wed 25/6/4   | Wed 25/5/28 | Wed 25/6/4   | 0 days      | 0   | 356          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 359                                                                         | Formwork Erection                      | 10 days  | Tue 25/6/3  | Thu 25/6/12 | Tue 25/6/3  | Thu 25/6/12  | Tue 25/6/3  | Thu 25/6/12  | 0 days      | 0   | 358FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 360                                                                         | Catchpit construcion                   | 8 days   | Wed 25/6/11 | Wed 25/6/18 | Wed 25/6/11 | Wed 25/6/18  | Wed 25/6/11 | Wed 25/6/18  | 0 days      | 0   | 359FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 361                                                                         | Concreting                             | 1 day    | Tue 25/6/17 | Tue 25/6/17 | Tue 25/6/17 | Tue 25/6/17  | Tue 25/6/17 | Tue 25/6/17  | 0 days      | 0   | 360FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 362                                                                         | Connection of ex. 300CU to SHT.CP8     | 28 days  | Mon 25/6/16 | Sun 25/7/13 | Mon 25/6/16 | Sun 25/7/13  | Sat 26/5/9  | Fri 26/6/5   | 327 days    | 0   | 361FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 363                                                                         | SHT.CP8~SHT.CP7,600CU(HD-G),L=8.5      | 17 days  | Wed 25/6/18 | Fri 25/7/4  | Wed 25/6/18 | Fri 25/7/4   | Wed 25/6/18 | Fri 25/7/4   | 0 days      | 0   |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 364                                                                         | Excavation and Lateral Support [A]     | 6 days   | Wed 25/6/18 | Mon 25/6/23 | Wed 25/6/18 | Mon 25/6/23  | Wed 25/6/18 | Mon 25/6/23  | 0 days      | 0   | 361          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 365                                                                         | Formwork Erection [A]                  | 8 days   | Sun 25/6/22 | Sun 25/6/29 | Sun 25/6/22 | Sun 25/6/29  | Sun 25/6/22 | Sun 25/6/29  | 0 days      | 0   | 364FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 366                                                                         | Catchpit construcion [A]               | 7 days   | Sat 25/6/28 | Fri 25/7/4  | Sat 25/6/28 | Fri 25/7/4   | Sat 25/6/28 | Fri 25/7/4</ |             |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |

| WING TAT CIVIL ENGINEERING CO LTD<br>CONTRACT NO. DC/2022/02 - DRAINAGE IMPROVEMENT WORKS AT YUEN LONG - STAGE 2<br>PROJECT PROGRAMME |                                        |          |             |             |             |              |             |             |             |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
|---------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------|----------|-------------|-------------|-------------|--------------|-------------|-------------|-------------|-----|--------------|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|----|
| ID                                                                                                                                    | Task Name                              | Duration | Start       | Finish      | Early Start | Early Finish | Late Start  | Late Finish | Total Slack | TRA | Predecessors | 2023 |    |    |    | 2024 |    |    |    | 2025 |    |    |    | 2026 |    |    |    | 2027 |    |    |    | Q1 |
|                                                                                                                                       |                                        |          |             |             |             |              |             |             |             |     |              | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 | Q1   | Q2 | Q3 | Q4 |    |
| 416                                                                                                                                   | Catchpit construcion [A]               | 11 days  | Tue 26/3/10 | Fri 26/3/20 | Tue 26/3/10 | Fri 26/3/20  | Tue 26/3/10 | Fri 26/3/20 | 0 days      | 0   | 415FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 417                                                                                                                                   | Concreting [A]                         | 1 day    | Thu 26/3/19 | Thu 26/3/19 | Thu 26/3/19 | Thu 26/3/19  | Thu 26/3/19 | Thu 26/3/19 | 0 days      | 0   | 416FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 418                                                                                                                                   | Connection of ex. 450CU to SHT.CP4 [A] | 28 days  | Wed 26/3/18 | Tue 26/4/14 | Wed 26/3/18 | Tue 26/4/14  | Sat 26/5/9  | Fri 26/6/5  | 52 days     | 0   | 417FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 419                                                                                                                                   | SHT.CP4~End.525CU(HD-Q).L=82.3         | 78 days  | Fri 26/3/20 | Fri 26/6/5  | Fri 26/3/20 | Fri 26/6/5   | Fri 26/3/20 | Fri 26/6/5  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 420                                                                                                                                   | Stage 1                                | 27 days  | Fri 26/3/20 | Wed 26/4/15 | Fri 26/3/20 | Wed 26/4/15  | Fri 26/3/20 | Wed 26/4/15 | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 421                                                                                                                                   | Excavation and Lateral Support [A]     | 10 days  | Fri 26/3/20 | Sun 26/3/29 | Fri 26/3/20 | Sun 26/3/29  | Fri 26/3/20 | Sun 26/3/29 | 0 days      | 0   | 417,103,106  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 422                                                                                                                                   | Formwork Erection [A]                  | 11 days  | Sat 26/3/28 | Tue 26/4/7  | Sat 26/3/28 | Tue 26/4/7   | Sat 26/3/28 | Tue 26/4/7  | 0 days      | 0   | 421FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 423                                                                                                                                   | Catchpit construcion [A]               | 10 days  | Mon 26/4/6  | Wed 26/4/15 | Mon 26/4/6  | Wed 26/4/15  | Mon 26/4/6  | Wed 26/4/15 | 0 days      | 0   | 422FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 424                                                                                                                                   | Concreting [A]                         | 1 day    | Tue 26/4/14 | Tue 26/4/14 | Tue 26/4/14 | Tue 26/4/14  | Tue 26/4/14 | Tue 26/4/14 | 0 days      | 0   | 423FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 425                                                                                                                                   | Stage 2                                | 27 days  | Wed 26/4/15 | Mon 26/5/11 | Wed 26/4/15 | Mon 26/5/11  | Wed 26/4/15 | Mon 26/5/11 | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 426                                                                                                                                   | Excavation and Lateral Support [A]     | 10 days  | Wed 26/4/15 | Fri 26/4/24 | Wed 26/4/15 | Fri 26/4/24  | Wed 26/4/15 | Fri 26/4/24 | 0 days      | 0   | 424          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 427                                                                                                                                   | Formwork Erection [A]                  | 11 days  | Thu 26/4/23 | Sun 26/5/3  | Thu 26/4/23 | Sun 26/5/3   | Thu 26/4/23 | Sun 26/5/3  | 0 days      | 0   | 426FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 428                                                                                                                                   | Catchpit construcion [A]               | 10 days  | Sat 26/5/2  | Mon 26/5/11 | Sat 26/5/2  | Mon 26/5/11  | Sat 26/5/2  | Mon 26/5/11 | 0 days      | 0   | 427FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 429                                                                                                                                   | Concreting [A]                         | 1 day    | Sun 26/5/10 | Sun 26/5/10 | Sun 26/5/10 | Sun 26/5/10  | Sun 26/5/10 | Sun 26/5/10 | 0 days      | 0   | 428FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 430                                                                                                                                   | Stage 3                                | 26 days  | Mon 26/5/11 | Fri 26/6/5  | Mon 26/5/11 | Fri 26/6/5   | Mon 26/5/11 | Fri 26/6/5  | 0 days      |     |              |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 431                                                                                                                                   | Excavation and Lateral Support [A]     | 10 days  | Mon 26/5/11 | Wed 26/5/20 | Mon 26/5/11 | Wed 26/5/20  | Mon 26/5/11 | Wed 26/5/20 | 0 days      | 0   | 429          |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 432                                                                                                                                   | Formwork Erection [A]                  | 10 days  | Tue 26/5/19 | Thu 26/5/28 | Tue 26/5/19 | Thu 26/5/28  | Tue 26/5/19 | Thu 26/5/28 | 0 days      | 0   | 431FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 433                                                                                                                                   | Catchpit construcion [A]               | 10 days  | Wed 26/5/27 | Fri 26/6/5  | Wed 26/5/27 | Fri 26/6/5   | Wed 26/5/27 | Fri 26/6/5  | 0 days      | 0   | 432FS-2 days |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |
| 434                                                                                                                                   | Concreting [A]                         | 1 day    | Fri 26/6/5  | Fri 26/6/5  | Fri 26/6/5  | Fri 26/6/5   | Fri 26/6/5  | Fri 26/6/5  | 0 days      | 0   | 433FS-1 day  |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |      |    |    |    |    |

